CONTRACT DOCUMENTS FOR:

ITB # 17-010

MLK COMMUNITY CENTER ROOF REPLACEMENT

PROJECT # IS72011601

OCTOBER 2016

MAYOR: CRAIG CATES

COMMISSIONERS:

RICHARD PAYNE

BILLY WARDLOW

JIMMY WEEKLEY

CLAYTON LOPEZ

MARGARET ROMERO

SAM KAUFMAN

PREPARED BY:
Engineering Services

CITY OF KEY WEST

KEY WEST, FLORIDA

CONTRACT DOCUMENTS

for

MLK COMMUNITY CENTER ROOF REPLACEMENT

****

CONSISTING OF:
BID REQUIREMENTS
CONTRACT FORMS
CONDITIONS OF THE CONTRACT
SUMMARY OF WORK
SPECIFICATIONS & DRAWINGS

****

KEY WEST, FLORIDA

OCTOBER 2016

Project No. IS72011601

Table of Contents

Page No.

PART 1 - BIDDING REQUIREMENTS

INVITATION TO BID 5
INSTRUCTIONS TO BIDDER 7
PROPOSAL 13
FLORIDA BID BOND 21
ANTI – KICKBACK AFFIDAVIT 23
FLORIDA STATUTES, ON PUBLIC ENTITY CRIMES 24
INDEMNIFICATION FORM 27
LOCAL VENDORS FORM 28
DOMESTIC PARTNERSHIP AFFIDAVIT 29
CONE OF SILENCE AFFIDAVIT 30
BIDDER'S CHECKLIST. 31

PART 2 - CONTRACT

CONTRACT 33
FLORIDA PERFORMANCE BOND 35
FLORIDA PAYMENT BOND 37

PART 3 - CONDITIONS OF THE CONTRACT

GENERAL CONDITIONS OF THE CONTRACT 40
SUPPLEMENTARY CONDITIONS 61

PART 4 - GENERAL REQUIREMENTS

GENERAL REQUIREMENTS 77
SUMMARY OF WORK 84

PART 5 STRUCTURAL REPORT & SPECIFICATIONS AND DRAWINGS

STRUCTURAL EVALUATION REPORT 89
COVER SHEET SITE PLAN A-0
PROPOSED ROOF PLAN A-1
PROPOSED ELEVATIONS A-2
SPECIFICATIONS A-3
EXISTING ROOF PLAN EX-1
EXISTING ELEVATIONS EX-2
STRUCTURAL NOTES S-1
STRUCTURAL PLANS & DETAILS S-2
PLUMBING NOTES, PLANS & DETAILS P-1

PART 1

BIDDING REQUIREMENTS

INVITATION TO BID

Sealed bids for the City of Key West ITB # 17-010 MARTIN LUTHER KING JR. (MLK) COMMUNITY CENTER ROOF REPLACEMENT / IS72011601 addressed to the City of Key West, will be received at the Office of the City Clerk, 3126 Flagler St., Key West Florida, 33040 until 3:30 pm on OCTOBER 26, 2016 and then will be publicly opened and read. Any bids received after the time and date specified will not be considered.

Please submit one (1) original and two (2) flash drives each with one single PDF file of the sections entitled "Bidding Requirements" and "Contract Forms". Bid package is to be enclosed in a sealed envelope, clearly marked on the outside "BID FOR" addressed and delivered to the City Clerk at the address noted above.

The project consists of roof replacement on the existing Martin Luther King Junior (MLK) Community Center and associated work.

Drawings and Specifications may be obtained from Demand Star by Onvia. Please contact Demand Star at www.demandstar.com or call 1-800-711-1712 or www.cityofkeywest-fl.gov

A **pre-bid meeting** will be held in the City Manager's conference room at 3132 Flagler Ave., Key West, Florida on October 12, 2016 at 10:00 a.m.

The successful Bidder will be required to furnish the necessary additional bond(s) for the faithful performance of the Contract, as prescribed in the Bidding Documents

EACH BID MUST BE SUBMITTED ON THE PRESCRIBED FORM AND ACCOMPANIED BY BID SECURITY AS PRESCRIBED IN THE INSTRUCTIONS TO BIDDERS, PAYABLE TO THE CITY OF KEY WEST, FLORIDA, IN AN AMOUNT NOT LESS THAN FIVE (5) PERCENT OF THE AMOUNT BID.

THE BIDDER MUST BE A LICENSED CONTRACTOR BY THE STATE OF FLORIDA AND SUBMIT PROOF OF SUCH WITH THE BID.

The Bidder shall furnish documentation showing that he is in compliance with the licensing requirements of the provisions of Chapter 66 Section 87 of the Code of Ordinances of the City of Key West; within 10 days the following the Notice of Award and must demonstrate that he holds at a minimum, the following licenses & certificates;

A. City of Key West Business Tax License Receipt
B. A valid Certificate of Competency issued by the Chief Building Official of Key West, Florida.

All bid bonds, contract bonds, insurance contracts, and certificates of insurance shall be either executed by or countersigned by a licensed resident agent of the Surety or Insurance Company having his place of business in the State of Florida, and in all ways complying with the insurance laws of the State of Florida. Further, the said Surety or Insurance Company shall be duly licensed and qualified to do business in the State of Florida.

Before a Contract will be awarded for the work contemplated herein, the CITY will conduct such investigation as is necessary to determine the performance record and ability of the apparent low Bidder to perform the size and type of work specified under this Contract. Upon request, the Bidder shall submit such information as deemed necessary by the CITY to evaluate the Bidder's qualifications.

For information concerning the proposed work contact Janet Muccino, Project Manager, Engineering Services Department for the City of Key West at jmuccino@cityofkeywest-fl.gov communications per the City's Cone of Silence Ordinance Section 2-773 are not allowed.

As stated above at the time of the bid submittal the Bidder must provide satisfactory documentation of State Licenses. The Bidder shall furnish documentation showing that he is in compliance with the licensing requirements of County, and City licenses as would be required within ten days of the award. The successful Bidder must also be able to satisfy the City Attorney as to such insurance coverage and legal requirements as may be demanded by the Bid in question. The City may reject bids for any and/or all of the following reasons: (1) for budgetary reasons, (2) if the bidder misstates or conceals a material fact in its bid, (3) if the bid does not strictly conform to the law or is non-responsive to the bid requirements, (4) if the bid is conditional, or (5) if a change of circumstances occurs making the purpose of the bid unnecessary to the City or (6) if such rejection is in the best interest of the City. The City may also waive any minor formalities or irregularities in any bid.

****

INSTRUCTIONS TO BIDDERS

1. CONTRACT DOCUMENTS

A. FORMAT

The Contract Documents are divided into parts, divisions, and sections for convenient organization and reference. Generally, there has been no attempt to divide the sections into work performed by the various building trades, work by separate subcontractors, or work required for separate facilities in the project.

B. DOCUMENT INTERPRETATION

The separate sections contained within these Contract Documents are intended to be mutually cooperative and to provide all details reasonably required for the execution of the proposed work.

Should there be any doubt as to the meaning or intent of said Contract Documents, the Bidder should request of the Engineer, in writing (at least 10 working days prior to bid opening) an interpretation thereof. Any interpretation or change in said Contract Documents will be made only in writing in the form of Addenda to the documents which will be furnished to all registered holders of Contract Documents. Bidders shall submit with their Proposals, or indicate receipt of, all Addenda. The CITY will not be responsible for any other explanation or interpretations of said Documents.

2. GENERAL DESCRIPTION OF THE PROJECT

A general description of the work to be done is contained in the Invitation to Bid. The scope is specified in applicable parts of these Contract Documents.

3. QUALIFICATION OF CONTRACTORS

The prospective Bidders must meet the statutorily prescribed requirements before award of Contract by the CITY. Bidders must hold or obtain all licenses and/or certificates as required by the State and Local Statutes in order to bid and perform the work specified herein.

4. BIDDER'S UNDERSTANDING

Each Bidder must inform himself of the conditions relating to the execution of the work, and it is assumed that he will inspect the site and make himself thoroughly familiar with all the Contract Documents. Failure to do so will not relieve the successful Bidder of his obligation to enter into a Contract and complete the contemplated work in strict accordance with the Contract Documents. It shall be the Bidder's obligation to verify for himself and to his complete satisfaction all information concerning site.

Each Bidder shall inform himself of, and the Bidder awarded a Contract shall comply with, federal, state, and local laws, statutes, and ordinances relative to the execution of the work. This

requirement includes, but is not limited to, applicable regulations concerning minimum wage rates, nondiscrimination in the employment of labor, protection of public and employee safety and health, environmental protection, the protection of natural resources, fire protection, burning and non-burning requirements, permits, fees, and similar subjects.

5. TYPE OF PROPOSAL

A. LUMP SUM

The Proposal for the work is to be submitted on a lump sum basis. Lump sum prices shall be submitted for all items of work set forth in the Proposal. All items required to complete the work specified but not included in the Proposal shall be considered incidental to those set forth in the Proposal.

The Bidder shall submit a Schedule of Values with the Proposal. It shall be broken down by technical specification and it shall be used as a basis for payment. Payment to the Contractor will be made on the measurement of the work actually performed by the Contractor as specified in the Contract Documents.

6. PREPARATION OF BIDS

A. GENERAL

All blank spaces in the BID form must be filled in, as required, preferably in BLACK ink. All price information shall be shown in both words and figures where required. No changes shall be made in the phraseology of the forms. Written amounts shall govern in case of discrepancy between the amounts stated in writing and the amounts stated in figures. In case of discrepancy between unit prices and extended totals, unit prices shall prevail.

Any BID shall be deemed informal which contains omissions, erasures, alterations, or additions of any kind, or prices uncalled for, or in which any of the prices are obviously unbalanced, or which in any manner shall fail to conform to the conditions of the published Invitation to Bid.

Only one BID from any individual, firm, partnership, or corporation, under the same or different names, will be considered. Should it appear to the CITY that any Bidder is interested in more than one Proposal for work contemplated; all Proposals in which such Bidder is interested will be rejected.

B. SIGNATURE

The Bidder shall sign his BID in the blank space provided therefore. If Bidder is a corporation, the legal name of the corporation shall be set forth above, together with the signature of the officer or officers authorized to sign Contracts on behalf of the corporation. If Bidder is a partnership, the true name of the firm shall be set forth above, together with the signature of the partner or partners authorized to sign Contracts in

behalf of the partnership. If signature is by an agent, other than an officer of a corporation or a member of a partnership, a notarized power-of-attorney must be on file with the CITY prior to opening of Proposals or submitted with the Proposal, otherwise the Proposal will be regarded as not properly authorized.

C. SPECIAL BIDDING REQUIREMENTS

The Bidder's attention is brought to the hiring practices and licenses and permits of the City of Key West. These are defined in the addition to Article 39, ORDINANCES, PERMITS, AND LICENSES, as set forth in the Supplementary Conditions.

The Bidder shall submit with his Bid his experience record showing his experience and expertise in roof construction and related work. Such experience record shall provide at least five current or recent projects of similar work, within the State Florida and preferably Monroe County. For each project the following information shall be provided:

1. Description and location of work.
2. Contract amount.
3. Dates work was performed.
4. Owner.
5. Name of Owner's contact person and phone number.
6. Engineer.
7. Name of Engineer's contact person and phone number.

The bidder shall submit with his bid a list of items to be performed by his own labor and that performed by subcontractors or others.

D. ATTACHMENTS

Bidder shall complete and submit the following forms with his bid:

Anti-Kickback Affidavit
Public Entity Crimes Form
Indemnification Form
Local Vendor Certificate
Domestic Partnership Affidavit
Cone of Silence Affidavit

7. STATE AND LOCAL SALES AND USE TAXES

Unless the Supplementary Conditions contains a statement that the CITY is exempt from state sales tax on materials incorporated into the work due to the qualification of the work under this Contract, the Contractor, as required by the laws and statutes of the state and its political subdivisions, shall pay all state and local sales and use taxes. Prices quoted in the Proposal shall include all nonexempt sales and use taxes, unless provision is made in the Proposal form to separately itemize the tax.

8. SUBMISSION OF BIDS

All BIDS must be submitted not later than the time prescribed, at the place, and in the manner set forth in the Invitation to Bid. BIDS must be made on the BID forms provided herewith, **submit one (1) ORIGINAL of bid package and two (2) FLASH DRIVES each containing a single PDF file of the entire bid package.**

Each BID must be submitted in a sealed envelope, so marked as to indicate the Bidder's name and its contents (project name and ITB number) without being opened, and addressed in conformance with the instructions in the Invitation to Bid.

9. MODIFICATION OR WITHDRAWAL OF BIDS

Prior to the time and date designated for receipt of BIDS, any BID submitted may be withdrawn by notice to the party receiving BIDS at the place designated for receipt of BIDS. Such notice shall be in writing over the signature of the Bidder or by telegram. If by telegram, written confirmation over the signature of the Bidder shall be mailed and postmarked on or before the date and time set for receipt of BID. No BID may be withdrawn after the time scheduled for opening of BIDS, unless the time specified in paragraph AWARD OF CONTRACT of these Instructions to Bidders shall have elapsed.

10. BID SECURITY

BIDS must be accompanied by cash, a certified check, or cashier's check drawn on a bank in good standing, or a bid bond issued by a Surety authorized to issue such bonds in the state where the work is located, in the amount of five (5) percent of the total amount of the Proposal submitted. This bid security shall be given as a guarantee that the Bidder will not withdraw his BID for a period of sixty (60) days after bid opening, and that if awarded the Contract, the successful Bidder will execute the attached Contract and furnish properly executed Performance and Payment Bonds, each in the full amount of the Contract price within the time specified. Agent and Surety phone numbers must be provided.

The Attorney-in-Fact who executes this bond in behalf of the Surety must attach a notarized copy of his power-of-attorney as evidence of his authority to bind the Surety on the date of execution of the bond. Where State Statute requires, certification by a resident agent shall also be provided.

If the Bidder elects to furnish a Bid Bond, he shall use the Bid Bond form bound herewith, or one conforming substantially thereto in form and content.

11. RETURN OF BID SECURITY

Within 15 days after the award of the Contract, the CITY will return the bid securities to all Bidders whose BIDS are not to be further considered in awarding the Contract. Retained bid securities will be held until the Contract has been finally executed, after which all bid securities,

other than Bidders' bonds and any guarantees, which have been forfeited, will be returned to the respective Bidders whose Proposals they accompanied.

12. AWARD OF CONTRACT

Within sixty (60) calendar days after the opening of Proposals, the CITY will accept one of the Proposals or will act in accordance with the following paragraphs. The acceptance of the Proposal will be by written notice of award, mailed to the office designated in the Proposal, or delivered to the Bidder's representative. In the event of failure of the lowest responsive, responsible Bidder to sign the Contract and provide an acceptable Performance Bond, Payment Bond, insurance certificate(s) and evidence of holding required licenses and certificates, the Owner may award the Contract to the next lowest responsive, responsible Bidder. Such award, if made, will be made within seventy-five (90) days after the opening of Proposals.

The CITY reserves the right to accept or reject any or all Proposals, and to waive any informalities and irregularities in said Proposals.

13. BASIS OF AWARD

The award will be made by the Owner on the basis of the BASE BID and owner selected Alternates from the lowest, responsive, responsible BIDDER which, in the Owner's sole and absolute judgment will best serve the interest of the Owner.

14. EXECUTION OF CONTRACT

The successful Bidder shall, within ten (10) working days after receiving Notice of Award, sign and deliver to the CITY an original Contract and two (2) copies in the form hereto attached, together with the insurance certificate examples of the bonds as required in the Contract Documents and evidence of holding required licenses and certificates. Within 10 working days after receiving the signed Contract from the successful Bidder, the City's authorized agent will sign the Contract. Signature by both parties constitutes execution of the Contract.

15. CONTRACT BONDS

A. PERFORMANCE AND PAYMENT BONDS

The successful Bidder shall file with the CITY, at the time of delivery of the signed Contract, a Performance Bond and Payment Bond on the form bound herewith, each in the full amount of the Contract price in accordance with the requirements of Florida Statutes Section 255.05 or 713.23, as applicable, as security for the faithful performance of the Contract and the payment of all persons supplying labor and materials for the construction of the work, and to cover all guarantees against defective workmanship or materials, or both, during the warranty period following the date of final acceptance of the work by the CITY. The Surety furnishing this bond shall have a sound financial standing and a record of service satisfactory to the CITY, shall be authorized to do business in the State of Florida, and shall be listed on the current U.S. Department of Treasury Circular Number 570, or amendments thereto in the Federal Register, of acceptable Sureties for federal projects. The CONTRACTOR shall supply the OWNER

with phone numbers, addresses, and contacts for the Surety and their agents. Pursuant to Section 255.05(7), Florida Statutes, in lieu of the bond required by law, the contractor may file with the city an alternative form of security in the form of cash, a money order, a certified check, a cashier's check or an irrevocable letter of credit.

B. POWER-OF-ATTORNEY

The Attorney-in-Fact (Resident Agent) who executes this Performance and Payment Bond in behalf of the Surety must attach a notarized copy of his power-of-attorney as evidence of his authority to bind the Surety on the date of execution of the bond.
All Contracts, Performance and Payment Bonds, and respective powers-of-attorney will have the same date.

16. FAILURE TO EXECUTE CONTRACT AND FURNISH BOND

The Bidder who has a Contract awarded to him and who fails to promptly and properly execute the Contract or furnish the required Bonds shall forfeit the bid security that accompanied his bid, and the bid security shall be retained as liquidated damages by the CITY, and it is agreed that this said sum is a fair estimate of the amount of damages the CITY will sustain in case the Bidder fails to enter into a Contract or furnish the required Bonds. Bid security deposited in the form of cash, a certified check, or cashier's check shall be subject to the same requirement as a Bid Bond.

17. PERFORMANCE OF WORK BY CONTRACTOR

The Contractor shall perform on the site and with his own organization, labor equivalent to at least forty (40) percent of the base bid total amount of the work to be performed under this Contract. If, during the progress of the work hereunder, the Contractor requests a reduction of such percentage, and the Engineer determines that it would be to the client's advantage, the percentage of the labor required to be performed by the Contractor's own organization may be reduced; PROVIDED prior written approval of such reduction is obtained by the contractor from the Engineer.

Each Bidder must furnish with his Proposal a list of the items that he will perform with his own forces and the estimated total cost of these items.

18. TIME OF COMPLETION

The time of completion of the work to be performed under this Contract is the essence of the Contract. Delays and extensions of time may be allowed in accordance with the provisions stated in the General Conditions.

When the Contractor receives a Notice to Proceed, he shall commence work as soon as possible and shall complete all work within the number of calendar days stipulated in this Proposal.

The term of this contract will be **90** calendar days.

* * * * * *

NOTE TO BIDDER: Use preferably BLACK ink for completing this Proposal form.

PROPOSAL

To:	The City of Key West
Address:	3126 Flagler Street, Key West, Florida 33041
Project Title:	MLK COMMUNITY CENTER ROOF REPLACEMENT ITB # 17-010

Bidder's contact person for additional information on this Proposal:

Company Name: _____

Contact Name & Telephone #: _____

Email Address: _____

BIDDER'S DECLARATION AND UNDERSTANDING

The undersigned, hereinafter called the Bidder, declares that the only persons or parties interested in this Proposal are those named herein, that this Proposal is, in all respects, fair and without fraud, that it is made without collusion with any official of the Owner, and that the Proposal is made without any connection or collusion with any person submitting another Proposal on this Contract.

The Bidder further declares that he has carefully examined the Contract Documents for the construction of the project, that he has personally inspected the site, that he has satisfied himself as to the quantities involved, including materials and equipment, and conditions of work involved, including the fact that the description of the quantities of work and materials, as included herein, is brief and is intended only to indicate the general nature of the work and to identify the said quantities with the detailed requirements of the Contract Documents, and that this Proposal is made according to the provisions and under the terms of the Contract Documents, which Documents are hereby made a part of this Proposal.

CONTRACT EXECUTION AND BONDS

The Bidder agrees that if this Proposal is accepted, he will, within 10 days, not including Sundays and legal holidays, after Notice of Award, sign the Contract in the form annexed hereto, and will at that time, deliver to the Owner examples of the Performance Bond and Payment Bond required herein, and evidence of holding required licenses and certificates, and will, to the extent of his Proposal, furnish all machinery, tools, apparatus, and other means of construction and do the work and furnish all the materials necessary to complete all work as specified or indicated in the Contract Documents.

CERTIFICATES OF INSURANCE

Bidder agrees to furnish the Owner, before commencing the work under this Contract, the certificates of insurance as specified in these Documents.

START OF CONSTRUCTION AND CONTRACT COMPLETION TIME

The Bidder further agrees to begin work within 14 calendar days after the date of the Notice to Proceed and to complete the project, in all respects within 90 calendar days after the date of the Notice to Proceed.

LIQUIDATED DAMAGES

In the event the Bidder is awarded the Contract and shall fail to complete the work within the time limit or extended time limit agreed upon, as more particularly set forth in the Contract Documents, liquidated damages shall be paid to the Owner at the rate of $500.00 per day for all work awarded until the work has been satisfactorily completed as provided by the Contract Documents. Sundays and legal holidays shall be excluded in determining days in default.

ADDENDA

The Bidder hereby acknowledges that he has received Addenda No's. _____, _____, ____, _____, ____, ____, _____, _____, _____, _____, _____, _____, _____, _____,
(Bidder shall insert No. of each Addendum received) and agrees that all addenda issued are hereby made part of the Contract Documents, and the Bidder further agrees that his Proposal(s) includes all impacts resulting from said addenda.

SALES AND USE TAXES

The Bidder agrees that all federal, state, and local sales and use taxes are included in the stated bid prices for the work.

LUMP SUM ITEMS

The Bidder further proposes to accept as full payment for the work proposed herein the amounts computed under the provisions of the Contract Documents and based on the following lump sum amounts. The Bidder agrees that the lump sum represent a true measure of the labor and materials required to perform the work, including all allowances for overhead and profit for each type and unit of work called for in these Contract Documents.

TOTAL LUMP SUM BASE BID:

1 LS $_____

_____Dollars & _____Cents
(amount written in words)

The award will be made by the Owner on the basis of the BASE BID plus the OWNER SELECTED ALTERNATES from the lowest, responsive, responsible BIDDER.

ADDITIVE / ALTERNATE

1.) INSTALLATION OF SOLAR HEATING / COOLING SYSTEM

1 LS $_____

_____Dollars & _____Cents
(amount written in words)

2.) INSTALLATION SEALOFLEX LIQUID ON ENTRY ROOF

1 LS $_____

_____Dollars & _____Cents
(amount written in words)

3.) INSTALLATION OF LIGHTENING PROTECTION

1 LS $_____

_____Dollars & _____Cents
(amount written in words)

TOTAL BASE BID AND ADD/ALTS # 1,2 & 3

$_____

_____Dollars & _____Cents
(amount written in words)

List items to be performed by CONTRACTOR's own forces and the estimated total cost of these items. (Use additional sheets if necessary.)

SUBCONTRACTORS

The Bidder further proposes that the following subcontracting firms or businesses will be awarded subcontracts for the following portions of the work in the event that the Bidder is awarded the Contract:

_____
Name

_____, _____, _____, _____
Street City State Zip

Name

_____, _____, _____ ,_____
Street City State Zip

_____
Name

_____, _____, _____,_____
Street City State Zip

_____
Name

_____, _____, _____,_____
Street City State Zip

SURETY

_____ whose address is

_____, _____, _____, _____
Street City State Zip

BIDDER

The name of the Bidder submitting this Proposal is

_____ doing business at

_____, _____, _____, _____
Street City State Zip

which is the address to which all communications concerned with this Proposal and with the Contract shall be sent.

The names of the principal officers of the corporation submitting this Proposal, or of the partnership, or of all persons interested in this Proposal as principals are as follows:

_____ _____

_____ _____

_____ _____

_____ _____

_____ _____

If Sole Proprietor or Partnership

IN WITNESS hereto the undersigned has set his (its) hand this _____ day of _____ 2016.

_____
Signature of Bidder

_____
Title

If Corporation

IN WITNESS WHEREOF the undersigned corporation has caused this instrument to be executed and its seal affixed by its duly authorized officers this _____ day of _____ 2016.

(SEAL)

_____
Name of Corporation

By _____

Title _____
Attest_____
Secretary

EXPERIENCE OF BIDDER

The Bidder states that he is an experienced CONTRACTOR and has completed similar projects within the last 5 years.

(List similar projects, with types, names of OWNERs, construction costs, ENGINEERs, and references with phone numbers. Use additional sheets if necessary.

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

_____

****

FLORIDA BID BOND

BOND NO. _____

AMOUNT: $ _____

KNOW ALL MEN BY THESE PRESENTS, that _____

_____

hereinafter called the PRINCIPAL, and _____

_____

a corporation duly organized under the laws of the State of _____

having its principal place of business at _____

_____in the State of _____,

and authorized to do business in the State of Florida, as SURETY, are held and firmly bound unto

_____

hereinafter called the OBLIGEE, in the sum of_____

DOLLARS ($_____) for the payment for which we bind ourselves, our heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these present.

THE CONDITION OF THIS BOND IS SUCH THAT:

WHEREAS, the PRINCIPAL is herewith submitting his or its Bid Proposal for the MLK COMMUNITY CENTER ROOF REPLACEMENT, said Bid Proposal, by reference thereto, being hereby made a part hereof.

WHEREAS, the PRINCIPAL contemplates submitting or has submitted a bid to the OBLIGEE for the furnishing of all labor, materials (except those to be specifically furnished by the CITY), equipment, machinery, tools, apparatus, means of transportation for, and the performance of the work covered in the Proposal and the detailed Specifications, entitled:

MLK COMMUNITY CENTER ROOF REPLACEMENT / IS72011601

WHEREAS, it was a condition precedent to the submission of said bid that a cashier's check, certified check, or bid bond in the amount of 5 percent of the base bid be submitted with said bid as a guarantee that the Bidder would, if awarded the Contract, enter into a written Contract with the CITY for the performance of said Contract, within 10 working days after written notice having been given of the award of the Contract.

NOW, THEREFORE, the conditions of this obligation are such that if the PRINCIPAL within 10 consecutive calendar days after written notice of such acceptance, enters into a written Contract with the OBLIGEE and furnishes the Performance and Payment Bonds, each in an amount equal to 100 percent of the base bid, satisfactory to the CITY, then this obligation shall be void; otherwise the sum herein stated shall be due and payable to the OBLIGEE and the Surety herein agrees to pay said sum immediately upon demand of the OBLIGEE in good and lawful money of the United States of America, as liquidated damages for failure thereof of said PRINCIPAL.

Signed and sealed this _____ day of _____, 2016.

PRINCIPAL

By_____

STATE OF _____)
: SS
COUNTY OF _____)

_____
SURETY

By _____

ANTI – KICKBACK AFFIDAVIT

STATE OF _____)
: SS
COUNTY OF _____)

I, the undersigned hereby duly sworn, depose and say that no portion of the sum herein bid will be paid to any employees of the City of Key West as a commission, kickback, reward or gift, directly or indirectly by me or any member of my firm or by an officer of the corporation.

By: _____

Sworn and subscribed before me this _____day of _____, 2016.

NOTARY PUBLIC, State of _____ at Large

My Commission Expires:

* * * * * *

SWORN STATEMENT UNDER SECTION 287.133(3)(A)
FLORIDA STATUTES, ON **PUBLIC ENTITY CRIMES**

THIS FORM MUST BE SIGNED IN THE PRESENCE OF A NOTARY PUBLIC OR OTHER OFFICER AUTHORIZED TO ADMINISTER OATHS.

1. This sworn statement is submitted with Bid or Proposal for _____

   _____

2. This sworn statement is submitted by_____
   (Name of entity submitting sworn statement)

   whose business address is _____

   _____

   and (if applicable) its Federal Employer Identification Number (FEIN) is_____

   _____

   (If the entity has no FEIN, include the Social Security Number of the individual

   signing this sworn statement _____

3. My name is _____
   (Please print name of individual signing)

   and my relationship to the entity named above is _____

4. I understand that a "public entity crime" as defined in Paragraph 287.133(1)(g), Florida Statutes, means a violation of any state or federal law by a person with respect to and directly related to the transaction of business with any public entity or with an agency or political subdivision of any other state or with the United States, including but not limited to, any bid or contract for goods or services to be provided to any public or an agency or political subdivision of any other state or of the United States and involving antitrust, fraud, theft, bribery, collusion, racketeering, conspiracy, material misrepresentation.

5. I understand that "convicted" or "conviction" as defined in Paragraph 287.133(1)(b), Florida Statutes, means a finding of guilt or a conviction of a public entity crime, with or without an adjudication guilt, in any federal or state trial court of record relating to charges brought by indictment information after July 1, 1989, as a result of a jury verdict, nonjury trial, or entry of a plea of guilty or nolo contendere.

6. I understand that an "affiliate" as defined in Paragraph 287.133(1)(a), Florida Statutes, means

    a. A predecessor or successor of a person convicted of a public entity crime; or

    b. An entity under the control of any natural person who is active in the management of the entity and who has been convicted of a public entity crime. The term "affiliate" includes those officers, directors, executives, partners, shareholders, employees, members, and agents who are active in the management of an affiliate. The ownership by one person of shares constituting controlling interest in another person, or a pooling of equipment or income among persons when not for fair market value under an arm's length agreement, shall be a prima facie case that one person controls another person. A person who knowingly enters into a joint venture with a person who has been convicted of a public entity crime in Florida during the preceding 36 months shall be considered an affiliate.

7. I understand that a "person" as defined in Paragraph 287.133(1)(8), Florida Statutes, means any natural person or entity organized under the laws of any state or of the United States with the legal power to enter into a binding contract and which bids or applies to bid on contracts for the provision of goods or services let by a public entity, or which otherwise transacts or applies to transact business with public entity. The term "person" includes those officers, directors, executives, partners, shareholders, employees, members, and agents who are active in management of an entity.

8. Based on information and belief, the statement which I have marked below is true in relation to the entity submitting this sworn statement. (Please indicate which statement applies).

    ____Neither the entity submitting this sworn statement, nor any officers, directors, executives, partners, shareholders, employees, members, or agents who are active in management of the entity, nor any affiliate of the entity have been charged with and convicted of a public entity crime subsequent to July 1, 1989, AND (Please indicate which additional statement applies.)

    _____There has been a proceeding concerning the conviction before a hearing of the State of Florida, Division of Administrative Hearings. The final order entered by the hearing officer did not place the person or affiliate on the convicted vendor list. (Please attach a copy of the final order.)

    _____The person or affiliate was placed on the convicted vendor list. There has been a subsequent proceeding before a hearing officer of the State of

    Florida, Division of Administrative Hearings. The final order entered by the hearing officer determined that it was in the public interest to remove the person or affiliate from the convicted vendor list. (Please attach a copy of the final order.)

_____The person or affiliate has not been put on the convicted vendor list. (Please describe any action taken by or pending with the Department of General Services.)

_____
(Signature)

_____
(Date)

STATE OF_____

COUNTY OF_____

PERSONALLY APPEARED BEFORE ME, the undersigned authority,

_____who, after first being sworn by me, affixed his/her
(Name of individual signing)

Signature in the space provided above on this_____day of _____ , 2016.

My commission expires:

_____
NOTARY PUBLIC

INDEMNIFICATION

To the fullest extent permitted by law, the CONTRACTOR expressly agrees to indemnify and hold harmless the City of Key West, their officers, directors, agents, and employees (herein called the "indemnitees") from liabilities, damages, losses and costs, including, but not limited to, reasonable attorney's fees and court costs, such legal expenses to include costs incurred in establishing the indemnification and other rights agreed to in this Paragraph, to persons or property, to the extent caused by the negligence, recklessness, or intentional wrongful misconduct of the CONTRACTOR, its Subcontractors or persons employed or utilized by them in the performance of the Contract. Claims by indemnitees for indemnification shall be limited to the amount of CONTRACTOR's insurance or $1 million per occurrence, whichever is greater. The parties acknowledge that the amount of the indemnity required hereunder bears a reasonable commercial relationship to the Contract and it is part of the project specifications or the bid documents, if any.

The indemnification obligations under the Contract shall not be restricted in any way by any limitation on the amount or type of damages, compensation, or benefits payable by or for the CONTRACTOR under workers' compensation acts, disability benefits acts, or other employee benefits acts, and shall extend to and include any actions brought by or in the name of any employee of the CONTRACTOR or of any third party to whom CONTRACTOR may subcontract a part or all of the Work. This indemnification shall continue beyond the date of completion of the work.

CONTRACTOR: _____ SEAL:

_____
Address

_____
Signature

_____
Print Name

_____
Title

_____
Date

LOCAL VENDOR CERTIFICATION PURSUANT TO CKW ORDINANCE 09-22 SECTION 2-798

The undersigned, as a duly authorized representative of the vendor listed herein, certifies to the best of his/her knowledge and belief, that the vendor meets the definition of a "Local Business." For purposes of this section, "local business" shall mean a business which:

a. Principle address as registered with the FL Department of State located within 30 miles of the boundaries of the city, listed with the chief licensing official as having a business tax receipt with its principle address within 30 miles of the boundaries of the city for at least one year immediately prior to the issuance of the solicitation.

b. Maintains a workforce of at least 50 percent of its employees from the city or within 30 miles of its boundaries.

c. Having paid all current license taxes and any other fees due the city at least 24 hours prior to the publication of the call for bids or request for proposals.

- Not a local vendor pursuant to Ordinance 09-22 Section 2-798
- Qualifies as a local vendor pursuant to Ordinance 09-22 Section 2-798

If you qualify, please complete the following in support of the self-certification & submit copies of your County and City business licenses. Failure to provide the information requested will result in denial of certification as a local business.

Business Name _____ Phone: _____

Current Local Address: _____ Fax:_____
(P.O Box numbers may not be used to establish status)

Length of time at this address:_____

_____ Date: _____
Signature of Authorized Representative

STATE OF_____ COUNTY OF_____

The foregoing instrument was acknowledged before me this _____day of_____, 2016.

By_____, of _____
(Name of officer or agent, title of officer or agent) (Name of corporation acknowledging)

or has produced identification_____as identification
(Type of identification)

_____
Signature of Notary

_____
Print, Type or Stamp Name of Notary

Return Completed form with
Supporting documents to:
City of Key West Purchasing

_____
Title or Rank

EQUAL BENEFITS FOR DOMESTIC PARTNERS AFFIDAVIT

STATE OF _____)
: SS
COUNTY OF _____)

I, the undersigned hereby duly sworn, depose and say that the firm of _____ provides benefits to domestic partners of its employees on the same basis as it provides benefits to employees' spouses per City of Key West Ordinance Sec. 2-799.

By: _____

Sworn and subscribed before me this

_____ Day of _____, 2016.

_____
NOTARY PUBLIC, State of _____ at Large

My Commission Expires: _____

CONE OF SILENCE AFFIDAVIT

STATE OF _____)
: SS
COUNTY OF _____)

I the undersigned hereby duly sworn depose and say that all owner(s), partners, officers, directors, employees and agents representing the firm of _____ have read and understand the limitations and procedures regarding communications concerning City of Key West issued competitive solicitations pursuant to City of Key West Ordinance Section 2-773 Cone of Silence (attached).

Sworn and subscribed before me this

_____ Day of _____, 2016.

_____

NOTARY PUBLIC, State of _____ at Large

My Commission Expires: _____

BIDDER'S CHECKLIST

(Note: The purpose of this checklist is to serve as a reminder of major items to be addressed in submitting a bid and is not intended to be all inclusive. It does not alleviate the Bidder from the responsibility of becoming familiar with all aspects of the Contract Documents and proper completion and submission of his bid.)

1.	All Contract Documents thoroughly read and understood.	[ ]
2.	All blank spaces in Proposal filled in, using black ink.	[ ]
3.	Total and unit prices added correctly and attached Schedule of Values	[ ]
4.	Addenda acknowledged.	[ ]
5.	Subcontractors are named as indicated in the Proposal.	[ ]
6.	Experience record included.	[ ]
7.	Proposal signed by authorized officer.	[ ]
8.	Bid Bond completed and executed, including power-of-attorney dated the same date as Bid Bond.	[ ]
9.	Bidder familiar with federal, state, and local laws, ordinances, rules and regulations affecting performance of the work.	[ ]
10.	Bidder, if successful, able to obtain and/or demonstrate possession of required licenses and certificates within (10) ten calendar days after receiving a Notice of Award.	[ ]
11.	BID submitted intact with the volume entitled “Bidding Requirements” and “Contract Forms”, 1 original, and 2 flash drives as stated in the invitation to bid.	[ ]
12.	Bid Documents submitted in sealed envelope and addressed and labeled in conformance with the instructions in the Invitation to Bid.	[ ]

PART 2

CONTRACT FORMS

CONTRACT

This Contract, made and entered into this _____ day of _____ 2016,

by and between the City of Key West, hereinafter called the "Owner", and_____

_____

hereinafter called the "Contractor";

WITNESSETH:

The Contractor, in consideration of the sum to be paid him by the Owner and of the covenants and agreements herein contained, hereby agrees at his own proper cost and expense to do all the work and furnish all the materials, tools, labor, and all appliances, machinery, and appurtenances for ITB # 17-010 MLK COMMUNITY CENTER ROOF REPLACEMENT IS72011601, Key West, Florida to the extent of the Proposal made by the Contractor, dated the _____ day of_____

_____2016, all in full compliance with the Contract Documents referred to herein.

The CONTRACT DOCUMENTS, including the signed copy of the PROPOSAL, CONTRACT FORMS, PERFORMANCE & PAYMENT BONDS, SUMMARY OF WORK, DRAWINGS, SPECIFICATIONS, GENERAL CONDITIONS OF THE CONTRACT.
& SUPPLEMENTARY CONDITIONS.

In consideration of the performance of the work as set forth in these Contract Documents, the Owner agrees to pay to the Contractor the amount bid in the Proposal as adjusted in accordance with the Contract Documents, or as otherwise herein provided, and to make such payments in the manner and at the times provided in the Contract Documents.

The Contractor agrees to complete the work within ninety (90) days and to accept as full payment hereunder the amounts computed as determined by the Contract Documents and based on the said BID.

The Contractor agrees to remedy all defects appearing in the work or developing in the materials furnished and the workmanship performed under this Contract during the warranty period after the date of final acceptance of the work by the Owner, and further agrees to indemnify and save the Owner harmless from any costs encountered in remedying such defects.

It is agreed that the Contract, based upon the BID, shall be fully complete within the stated number of consecutive calendar days from the date the Notice to Proceed is issued.

In the event the Contractor fails to complete the work within the time limit or extended time limit agreed upon, as more particularly set forth in the Contract Documents, liquidated damages shall be paid at a rate of $500.00 per day. Sundays and legal holidays shall be included in determining days in default.

This contract will automatically expire upon completion of the project. Contractors warranty obligations remain in effect.

IN WITNESS WHEREOF, we, the parties hereto, each herewith subscribe the same this

_____ Day of _____, A.D., 2016.

CITY OF KEY WEST

By_____

Title_____

CONTRACTOR

By_____

Title_____

* * * *

FLORDIA PERFORMANCE BOND

BOND NO._____

AMOUNT: $_____

KNOW ALL MEN BY THESE PRESENTS, that in accordance with Florida Statutes Section

255.05 _____

with offices at _____

hereinafter called the CONTRACTOR (Principal), and

_____

with offices at_____

a corporation duly organized and existing under and by virtue of the laws of the State of Florida, hereinafter called the SURETY, and authorized to transact business within the State of Florida, as SURETY, are held and firmly bound unto the **CITY OF KEY WEST,** hereinafter called the CITY (Obligee), in the sum of:

_____DOLLARS ($_____,)
lawful money of the United States of America, for the payment of which, well and truly be made to the CITY, the CONTRACTOR and the SURETY bind themselves and each of their heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents as follows:

THE CONDITION OF THE ABOVE OBLIGATION IS SUCH THAT:
WHEREAS, the CONTRACTOR has executed and entered into a certain Contract for,
ITB # 17-010 MLK COMMUNITY CENTER ROOF REPLACEMENT IS72011601, with the CITY, dated _____, 2016, to furnish at his own cost, charges, and expense all the necessary materials, equipment, and/or labor in strict and express accordance with said Contract and the Contract Documents as defined therein, all of which is made a part of said Contract by certain terms and conditions in said Contract more particularly mentioned, which Contract, consisting of the various Contract Documents is made a part of this Bond as fully and completely as if said Contract Documents were set forth herein;

NOW THEREFORE, the conditions of this obligation are such that if the above bounden CONTRACTOR:

1. Shall in all respects comply with the terms and conditions of said Contract and his obligation there under, including the Contract Documents (which include the scope of work and conditions as prepared by the CITY, invitation to bid, instructions to bidders, the CONTRACTOR'S bid as accepted by the above CITY, the bid and contract performance and payment bonds, and all

addenda, if any, issued prior to the opening of bids), being made a part of this bond by reference, at the times and in the manner prescribed in the contract; and

2. Promptly makes payments to all claimants, as defined in Section 255.05(1), Florida Statutes, supplying PRINCIPAL with labor, materials, or supplies, used directly or indirectly by PRINCIPAL in the prosecution of the work provided for in the contract; and

3. Pays CITY all losses, costs, expenses, damages, attorney's fees, including appellate proceedings, injury or loss of whatever kind and however arising including, without limitation, delay damages to which said CITY may be subject by reason of any wrongdoing, misconduct, want of care or skill, negligence, failure of performance, breach, failure to petition within the prescribed time, or default, including patent infringements, on the part of said CONTRACTOR, his agents or employees, in the execution or performance of said Contract; and

4. Performs the guarantee of all work and materials furnished under the contract for the time specified in the contract, then this obligation shall be void; otherwise, to remain in full force and effect for the term of said Contract.

AND, the said Surety for value received, hereby stipulates and agrees that no change involving any extension of time, or addition to the terms of the Contract Documents, or to the work to be performed, or materials to be furnished there under shall affect said obligation of said Surety on this Bond, and the said Surety does hereby waive notice of any such changes, extension of time, alterations, or additions of the terms of the Contract Documents, or to the work.

Any action instituted by a claimant under this bond for payment must be in accordance with the notice and time limitation provisions in Section 255.05(2), Florida Statutes.

IN WITNESS WHEREOF, the above parties bonded together have executed this instrument

this _____ day of _____, 2016, the name and corporate seal of each corporate party being hereto affixed and those presents duly signed by its undersigned representative, pursuant to authority of its governing body.

CONTRACTOR

By: _____

(SEAL)

ATTEST

SURETY

By: _____

(SEAL)

ATTEST

FLORIDA PAYMENT BOND

BOND NO._____

AMOUNT: $_____

KNOW ALL MEN BY THESE PRESENTS, that in accordance with Florida Statutes Section

255.05,_____

with offices at_____
hereinafter called the CONTRACTOR, (Principal), and

_____

with offices at _____

a corporation duly organized and existing under and by virtue of the laws of the State of _____

_____ , hereinafter called the SURETY, and authorized to transact business within the State of Florida, as SURETY, are held and firmly bound unto CITY OF KEY WEST**,** hereinafter called the City (Obligee), in the sum of:

_____DOLLARS ($ _____),
lawful money of the United States of America, for the payment of which, well and truly be made to the CITY, and the CONTRACTOR and the SURETY bind themselves and each of their heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these presents as follows:

THE CONDITION OF THE ABOVE OBLIGATION IS SUCH THAT:

WHEREAS, the CONTRACTOR has executed and entered into a certain Contract for

ITB # 17-010 MLK COMMUNITY CENTER ROOF REPLACEMENT IS72011601

attached hereto, with the CITY, dated_____,2016,
to furnish at his own cost, charges, and expense the necessary materials, equipment, and/or labor in strict and express accordance with said Contract and the plans, drawings (if any), and specifications prepared by the CITY, all of which is made a part of said Contract by certain terms and conditions in said Contract more particularly mentioned, which Contract, consisting of the various Contract Documents specifically mentioned herein and relative hereto, is made a part of this Bond as fully and completely as if said Contract Documents were set forth herein.

NOW THEREFORE, the conditions of this obligation are such that if the above bounden CONTRACTOR shall in all respects comply with the terms and conditions of said Contract and

his obligation thereunder, including the Contract Documents, which include Scope of work and conditions prepared by the CITY, invitation to bid, instructions to bidders, the

CONTRACTOR'S bid as accepted by the CITY, the bid and contract and payment bonds, and all addenda, if any, issued prior to the opening of bids), and further that if said CONTRACTOR shall promptly make payments to all persons supplying materials, equipment, and/or labor, used directly or indirectly by said CONTRACTOR or subcontractors in the prosecution of the work for said contract is accordance with Florida Statutes, Section 255.05 or Section 713.23, then this obligation shall be void; otherwise to remain in full force and effect for the term of said contract, including and all guarantee periods as specifically mentioned in said Contract Documents.

AND, the said SURETY for value received, hereby stipulates and agrees that no change involving any extension of time, or addition to the terms of the Contract or to the work to be performed, or materials to be furnished thereunder, or in the Contract Documents and specifications accompanying the said contract shall affect said obligation of said SURETY on this Bond, and the said SURETY does hereby waive notice of any such changes, extension of time, alternations, or additions of the terms of the Contract, or to the work, to the Contract Documents, or to the specifications.

Claimant shall give written notice to the CONTRACTOR and the SURETY as required by Section 255.05 or Section 713.23, Florida Statutes. Any action instituted against the CONTRACTOR or SURETY under this bond for payment must be in accordance with the notice and time limitation provisions in Section 255.05(2) or Section 713.23, Florida Statutes.

IN WITNESS WHEREOF, the above parties bounded together have executed this instrument

this _____ day of _____, 2016, the name and corporate seal of each corporate party being hereto affixed and those presents duly signed by its undersigned representative, pursuant to authority of its governing body.

CONTRACTOR

By:_____

(SEAL)

ATTEST

SURETY

By:_____

(SEAL)

ATTEST

PART 3

CONDITIONS OF THE CONTRACT

GENERAL CONDITIONS
CONTENTS

Article

DEFINITIONS

1. AS APPROVED
2. AS SHOWN, AND AS INDICATED
3. BIDDER
4. CONTRACT DOCUMENTS
5. CONTRACTOR
6. CONTRACT COMPLETION
7. DAYS
8. DRAWINGS
9. ENGINEER
10. NOTICE
11. OR EQUAL
12. OWNER
13. PLANS
14. SPECIFICATIONS
15. NOTICE TO PROCEED
16. SUBSTANTIAL COMPLETION
17. WORK

CONTRACT DOCUMENTS

18. INTENT OF CONTRACT DOCUMENTS
19. DISCREPANCIES AND OMISSIONS
20. CHANGES IN THE WORK
21. EXAMINATION AND VERIFICATION OF CONTRACT DOCUMENTS
22. DOCUMENTS TO BE KEPT ON THE JOBSITE
23. ADDITIONAL CONTRACT DOCUMENTS
24. OWNERSHIP OF CONTRACT DOCUMENTS

THE ENGINEER

25. AUTHORITY OF THE ENGINEER
26. DUTIES AND RESPONSIBILITIES OF THE ENGINEER
27. LIMITATIONS ON ENGINEER'S RESPONSIBILITIES
28. REJECTED WORK
29. LINES AND GRADES
30. SUBMITTALS
31. DETAIL DRAWINGS AND INSTRUCTIONS

THE CONTRACTOR AND HIS EMPLOYEES

32. CONTRACTOR, AN INDEPENDENT AGENT
33. SUBCONTRACTING
34. INSURANCE AND LIABILITY
    A. GENERAL
    B. CONTRACTOR AND SUB-CONTRACTOR INSURANCE
    C. COMPENSATION AND EMPLOYER'S LIABILITY INSURANCE
    D. GENERAL LIABILITY INSURANCE (INCLUDING AUTOMOBILE)
    E. BUILDER'S RISK ALL RISK INSURANCE
    F. NO PERSONAL LIABILITY OF PUBLIC OFFICIALS
35. INDEMNITY
36. EXCLUSION OF CONTRACTOR CLAIMS
37. TAXES AND CHARGES
38. REQUIREMENTS OF STATE LAW FOR PUBLIC WORKS PROJECTS
39. CODES, ORDINANCES, PERMITS, AND LICENSES
40. SUPERINTENDENCE
41. RECEPTION OF ENGINEER'S COMMUNICATIONS
42. SAFETY
43. PROTECTION OF WORK AND PROPERTY
44. RESPONSIBILITY OF CONTRACTOR TO ACT IN AN EMERGENCY
45. MATERIALS AND APPLIANCES
46. CONTRACTORS' AND MANUFACTURERS' COMPLIANCE WITH STATE SAFETY, OSHA AND OTHER CODE REQUIREMENTS
47. SUBSTITUTION OF MATERIALS
48. TESTS, SAMPLES, AND OBSERVATIONS
49. ROYALTIES AND PATENT
50. CONTRACTOR'S RIGHT TO TERMINATE CONTRACT
51. CORRECTION OF DEFECTIVE WORK DURING WARRANTY PERIOD

PROGRESS OF THE WORK

52. BEGINNING OF THE WORK
53. SCHEDULES AND PROGRESS REPORTS
54. PROSECUTION OF THE WORK
55. OWNER'S RIGHT TO RETAIN IMPERFECT WORK
56. OWNER'S RIGHT TO DO WORK
57. OWNER'S RIGHT TO TRANSFER EMPLOYMENT
58. DELAYS AND EXTENSION OF TIME
59. DIFFERING SITE CONDITION

GENERAL CONDITIONS
CONTENTS

Article

60. LIQUIDATED DAMAGES
61. OTHER CONTRACTS
62. USE OF PREMISES
63. SUBSTANTIAL COMPLETION DATE
64. PERFORMANCE TESTING
65. OWNER'S USE OF PORTION OF THE WORK
66. CUTTING AND PATCHING
67. CLEANING UP

PAYMENT

68. CHANGE ORDERS
A. UNIT PRICE
B. LUMP SUM
C. COST REIMBURSEMENT WORK
69. PARTIAL PAYMENTS
A. GENERAL
B. ESTIMATE
C. DEDUCTION FROM ESTIMATE
D. QUALIFICATIONS FOR PARTIAL PAYMENT FOR MATERIALS DELIVERED
E. PAYMENT
70. CLAIMS FOR EXTRA WORK
71. RELEASE OF LIENS OR CLAIMS
72. FINAL PAYMENT
73. NO WAIVER OF RIGHTS
74. ACCEPTANCE OF FINAL PAYMENT CONSTITUTES RELEASE

****

DEFINITIONS

Whenever in the Contract Documents the following terms are used, the intent and meaning shall be interpreted as follows:

1. AS APPROVED

The words "as approved", unless otherwise qualified, shall be understood to be followed by the words "by the ENGINEER for conformance with the Contract Document".

2. AS SHOWN, AND AS INDICATED

The words "as shown" and "as Indicated" shall be understood to be followed by the words "on the Drawings".

3. BIDDER

The person or persons, partnership, firm, or corporation submitting a Proposal for the work contemplated.

4. CONTRACT DOCUMENTS

The "Contract Documents" consist of the Bidding Requirements, Contract Forms, Conditions of the Contact, Specifications, Drawings, all modifications thereof incorporated into the Documents before their execution, Change Orders, and all other requirements incorporated by specific reference thereto. These form the Contract.

5. CONTRACTOR

The person or persons, partnership, firm, or corporation who enters into the Contract awarded him by the OWNER.

6. CONTRACT COMPLETION

The "Contract Completion" is the date the OWNER accepts the entire work as being in compliance with the Contract Documents, or formally waives nonconforming work to extent of nonconformity, and issues the final payment in accordance with the requirements set forth in Article, "Final Payment" of these General Conditions.

7. DAYS

Unless otherwise specifically stated, the term "days" will be understood to mean calendar days. Business day or working day means any day other than Saturday, Sunday, or legal holiday.

8. DRAWINGS

The term "Drawings" refers to the official Drawings, Profiles, cross sections, elevations, details, and other working drawings and supplementary drawings, or reproductions thereof, signed by the ENGINEER, which shows the location, character, dimensions, and details of the work to be performed. Drawings may either be bound in the same book as the balance of the Contract Documents, or bound in separate sets, and are a part of the Contract Documents, regardless of the method of binding.

9. ENGINEER

The person or organization identified as such in the Contract Documents. The Term "ENGINEER" means ENGINEER or his authorized representative.

10. NOTICE

The term "notice" or the requirement to notify, as used in the Contract Documents or applicable state or federal statutes, shall signify a written communication delivered in person or by registered mail to the individual, or to a member of the firm, or to an

officer of the corporation for whom it is intended. Certified or registered mail shall be addressed to the last business address known to him who gives the notice.

11. OR EQUAL

The term "or equal" shall be understood to indicate that the "equal" Product is equivalent to or better than the Product named in function, performance, reliability, quality, and general configuration. Determination of equality in reference to the Project design requirements will be made by the ENGINEER. Such equal Products shall not be purchased or installed by the CONTRACTOR without written authorization.

12. OWNER

The person, organization, or public body identified as such in the Contract Documents.

13. PLANS (See Drawings)

14. SPECIFICATIONS

The term "Specifications" refers to those portions of the Contract Documents consisting of written technical descriptions of materials, equipment, construction systems, standards, and workmanship as applied to the work and certain administrative details applicable thereto. Where standard specifications, such as those of ASTM, AASHTO, etc., have been referred to, the applicable portions of such standard specifications shall become a part of these Contract Documents. If referenced specifications conflict with specifications contained herein, the requirements contained herein shall prevail.

15. NOTICE TO PROCEED

A written notice given by the OWNER to the CONTRACTOR (with a copy to the ENGINEER) fixing the date on which the Contract time will commence to run and on which the CONTRACTOR shall start to perform his obligation under the Contract Documents. The Notice to Proceed will be given within 30 days following the execution of the Contract by the OWNER.

16. SUBSTANTIAL COMPLETION

"Substantial Completion" shall be that degree of completion of the Project or a defined portion of the Project, as evidenced by the ENGINEER's written notice of Substantial Completion, sufficient to Provide the OWNER, at his discretion, the full-time use of the Project or defined portion of the Project for the purposes for which it was intended. "Substantial Completion" of an operating facility shall be that degree of completion that has Provided a minimum of 7 continuous days of successful, trouble-free, operation, which period shall begin after all performance and acceptance testing has been successfully demonstrated to the ENGINEER. All equipment contained in the work, plus all other components necessary to enable the OWNER to operate the facility in a manner that was intended, shall be complete on the substantial completion date.

17. WORK

The word "work" within these Contract Documents shall include all material, labor, tools, and all appliances, machinery, transportation, and appurtenances necessary to perform and complete the Contract, and such additional items not specifically indicated or described which can be reasonably inferred as belonging to the item described or indicated and as required by good Practice to Provide a complete and satisfactory system or structure. As used herein, "Provide" shall be understood to mean "furnish and install, complete in-place ".

<u>CONTRACT DOCUMENTS</u>

18. INTENT OF CONTRACT DOCUMENTS

The Contract Documents are complementary, and what is called for by one shall be as binding as if called for by all. The intent of the Documents is to describe a functionally complete Project (or part thereof) to be constructed in accordance with the Contract

Documents. Any work, materials, or equipment that may reasonably be inferred from the Contract Documents as being required to produce the intended result shall be supplied whether or not specifically called for. When words which have a well-known technical or trade meaning are used to describe work, materials, or equipment, such words shall be interpreted in accordance with that meaning.

Reference to standard specifications, manuals, or codes of any technical society, organization or association, or to the laws or regulations of any governmental authority, whether such reference be specific or by implication, shall mean the latest standard specification, manual, code or laws or regulations in effect on the first published date of the Invitation to Bid, except as may be otherwise specifically stated. However, no Provision of any referenced standard specification, manual or code (whether or not specifically incorporated by reference in the Contract Documents) shall be effective to change the duties and responsibilities of OWNER, CONTRACTOR, or ENGINEER, or any of their consultants, agents, or employees from those set forth in the Contract Documents, nor shall it be effective to assign to ENGINEER, or any ENGINEER's consultants, agents, or employees, any duty or authority to supervise or direct the furnishing or performance of the work or any duty or authority to undertake responsibility contrary to the Provisions of Article LIMITATIONS ON ENGINEER'S RESPONSIBILITIES.

19. DISCREPANCIES AND OMISSIONS

Any discrepancies or omissions found in the Contract Documents shall be reported to the ENGINEER immediately. The ENGINEER will clarify discrepancies or omissions, in writing, within a reasonable time.

In resolving inconsistencies among two or more sections of the Contract Documents, Precedence shall be given in the following order:

A. CONTRACT
B. PROPOSAL
C. SUPPLEMENTARY CONDITIONS
D. INVITATION TO BID
E. INSTRUCTIONS TO BIDDERS
F. GENERAL CONDITIONS
G. SPECIFICATIONS
H. DRAWINGS

Addenda shall take Precedence over all sections referenced therein. Figure dimensions on Drawings shall take precedence over scale dimensions. Detailed Drawings shall take precedence over general Drawings.

20. CHANGES IN THE WORK

The OWNER, without notice to the Sureties and without invalidating the Contract, may order changes in the work within the general scope of the Contract by altering, adding to, or deducting from the work, the Contract being adjusted accordingly. All such work shall be executed under the conditions of the original Contract, except as specifically adjusted at the time of ordering such change.

In giving instructions, the ENGINEER may order minor changes in the work not involving extra cost and not inconsistent with the purposes of the Project, but otherwise, except in an emergency endangering life and Property, additions or deductions from the work shall be performed only in pursuance of an approved Change Order from the OWNER, countersigned by the ENGINEER.

If the work is reduced by alterations, such action shall not constitute a claim for damages based on loss of anticipated Profits.

21. EXAMINATION AND VERIFICATION OF CONTRACT DOCUMENTS

The CONTRACTOR shall thoroughly examine and become familiar with all of the various parts of these Contract Documents and determine the nature and location of the work, the general and local conditions, and all other matters, which can in any way affect the work under this Contract. Failure to make an examination necessary for this determination shall not release the CONTRACTOR from the obligations of this Contract. No verbal agreement or conversation with any officer, agent, or employee

of the OWNER or with the ENGINEER either before or after the execution of this Contract shall affect or modify any of the terms or obligations herein contained.

22. DOCUMENTS TO BE KEPT ON THE JOBSITE

The CONTRACTOR shall keep one copy of the Contract Documents on the job- site, in good order, available to the ENGINEER and to his representatives.

The CONTRACTOR shall maintain on a daily basis at the jobsite, and make available to the ENGINEER on request, one current record set of the Drawings which have been accurately marked to indicate all modifications in the completed work that differ from the design information shown on the Drawings. Upon Substantial completion of the work, the CONTRACTOR shall give the ENGINEER one complete set of these marked up record Drawings.

23. ADDITIONALCONTRACT DOCUMENTS

Copies of Contract Documents or Drawings may be obtained on request from the ENGINEER and by paying the actual cost of reproducing the Contract Documents or Drawings.

24. OWNERSHIP OF CONTRACT DOCUMENTS

All portions of the Contract Documents, and copies thereof furnished by the ENGINEER are instruments of service for this Project. They are not to be used on other work and are to be returned to the ENGINEER on request at the completion of the work. Any reuse of these materials without specific written verification or adaptation by the ENGINEER will be at the risk of the user and without liability or legal expense to the ENGINEER. Such user shall hold the ENGINEER harmless from any and all damages, including reasonable attorneys' fees, from any and all claims arising from any such reuse. Any such verification and adaptation shall entitle the ENGINEER to further compensation at rates to be agreed upon by the user and the ENGINEER.

<u>THE ENGINEER</u>

25. AUTHORITY OF THE ENGINEER

The ENGINEER will be the OWNER's representative during the construction period. His authority and responsibility will be limited to the Provisions set forth in these Contract Documents. The ENGINEER will have the Authority to reject work that does not conform to the Contract Documents. However, neither the ENGINEER's authority to act under this Provision, nor any decision made by him in good faith either to exercise or not to exercise such authority, shall give rise to any duty or responsibility of the ENGINEER to the CONTRACTOR, any SUBCONTRACTOR, their respective Sureties, any of their agents or employees, or any other person performing any of the work.

26. DUTIES AND RESPONSIBILITIES OF THE ENGINEER

The ENGINEER will make visits to the site at intervals appropriate to the various stages of construction to observe the Progress and quality of the work and to determine, in general, if the work is proceeding in accordance with the intent of the Contract Documents. He will not make comprehensive or continuous review or observation to check quality or quantity of the work, and he will not be responsible for construction means, methods, techniques, sequences, or Procedures, or for safety Precautions and Programs in connection with the work. Visits and observations made by the ENGINEER shall not relieve the CONTRACTOR of his obligation to conduct comprehensive inspections of the work and to furnish materials and perform acceptable work, and to provide adequate safety Precautions, in conformance with the intent of the Contract.

The ENGINEER will make recommendations to the OWNER, in writing, on all claims of the OWNER or the CONTRACTOR arising from interpretation or execution of the Contract Documents. Such recommendations will be of factual and/or technical nature, and will not include the legal interpretation of the Contract Documents. Any necessary legal interpretation of the Contract Document will be made by the OWNER. Such recommendation shall be necessary before the CONTRACTOR can receive additional money under the terms of the Contract. Changes in work ordered by the ENGINEER shall be made in compliance with Article CHANGES IN THE WORK.

One or more Project representatives may be assigned to observe the work. It is understood that such Project representatives shall have the authority to issue notice of nonconformance and make decisions within the limitations of the authority of the ENGINEER. The CONTRACTOR shall furnish all reasonable assistance required by the ENGINEER or Project representatives for Proper observation of the work. The above-mentioned Project representatives shall not relieve the CONTRACTOR of his obligations to conduct comprehensive inspections of the work and to furnish materials and perform acceptable work, and to provide adequate safety Precautions, in conformance with the intent of the Contract.

27. LIMITATIONS ON ENGINEER'S RESPONSIBILITIES

ENGINEER will not be responsible for CONTRACTOR's means, methods, techniques, sequences, or Procedures of construction, or the safety Precautions and Programs incident thereto, and ENGINEER will not be responsible for CONTRACTOR's failure to perform or furnish the work in accordance with the Contract Documents.

ENGINEER will not be responsible for the acts or omissions of CONTRACTOR or of any SUBCONTRACTOR, any supplier, or of any other person or organization performing or furnishing any of the work.

Whenever in the Contract Documents the terms "as ordered", "as directed", "as required", "as allowed", "as approved", or terms of like effect or import are used, or the adjectives "reasonable", "suitable", "acceptable", "Proper", or "satisfactory", or adjectives of like effect or import are used to describe a requirement, direction, review or judgment of ENGINEER as to the work, it is intended that such requirement, direction, review or judgment will be solely to evaluate the work for compliance with the Contract Documents (unless there is a specific statement indicating otherwise). The use of any such term or adjective shall not be effective to assign to ENGINEER any duty or authority to supervise or direct the furnishing or performance of the work or any duty or authority to undertake responsibility contrary to the Provisions of this Article.

28. REJECTED WORK

Any defective work or nonconforming materials or equipment that may be discovered at any time prior to expiration of the warranty period shall be removed and replaced by work which shall conform to the Provisions of the Contract Documents. Any material condemned or rejected shall be removed at once from the Project site.

Failure on the part of the ENGINEER to condemn or reject bad or inferior work or to note nonconforming materials or equipment on CONTRACTOR submittals shall not be construed to imply acceptance of such work. The OWNER shall reserve and retain all of its rights and remedies at law against the CONTRACTOR and its Surety for correction of any and all latent defects discovered after the guarantee period.

29. LINES AND GRADES

Lines and grades shall be established as provided in the supplementary conditions. All stakes, marks, and other reference information shall be carefully preserved by the CONTRACTOR, and in case of their careless or unnecessary destruction or removal by him or his employees, such stakes, marks, and other information shall be replaced at the CONTRACTOR's expense.

30. SUBMITTALS

After checking and verifying all field measurements and after complying with applicable Procedures specified in Division I, GENERAL REQUIREMENTS, CONTRACTOR shall submit to ENGINEER, in accordance with the schedule for submittals for review, shop drawings, electrical diagrams, and catalog cuts for fabricated items and manufactured items (including mechanical and electrical equipment), which shall bear a stamp or specific written indication that CONTRACTOR has satisfied CONTRACTOR's responsibilities under the Contract Documents with respect to the review of the submittal. All submittals shall be identified as ENGINEER may require. The data shown shall be complete with respect to quantities, dimensions specified, performance and design criteria, materials, and similar data to enable ENGINEER to review the information. CONTRACTOR shall also submit to ENGINEER for review, with such promptness as to cause no delay in work, all samples required by the Contract Documents. All samples shall have been checked by and accompanied by a specific written indication that CONTRACTOR has satisfied CONTRACTOR's responsibilities under the Contract Documents with respect to the review of the submission and shall be identified clearly as to material, supplier, pertinent data such as catalog numbers and the use for which

intended.

Before submission of each submittal, CONTRACTOR shall have determined and verified all quantities, dimensions, specified performance criteria, installation requirements, materials, catalog numbers, and similar data with respect thereto and reviewed or coordinated each submittal with other submittals and with the requirements of the work and the Contract Documents.

At the time of each submission, CONTRACTOR shall give ENGINEER specific written notice of each variation that the submittal may have from the requirements of the Contract Documents, and, in addition, shall cause a specific notation to be made on each shop drawing submitted to ENGINEER for review and approval of each variation.

ENGINEER will review submittals with reasonable Promptness, but ENGINEER's review will be only for conformance with the design concept of the Project and for compliance with the information given in the Contract Documents and shall not extend to means, methods, techniques, sequences, or Procedures of construction (except where a specific means, method, technique, sequence, or Procedure of construction is indicated in or required by the Contract Documents) or to safety Precautions or Programs incident thereto. The review of a separate item as such will not indicate review of the assembly in which the item functions. CONTRACTOR shall make corrections required by ENGINEER, and shall return the required number of corrected copies of shop drawings and submit as required new samples for review. CONTRACTOR shall direct specific attention in writing to revisions other than the corrections called for by ENGINEER on Previous submittals.

ENGINEER's review of submittals shall not relieve CONTRACTOR from the responsibility for any variation from the requirements of the Contract Documents unless CONTRACTOR has in writing called ENGINEER's attention to each such variation at the time of submission and ENGINEER has given written approval of each such variation by a specific written notation thereof incorporated therein or accompanying the shop drawing or sample approval; nor will any approval by ENGINEER relieve CONTRACTOR from responsibility for errors or omissions in the shop drawings or from responsibility for having complied with the Provisions herein.
Where a shop drawing or sample is required by the specifications, any related work performed prior to ENGINEER's review and approval of the pertinent submission shall be at the sole expense and responsibility of the CONTRACTOR.

31. DETAIL DRAWINGS AND INSTRUCTIONS

The ENGINEER will furnish, with reasonable Promptness, additional instructions by means of Drawings or otherwise, if, in the ENGINEER's opinion, such are required for the Proper execution of the work. All such Drawings and instructions will be consistent with the Contract Documents, true developments thereof, and reasonably inferable there from.

<u>THE CONTRACTOR AND HIS EMPLOYEES</u>

32. CONTRACTOR, AN INDEPENDENT AGENT

The CONTRACTOR shall independently perform all work under this Contract and shall not be considered as an agent of the OWNER or of the ENGINEER, nor shall the CONTRACTOR's SUBCONTRACTORS or employees be subagents of the OWNER or of the ENGINEER.

33. SUBCONTRACTING

Unless modified in the Supplementary Conditions, within 10 days after the execution of the Contract, the CONTRACTOR shall submit to the ENGINEER the names of all SUBCONTRACTORS Proposed for the work, including the names of any SUBCONTRACTORS that were submitted with the Proposal. The CONTRACTOR shall not employ any SUBCONTRACTORS to which the OWNER may object to as lacking capability to properly perform work of the type and scope anticipated.

The CONTRACTOR is as fully responsible to the OWNER for the acts and omissions of his SUBCONTRACTORS and of persons either directly or indirectly employed by them as he is for the acts and omissions of persons directly employed by him.

Nothing contained in the Contract Documents shall create any contractual relationship between any SUBCONTRACTOR and the OWNER or ENGINEER.

34. INSURANCE AND LIABILITY

A. GENERAL

The CONTRACTOR shall provide (from insurance companies acceptable to the OWNER) the insurance coverage designated hereinafter and pay all costs before commencing work under this Contract. The CONTRACTOR shall furnish the OWNER with certificates of insurance specified herein showing the type, amount class of operations covered, effective dates, and date of expiration of policies, and containing substantially the following statement:

"The insurance covered by this certificate shall not be canceled or materially altered, except after 30 days' written notice has been received by the OWNER."

In case of the breach of any Provision of this Article, the OWNER, at his option, may take out and maintain, at the expense of the CONTRACTOR, such insurance as the OWNER may deem Proper and may deduct the cost of such insurance from any monies which may be due or become due the CONTRACTOR under this Contract.

B. CONTRACTOR AND SUBCONTRACTOR INSURANCE

The CONTRACTOR shall not commence work under this Contract until he has obtained all the insurance required hereunder and such insurance has been reviewed by the OWNER, nor shall the CONTRACTOR allow any SUBCONTRACTOR to commence work on his subcontract until insurance specified below has been obtained. Review of the insurance by the OWNER shall not relieve or decrease the liability of the CONTRACTOR hereunder.

C. COMPENSATION AND EMPLOYER'S LIABILITY INSURANCE

The CONTRACTOR shall maintain during the life of this Contract the statutory amount of Workmen's Compensation Insurance, in addition, Employer's Liability Insurance in an amount as specified in the Supplementary Conditions, for each occurrence, for all of his employees to be engaged in work on the Project under this Contract. In case any such work is subcontracted, the CONTRACTOR shall require the SUBCONTRACTOR to provide similar Workmen's Compensation and Employer's Liability Insurance for all of the SUBCONTRACTOR's employees to be engaged in such work.

D. GENERAL LIABILITY INSURANCE (INCLUDING AUTOMOBILE)

The CONTRACTOR shall maintain during the life of this Contract such general liability, completed operations and Products liability, and automobile liability insurance as will Provide coverage for claims for damages for personal injury, including accidental death, as well as for claims for Property damage, which may arise directly or indirectly from performance of the work under this Contract. The general liability policy shall include contractual liability assumed by the CONTRACTOR under Article **INDEMNITY.** Coverage for Property damage shall be on a "broad form" basis with no exclusions for "X, C & U". The amount of insurance to be provided shall be as specified in the Supplementary Conditions.

In the event any work under this Contract is performed by a SUBCONTRACTOR, the CONTRACTOR shall be responsible for any liability directly or indirectly arising out of the work performed by the SUBCONTRACTOR; to the extent such liability is not covered by the SUBCONTRACTOR's insurance.

The OWNER and ENGINEER, their officers, agents, and employees shall be named as Additional Insured's on the CONTRACTOR's and any SUBCONTRACTOR's general liability and automobile liability insurance policies for any claims arising out of work performed under this Contract.

E. BUILDERS RISK ALL RISK INSURANCE

Unless otherwise modified in the Supplementary Conditions, the CONTRACTOR shall secure and maintain during the life of this Contract, Builders Risk All Risk Insurance coverage in an amount equal to the full value of the facilities under construction. Such insurance shall include coverage for earthquake, landslide, flood, collapse, loss due to the results of faulty workmanship or design, and all other normally covered risks, and shall provide for losses to be paid to the CONTRACTOR, OWNER, and ENGINEER as

their interests may appear.

The OWNER and ENGINEER, their officers, agents, and employees shall be named as additional insured's on the CONTRACTOR's and any SUBCONTRACTOR's Builders Risk All Risk insurance policies for any claims arising out of work performed under this Contract.

This insurance shall include a waiver of subrogation as to the ENGINEER, the OWNER, the CONTRACTOR, and their respective officers, agents, employees and SUBCONTRACTORS.

F. NO PERSONAL LIABILITY OF PUBLIC OFFICIALS

In carrying out any of the Provisions hereof in exercising any authority granted by the Contract, there will be no personal liability upon any public official.

35. INDEMNITY

To the maximum extent permitted by law, the CONTRACTOR shall indemnify and defend the OWNER and the ENGINEER, and their officers, employees, agents, and sub-consultants, from all claims and losses, including attorney's fees and litigation costs arising out of Property losses or health, safety, personal injury, or death claims by the CONTRACTOR, its SUBCONTRACTORS of any tier, and their employees, agents, or invitees regardless of the fault, breach of Contract, or negligence of the OWNER or ENGINEER, excepting only such claims or losses that have been adjudicated to have been caused solely by the negligence of the OWNER or the ENGINEER and regardless of whether or not the CONTRACTOR is or can be named a party in a litigation.

36. EXCLUSION OF CONTRACTOR CLAIMS

In performing its obligations, the ENGINEER and its consultants may cause expense for the CONTRACTOR or its SUBCONTRACTORS and equipment or material suppliers. However, those parties and their sureties shall maintain no direct action against the ENGINEER, its officers, employees, agents, and consultants for any claim arising out of, in connection with, or resulting from the engineering services performed or required to be performed.

37. TAXES AND CHARGES

The CONTRACTOR shall withhold and pay any and all sales and use taxes and all withholding taxes, whether State or Federal, and pay all Social Security charges and also all State Unemployment Compensation charges, and pay or cause to be withheld, as the case may be, any and all taxes, charges, or fees or sums whatsoever, which are now or may hereafter be required to be paid or withheld under any laws.

38. REQUIREMENTS OF STATE LAW FOR PUBLIC WORKS PROJECTS

When the Contract Documents concern public works of the state or any county, municipality, or political subdivision created by its laws, the applicable statutes shall apply. All parties to this Contract shall determine the contents of all applicable statutes and comply with their Provisions throughout the performance of the Contract.

39. CODES, ORDINANCES, PERMITS AND LICENSES

The CONTRACTOR shall keep himself fully informed of all local codes and ordinances, as well as state and federal laws, which in any manner affect the work herein specified. The CONTRACTOR shall at all times comply with said codes and ordinances, laws, and regulations, and Protect and indemnify the OWNER, the ENGINEER and their respective employees, and its officers and agents against any claim or liability arising from or based on the violation of any such laws, ordinances, or regulations. All permits, licenses and inspection fees necessary for Prosecution and completion of the work shall be secured and paid for by the CONTRACTOR, unless otherwise specified.

40. SUPERINTENDENCE

The CONTRACTOR shall keep at the project site, competent supervisory personnel. The CONTRACTOR shall designate, in writing, before starting work, a Project superintendent who shall be an employee of the CONTRACTOR and shall have complete authority to represent and to act for the CONTRACTOR. ENGINEER shall be notified in writing prior to any change in superintendent assignment. The CONTRACTOR shall give efficient supervision to the work, using his best skill and attention. The CONTRACTOR shall be solely responsible for all construction means, methods, techniques, and Procedures, and for providing adequate safety Precautions and coordinating all portions of the work under the Contract. It is specifically understood and agreed that the ENGINEER, its employees and agents, shall not have control or charge of and shall not be responsible for the construction means, methods, techniques, Procedures, or for providing adequate safety Precautions in connection with the work under Contract.

41. RECEPTION OF ENGINEER'S COMMUNICATIONS

The superintendent shall receive for the CONTRACTOR all communications from the ENGINEER. Communications of major importance will be confirmed in writing upon request from the CONTRACTOR.

The ENGINEER may schedule Project meetings for the purposes of discussing and resolving matters concerning the various elements of the work. Time and place for these meetings and the names of persons required to be Present shall be as determined by the ENGINEER. CONTRACTOR shall comply with these attendance requirements and shall also require his SUBCONTRACTORS to comply.

42. SAFETY

The CONTRACTOR shall be solely and completely responsible for conditions of the jobsite, including safety of all persons (including employees) and Property during performance of the work. This requirement shall apply continuously and not be limited to normal working hours. Safety Provisions shall conform to U.S. Department of Labor (OSHA), and all other applicable federal, state, county, and local laws, ordinances, codes, and regulations. Where any of these are in conflict, the more stringent requirement shall be followed. The CONTRACTOR's failure to thoroughly familiarize himself with the aforementioned safety Provisions shall not relieve him from compliance with the obligations and penalties set forth therein.

The CONTRACTOR shall develop and maintain for the duration of this Contract, a safety Program that will effectively incorporate and implement all required safety Provisions. The CONTRACTOR shall appoint an employee who is qualified and authorized to supervise and enforce compliance with the safety Program. The duty of the ENGINEER to conduct construction review of the work does not include review or approval of the adequacy of the CONTRACTOR's safety Program, safety supervisor, or any safety measures taken in, on, or near the construction site. The CONTRACTOR, as a part of his safety Program, shall maintain at his office or other well-known place at the jobsite, safety equipment applicable to the work as Prescribed by the aforementioned authorities, all articles necessary for giving first-aid to the injured, and shall establish the Procedure for the immediate removal to a hospital or a doctor's care of persons (including employees) who may be injured on the jobsite.

If death or serious injuries or serious damages are caused, the accident shall be reported immediately by telephone or messenger to both the ENGINEER and the OWNER. In addition, the CONTRACTOR must promptly report in writing to the ENGINEER all accidents whatsoever arising out of, or in connection with, the performance of the work whether on, or adjacent to, the site, giving full details and statements of witnesses.

If a claim is made by anyone against the CONTRACTOR or any SUBCONTRACTOR on account of any accident, the CONTRACTOR shall promptly report the facts in writing to the ENGINEER, giving full details of the claim.

43. PROTECTION OF WORK AND PROPERTY

The CONTRACTOR shall at all times safely guard and Protect from damage the OWNER's Property, adjacent Property, and his own work from injury or loss in connection with this Contract. All facilities required for Protection by federal, state, or municipal laws and regulations and local conditions must be provided and maintained.

The CONTRACTOR shall Protect his work and materials from damage due to the nature of the work, the elements, carelessness of other CONTRACTORs, or from any cause whatever until the completion and acceptance of the work. All loss or damages arising out of the nature of the work to be done under these Contract Documents, or from any unforeseen obstruction or defects which may be encountered in the Prosecution of the work, or from the action of the elements, shall be sustained by the

CONTRACTOR.

44. RESPONSIBILITY OF CONTRACTOR TO ACT IN AN EMERGENCY

In case of an emergency which threatens loss or injury of Property, and/or safety of life, the CONTRACTOR shall act, without previous instructions from the OWNER or ENGINEER, as the situation may warrant. The CONTRACTOR shall notify the ENGINEER thereof immediately thereafter. Any claim for compensation by the CONTRACTOR, together with substantiating documents in regard to expense, shall be submitted to the OWNER through the ENGINEER and the amount of compensation shall be determined by agreement.

45. MATERIALS AND APPLIANCES

Unless otherwise stipulated, the CONTRACTOR shall Provide and pay for all materials, labor, water, tools, equipment, heat, light, fuel, power, transportation, construction equipment and machinery, appliances, telephone, sanitary facilities, temporary facilities and other facilities and incidentals necessary for the execution and completion of the work.

Unless otherwise specified, all materials shall be new, and both workmanship and materials shall be of good quality. The CONTRACTOR shall, if required, furnish satisfactory evidence as to the kind and quality of materials.

In selecting and/or approving equipment for installation in the Project, the OWNER and ENGINEER assume no responsibility for injury or claims resulting from failure of the equipment to comply with applicable federal, state, and local safety codes or requirements, or the safety requirements of a recognized agency, or failure due to faulty design concepts, or defective workmanship and materials.

46. CONTRACTORS' AND MANUFACTURERS' COMPLIANCE WITH STATE SAFETY, OSHA, AND OTHER CODE REQUIREMENTS

The completed work shall include all necessary permanent safety devices, such as machinery guards and similar ordinary safety items required by the state and federal (OSHA) industrial authorities and applicable local and national codes. Further, any features of the work subject to such safety regulations shall be fabricated, furnished, and installed (including OWNER-furnished equipment) in compliance with these requirements. CONTRACTORs and manufacturers of equipment shall be held responsible for compliance with the requirements included herein. CONTRACTORs shall notify all equipment suppliers and SUBCONTRACTORS of the Provisions of this Article.

47. SUBSTITUTION OF MATERIALS

Except for OWNER-selected equipment items, and items where no substitution is clearly specified, whenever any material, article, device, Product, fixture, form, type of construction, or Process is indicated or specified by patent or Proprietary name, by name of manufacturer, or by catalog number, such specifications shall be deemed to be used for the purpose of establishing a standard of quality and facilitating the description of the material or Process desired. This Procedure is not to be construed as eliminating from competition other Products of equal or better quality by other manufacturers where fully suitable in design, and shall be deemed to be followed by the words "or equal". The CONTRACTOR may, in such cases, submit complete data to the ENGINEER for consideration of another material, type, or Process that shall be substantially equal in every respect to that so indicated or specified. Substitute materials shall not be used unless approved in writing. The ENGINEER will be the sole judge of the substituted article or material.

48. TESTS, SAMPLES, AND OBSERVATIONS

The CONTRACTOR shall furnish, without extra charge, the necessary test pieces and samples, including facilities and labor for obtaining the same, as requested by the ENGINEER. When required, the CONTRACTOR shall furnish certificates of tests of materials and equipment made at the point of manufacture by a recognized testing laboratory.

The OWNER, ENGINEER, and authorized government agents, and their representatives shall at all times be Provided safe access to the work wherever it is in Preparation or Progress, and the CONTRACTOR shall Provide facilities for such access and for

observations, including maintenance of temporary and permanent access.

If the Specifications, laws, ordinances, or any public authority require any work, to be specially tested or approved, the CONTRACTOR shall give timely notice of its readiness for observations. If any work should be covered up without approval or consent of the ENGINEER, it shall, if required by the ENGINEER, be uncovered for examination at the CONTRACTOR's expense.
Reexamination of questioned work may be ordered by the ENGINEER, and, if so ordered, the work shall be uncovered by the CONTRACTOR. If such work is found to be in accordance with the Contract Documents, the OWNER will pay the cost of uncovering, exposure, observation, inspection, testing and reconstruction. If such work is found to be not in accordance with the Contract Documents, the CONTRACTOR shall correct the defective work, and the cost of reexamination and correction of the defective work shall be paid by the CONTRACTOR.

49. ROYALTIES AND PATENTS

The CONTRACTOR shall pay all royalty and licenses fees, unless otherwise specified. The CONTRACTOR shall defend all suits or claims for infringement of any patent rights and shall save the OWNER and the ENGINEER harmless from any and all loss, including reasonable attorneys' fees, on account thereof.

50. CONTRACTOR'S RIGHT TO TERMINATE CONTRACT

If the work should be stopped under an order of any court or other public authority for a period of more than 3 months, through no act or fault of the CONTRACTOR, its SUBCONTRACTORS, or respective employees or if the ENGINEER should fail to make recommendation for payment to the OWNER or return payment request to CONTRACTOR for revision within 30 days after it is due, or if the OWNER should fail to pay the CONTRACTOR within 30 days after time specified in Article PARTIAL PAYMENTS, any sum recommended by the ENGINEER, then the CONTRACTOR may, upon 15 days' written notice to the OWNER and the ENGINEER, stop work or terminate this Contract and recover from the OWNER payment for all acceptable work performed and reasonable termination expenses, unless said default has been remedied.

51. CORRECTION OF DEFECTIVE WORK DURING WARRANTY PERIOD

The CONTRACTOR hereby agrees to make, at his own expense, all repairs or replacements necessitated by defects in materials or workmanship, Provided under terms of this Contract, and pay for any damage to other works resulting from such defects, which become evident within 2 years after the date of final acceptance of the work or within 2 years after the date of substantial completion established by the ENGINEER for specified items of equipment, or within such longer period as may be Prescribed by law or by the terms of any applicable special guarantee required by the Contract Documents. Un-remedied defects identified for correction during the warranty period but remaining after its expiration shall be considered as part of the obligations of the warranty. Defects in material, workmanship, or equipment which are remedied as a result of obligations of the warranty shall subject the remedied portion of the work to an extended warranty period of 2 years after the defect has been remedied.

The CONTRACTOR further assumes responsibility for a similar guarantee for all work and materials provided by SUBCONTRACTORS or manufacturers of packaged equipment components. The effective date for the start of the guarantee or warranty period for equipment qualifying as substantially complete is defined in Article SUBSTANTIAL COMPLETION, AND Article SUBSTANTIAL COMPLETION DATE, in these General Conditions.

The CONTRACTOR also agrees to hold the OWNER and the ENGINEER harmless from liability of any kind arising from damage due to said defects. The CONTRACTOR shall make all repairs and replacements promptly upon receipt of written order for same from the OWNER. If the CONTRACTOR fails to make the repairs and replacements promptly, or in an emergency where delay would cause serious risk, or loss, or damage, the OWNER may have the defective work corrected or the rejected work removed and replaced, and the CONTRACTOR and his Surety shall be liable for the cost thereof.

<u>PROGRESS OF THE WORK</u>

52. BEGINNING OF THE WORK

Following execution of the Contract, the CONTRACTOR shall meet with the OWNER and ENGINEER relative to his arrangements for prosecuting the work.

53. SCHEDULES AND PROGRESS REPORTS

Prior to starting the construction, the CONTRACTOR shall Prepare and submit to the ENGINEER, a Progress schedule showing the dates on which each part or division of the work is expected to be started and finished, and a Preliminary schedule for submittals. The Progress schedule for submittals shall be brought up to date and submitted to the ENGINEER at the end of each month or at such other times the ENGINEER may request.

The CONTRACTOR shall forward to the ENGINEER, at the end of each month, an itemized report of the delivery status of major and critical items of purchased equipment and material, including shop drawings and the status of shop and field fabricated work. These Progress reports shall indicate the date of the purchase order, the current percentage of completion, estimated delivery, and cause of delay, if any.
If the completion of any part of the work or the delivery of materials is behind the submitted Progress schedule, the CONTRACTOR shall submit in writing a plan acceptable to the OWNER and ENGINEER for bringing the work up to schedule.

The OWNER shall have the right to withhold Progress payments for the work if the CONTRACTOR fails to update and submit the Progress schedule and reports as specified.

54. PROSECUTION OF THE WORK

It is expressly understood and agreed that the time of beginning, rate of Progress, and time of completion of the work are the essence of this Contract. The work shall be prosecuted at such time, and in or on such part or parts of the Project as may be required, to complete the Project as contemplated in the Contract Documents and the Progress schedule.

If the CONTRACTOR desires to carry on work at night or outside the regular hours, he shall give timely notice to the ENGINEER to allow satisfactory arrangements to be made for observing the work in Progress.

55. OWNER'S RIGHT TO RETAIN IMPERFECT WORK

If any part or portion of the work completed under this Contract shall Prove defective and not in accordance with the Drawings and Specifications, and if the imperfection in the same shall not be of sufficient magnitude or importance as to make the work dangerous or unsuitable, or if the removal of such work will create conditions which are dangerous or undesirable, the OWNER shall have the right and authority to retain such work but will make such deductions in the final payment therefore as may be just and reasonable.

56. OWNER'S RIGHT TO DO WORK

Should the CONTRACTOR neglect to Prosecute the work in conformance with the Contract Documents or neglect or refuse at his own cost to remove and replace work rejected by the ENGINEER, then the OWNER may notify the Surety of the condition, and after 10 days' written notice to the CONTRACTOR and the Surety, or without notice if an emergency or danger to the work or public exists, and without Prejudice to any other right which the OWNER may have under Contract, or otherwise, take over that portion of the work which has been improperly or non-timely executed, and make good the deficiencies and deduct the cost thereof from the payments then or thereafter due the CONTRACTOR.

57. OWNER'S RIGHT TO TRANSFER EMPLOYMENT

If the CONTRACTOR should abandon the work or if he should persistently or repeatedly refuse or should fail to make prompt payment to SUBCONTRACTORS for material or labor, or to persistently disregard laws, ordinances, or to prosecute the work in conformance with the Contract Documents, or otherwise be guilty of a substantial violation of any Provision of the Contract or any laws or ordinance, then the OWNER may, without Prejudice to any other right or remedy, and after giving the CONTRACTOR and Surety 10 days' written notice, transfer the employment for said work from the CONTRACTOR to the Surety. Upon receipt of such notice, such Surety shall enter upon the Premises and take possession of all materials, tools, and

appliances thereon for the purpose of completing the work included under this contract and employ by Contract or otherwise, any qualified person or persons to finish the work and Provide the materials therefore, in accordance with the Contract Documents, without termination of the continuing full force and effect of this contract. In case of such transfer of employment to such Surety, the Surety shall be paid in its own name on estimates according to the terms hereof without any right of the CONTRACTOR to make any claim for the same or any part thereof.

If, after the furnishing of said written notice to the Surety, the CONTRACTOR and the Surety still fail to make reasonable Progress on the performance of the work, the OWNER may terminate the employment of the CONTRACTOR and take possession of the Premises and of all materials, tools, and appliances thereon and finish the work by whatever method he may deem expedient and charge the cost thereof to the CONTRACTOR and the Surety. In such case, the CONTRACTOR shall not be entitled to receive any further payment until the work is finished. If the expense of completing the Contract, including compensation for additional managerial and administrative services, shall exceed such unpaid balance, the CONTRACTOR and the Surety shall pay the difference to the OWNER.

58. DELAYS AND EXTENSION OF TIME

If the CONTRACTOR is delayed in the Progress of the work by any act or neglect of the OWNER or the ENGINEER, or by any separate CONTRACTOR employed by the OWNER, or by strikes, lockouts, fire, adverse weather conditions not reasonably anticipated, or acts of Nature, and if the CONTRACTOR, within 48 hours of the start of the occurrence, gives written notice to the OWNER of the cause of the potential delay and estimate of the possible time extension involved, and within 10 days after the cause of the delay has been remedied, the CONTRACTOR gives written notice to the OWNER of any actual time extension requested as a result of the aforementioned occurrence, then the Contract time may be extended by change order for such reasonable time as the ENGINEER determines. It is agreed that no claim shall be made or allowed for any damages, loss, or expense which may arise out of any delay caused by the above referenced acts or occurrences other than claims for the appropriate extension of time. No extension of time will be granted to the CONTRACTOR for delays occurring to parts of the work that have no measurable impact on the completion of the total work under this Contract. No extension of time will be considered for weather conditions reasonably anticipated for the area in which the work is being performed. Reasonably anticipated weather conditions will be based on official records of monthly Precipitation and other historical data. Adverse weather conditions, if determined to be of a severity that would impact Progress of the work, may be considered as cause for an extension of Contract completion time.

Delays in delivery of equipment or material purchased by the CONTRACTOR or his SUBCONTRACTORS, including OWNER-selected equipment shall not be considered as a just cause for delay, unless the OWNER determines that for good cause the delay is beyond the control of the CONTRACTOR. The CONTRACTOR shall be fully responsible for the timely ordering, scheduling, complete the work is the per-diem rate, as stipulated in the Proposal. The said amount is hereby agreed upon as a reasonable estimate of the costs, which may be accrued by the OWNER after the expiration of the time of completion. It is expressly understood and agreed that this amount is not to be considered in the nature of a penalty, but as liquidated damages which have accrued against the CONTRACTOR. The OWNER shall have the right to deduct such damages from any amount due, or that may become due the CONTRACTOR, or the amount of such damages shall be due and collectible from the CONTRACTOR or Surety.

59. DIFFERING SITE CONDITIONS

The CONTRACTOR shall promptly, and before the conditions are disturbed, give a written notice to the OWNER and ENGINEER of:

A. subsurface or latent physical conditions at the site which differ materially from those indicated in this contract,
B. unknown physical conditions at the site, of an unusual nature, which differ materially from those ordinarily encountered and generally recognized as inherent in work of the character provided for in the Contract.

The ENGINEER will investigate the site conditions promptly after receiving the notice. If the conditions do materially so differ and cause an increase or decrease in the CONTRACTOR's cost of, or the time required for, performing any part of the work under this Contract, whether or not changed as a result of the conditions, and equitable adjustment shall be made under this Article and the Contract modified in writing accordingly.

No request by the CONTRACTOR for an equitable adjustment to the Contract under this Article will be allowed, unless the

CONTRACTOR has given the written notice required; Provided that the time prescribed above for giving written notice may be extended by the OWNER.

No request by the CONTRACTOR for an equitable adjustment to the Contract for differing site conditions will be allowed if made after final payment under this Contract.

60. LIQUIDATED DAMAGES

Should the CONTRACTOR fail to complete the work, or any part thereof, in the time agreed upon in the Contract or within such extra time as may have been allowed for delays by extensions granted as Provided in the Contract, the CONTRACTOR shall reimburse the OWNER for the additional expense and damage for each calendar day, Sundays and legal holidays included, that the Contract remains uncompleted after the Contract completion date. It is agreed that the amount of such additional expense and damage incurred by reason of failure to complete the work is the per-diem rate, as stipulated in the Proposal. The said amount is hereby agreed upon as a reasonable estimate of the costs which may be accrued by the OWNER after the expiration of the time of completion. It is expressly under- stood and agreed that this amount is not to be considered in the nature of a penalty, but as liquidated damages which have accrued against the CONTRACTOR. The OWNER shall have the right to deduct such damages from any amount due, or that may become due the CONTRACTOR, or the amount of such damages shall be due and collectible from the CONTRACTOR or Surety.

61. OTHER CONTRACTS

The OWNER reserves the right to let other Contracts in connection with the work. The CONTRACTOR shall afford other CONTRACTORs reasonable opportunity for the introduction and storage of their materials and the execution of their work and shall properly connect and coordinate his work with theirs.

If any part of the work under this Contract depends for Proper execution or results upon the work of any other CONTRACTOR, utility service company or OWNER, the CONTRACTOR shall inspect and Promptly report to the ENGINEER in writing any patent or apparent defects to deficiencies in such work that render it unsuitable for such Proper execution and results. The CONTRACTOR's failure to so report shall constitute and acceptance of the work by others as being fit and Proper for integration with work under this Contract, except for latent or non-apparent defects and deficiencies in the work.

62. USE OF PREMISES

The CONTRACTOR shall confine his equipment, the storage of materials and the operation of his workers to limits shown on the Drawings or indicated by law, ordinances, permits, or directions of the ENGINEER, and shall not unreasonably encumber the Premises with his materials. The CONTRACTOR shall provide, at his own expense, the necessary rights-of-way and access to the work, which may be required outside the limits of the OWNER's Property and shall furnish the ENGINEER copies of permits and agreements for use of the Property outside that provided by the OWNER.

The CONTRACTOR shall not load nor permit any part of the structure to be loaded in any manner that will endanger the structure, nor shall CONTRACTOR subject any part of the work or adjacent Property to stresses or Pressures that will endanger it.

63. SUBSTANTIAL COMPLETION DATE

The ENGINEER may issue a written notice of substantial completion for the purpose of establishing the starting date for specific equipment guarantees, and to establish the date that the OWNER will assume the responsibility for the cost of operating such equipment. Said notice shall not be considered as final acceptance of any portion of the work or relieve the CONTRACTOR from completing the remaining work within the specified time and in full compliance with the Contract Documents. See SUBSTANTIAL COMPLETION under DEFINITIONS of these General Conditions.

64. PERFORMANCE TESTING

Operating equipment and systems shall be performance tested in the Presence of the ENGINEER to demonstrate compliance with the specified requirements. Performance testing shall be conducted under the specified design operating conditions or under such

simulated operating conditions as recommended or approved by the ENGINEER. Schedule such testing with the ENGINEER at least one week in advance of the planned date for testing.

65. OWNER'S USE OF PORTIONS OF THE WORK

Following issuance of the written notice of Substantial Completion, the OWNER may initiate operation of the facility. Such use shall not be considered as final acceptance of any portion of the work, nor shall such use be considered as cause for an extension of the Contract completion time, unless authorized by a Change Order issued by the OWNER.

66. CUTTING AND PATCHING

The CONTRACTOR shall do all cutting, fitting, or patching of his work that may be required to make its several parts come together Properly and fit it to receive or be received by work of other CONTRACTORs shown upon or reasonably implied by the Drawings.

67. CLEANING UP

The CONTRACTOR shall, at all times, keep Property on which work is in Progress and the adjacent Property free from accumulations of waste material or rubbish caused by employees or by the work. Upon completion of the construction, the CONTRACTOR shall remove all temporary structures, rubbish, and waste materials resulting from his operations.

PAYMENT

68. PAYMENT FOR CHANGE ORDERS

The OWNER's request for quotations on alterations to the work shall not be considered authorization to proceed with the work expediting, delivery, and installation of all equipment and materials. Within a reasonable period after the CONTRACTOR submits to the OWNER a written request for an extension of time, the ENGINEER will Present his written opinion to the OWNER as to whether an extension of time is justified, and, if so, his recommendation as to the number of days for time extension. The OWNER will make the final decision on all requests for extension of time.

Prior to the issuance of a formal Change Order, nor shall such request justify any delay in existing work. Quotations for alterations to the work shall include substantiating documentation with an itemized breakdown of CONTRACTOR and SUBCONTRACTOR costs, including labor, material, rentals, approved services, overhead, and profit. OWNER may require detailed cost data in order to substantiate the reasonableness of the proposed costs.

Any compensation paid in conjunction with the terms of a Change Order shall comprise total compensation due the CONTRACTOR for the work or alteration defined in the Change Order. By signing the Change Order, the CONTRACTOR acknowledges that the stipulated compensation includes payment for the work or alteration plus all payment for the interruption of schedules, extended overhead, delay, or any other impact claim or ripple effect, and by such signing specifically waives any reservation or claim for additional compensation in respect to the subject Change Order.

At the OWNER's option, payment or credit for any alterations covered by a Change Order shall be determined by one or a combination of the methods set forth in A, B, or C below, as applicable:

A. UNIT PRICES

Those unit Prices stipulated in the Proposal shall be utilized where they are applicable. In the event the Change Order results in a change in the original quantity that is materially and significantly different from the original bid quantity, a new unit Price shall be negotiated upon demand of either party. Unit Prices for new items included in the Change Order shall be negotiated and mutually agreed upon.

B. LUMP SUM

A total lump sum for the work negotiated and mutually acceptable to the CONTRACTOR and the OWNER. Lump sum quotations for modifications to the work shall include substantiating documentation with an itemized breakdown of CONTRACTOR and SUBCONTRACTOR costs, including labor, material, rentals, approved services, overhead, and Profit, all calculated as specified under "C" below.

C. COST REIMBURSEMENT WORK

The term "cost reimbursement" shall be understood to mean that payment for the work will be made on a time and expense basis, that is, on an accounting of the CONTRACTOR's forces, materials, equipment, and other items of cost as required and used to do the work.

If the method of payment cannot be agreed upon Prior to the beginning of the work, and the OWNER directs by written Change Order that the work be done on a cost reimbursement basis, then the CONTRACTOR shall furnish labor, and furnish and install equipment and materials necessary to complete the work in a satisfactory manner and within a reasonable period of time. For the work performed, payment will be made for the documented actual cost of the following:

1. Labor including foremen for those hours they are assigned and participating in the cost reimbursement work (actual payroll cost, including wages, fringe benefits as established by negotiated labor agreements, labor insurance, and labor taxes as established by law). No other fixed labor burdens will be considered, unless approved in writing by the OWNER.
2. Material delivered and used on the designated work, including sales tax, if paid by the CONTRACTOR or his SUBCONTRACTOR.
3. Rental or equivalent rental cost of equipment, including necessary transportation for items having a value in excess of $100. Rental or equivalent rental cost will be allowed for only those days or hours during which the equipment is in actual use. Rental and transportation allowances shall not exceed the current rental rates prevailing in the locality. The rentals allowed for equipment will, in all cases, be understood to cover all fuel, supplies, repairs, and renewals, and no further allowances will be made for those items, unless specific agreement to that effect is made.
4. Additional bond, as required and approved by the OWNER.
5. Additional insurance (other than labor insurance) as required and approved by the OWNER.

In addition to items 1 through 5 above, an added fixed fee for general overhead and Profit shall be negotiated and allowed for the CONTRACTOR (or approved SUBCONTRACTOR) actually executing the Cost Reimbursement work.

An additional fixed fee shall be negotiated and allowed the CONTRACTOR for the administrative handling of portions of the work that are executed by an approved SUBCONTRACTOR. No additional fixed fee will be allowed for the administrative handling of work executed by a SUBCONTRACTOR of a SUBCONTRACTOR, unless by written permission from the OWNER.

The added fixed fees shall be considered to be full compensation, covering the cost of general supervision, overhead, Profit, and any other general expense. The CONTRACTOR's records shall make clear distinction between the direct costs of work paid for on a cost reimbursement basis and the costs of other work. The CONTRACTOR shall furnish the ENGINEER report sheets in duplicate of each day's cost reimbursement work no later than the working day following the performance of said work. The daily report sheets shall itemize the materials used, and shall cover the direct cost of labor and the charges for equipment rental, whether furnished by the CONTRACTOR, SUBCONTRACTOR or other forces. The daily report sheets shall provide names or identifications and classifications of workers, the hourly rate of pay and hours worked, and also the size, type, and identification number of equipment and hours operated.
Material charges shall be substantiated by valid copies of vendors' invoices. Such invoices shall be submitted with the daily report sheets, or, if not available, they shall be submitted with subsequent daily report sheets. Said daily report sheets shall be signed by the CONTRACTOR or his authorized agent.

The OWNER reserves the right to furnish such materials and equipment as he deems expedient and the CONTRACTOR shall have no claim for profit or added fees on the cost of such materials and equipment. To receive partial payments and final payment for cost reimbursement work, the CONTRACTOR shall submit to the ENGINEER, detailed and complete documented

verification of the CONTRACTOR's and any of his SUBCONTRACTORS' actual costs involved in the cost reimbursement work. Such costs shall be submitted within 30 days after said work has been performed.

69. PARTIAL PAYMENTS

A. GENERAL

Nothing in this Article shall be construed to affect the right, hereby reserved, to reject the whole or any part of the aforesaid work, should such work be later found not to comply with the Provisions of the Contract Documents. All estimated quantities of work for which partial payments have been made are subject to review and correction on the final estimate. Payment by the OWNER and acceptance by the CONTRACTOR of partial payments based on periodic estimates of quantities of work performed shall not, in any way, constitute acceptance of the estimated quantities used as a basis for computing the amounts of the partial payments.

B. ESTIMATE

At least 30 days before each Progress payment falls due, as specified in the Supplementary Conditions, the CONTRACTOR shall submit to the ENGINEER a detailed estimate of the amount earned during the Preceding month for the separate portions of the work, and request payment. As used in this Article, the words "amount earned" means the value, on the date of the estimate for partial payment, of the work completed in accordance with the Contract Documents, and the value of approved materials delivered to the Project site suitable stored and Protected Prior to incorporation into the work.

ENGINEER will, within 7 days after receipt of each request for payment, either indicate in writing a recommendation of payment and present the request to OWNER, or return the request to CONTRACTOR indicating in writing ENGINEER's reasons for refusing to recommend payment. In the latter case, CONTRACTOR may, within 7 days, make the necessary corrections and resubmit the request.

ENGINEER may refuse to recommend the whole or any part of any payment if, in his opinion, it would be incorrect to make such representations to OWNER. ENGINEER may also refuse to recommend any such payment, or, because of subsequently discovered evidence or the results of subsequent inspections or tests, nullify any such payment previously recommended to such an extent as may be necessary in ENGINEER's opinion to protect the OWNER from loss because:

1. The work is defective, or completed work has been damaged requiring correction or replacement;

2. Written claims have been made against OWNER or Liens have been filed in connection with the work;

3. The Contract Price has been reduced because of Change Orders;

4. OWNER has been required to correct defective work or complete the work in accordance with Article OWNER'S RIGHT TO DO WORK;

5. Of CONTRACTOR's unsatisfactory Prosecution of the work in accordance with the Contract Documents; or

6. CONTRACTOR's failure to make payment to SUBCONTRACTORS or for labor, materials, or equipment.

C. DEDUCTION FROM ESTIMATE

Unless modified in the Supplementary Conditions, deductions from the estimate will be as described below:

1. The OWNER will deduct from the estimate, and retain as part security, 10 percent of the amount earned for work satisfactorily completed. A deduction and retainage of 10 percent will be made on the estimated amount earned for approved items of material delivered to and properly stored at the jobsite but not incorporated into the work. When the work is 50 percent complete, the OWNER may reduce the retainage to 5 percent of the dollar value of all work satisfactorily completed to date provided the CONTRACTOR is making satisfactory progress and there is no specific cause for a greater retainage. The OWNER may reinstate the retainage up to 10 percent if the OWNER determines, at

his discretion, that the CONTRACTOR is not making satisfactory progress or where there is other specific cause for such withholding.

D. QUALIFICATION FOR PARTIAL PAYMENT FOR MATERIALS DELIVERED

Unless modified in the Supplementary Conditions, qualification for partial payment for materials delivered but not yet incorporated into the work shall be as described below:

1. Materials, as used herein, shall be considered to be those items which are fabricated and manufactured material and equipment. No consideration shall be given to individual purchases of less than $200 for any one item.

2. To receive partial payment for materials delivered to the site, but not incorporated in the work, it shall be necessary for the CONTRACTOR to include a list of such materials on the Partial Payment Request. At his sole discretion, the ENGINEER may approve items for which partial payment is to be made. Partial payment shall be based on the CONTRACTOR's actual cost for the materials as evidenced by invoices from the supplier. Proper storage and Protection shall be provided by the CONTRACTOR, and as approved by the ENGINEER. Final payment shall be made only for materials actually incorporated in the work and, upon acceptance of the work, all materials remaining for which advance payments had been made shall revert to the CONTRACTOR, unless otherwise agreed, and partial payments made for these items shall be deducted from the final payment for the work.

3. CONTRACTOR warrants and guarantees that title to all work, materials, and equipment covered by any Application for Payment, whether incorporated in the Project or not, will pass to OWNER at the time of payment free and clear of all liens, claims, security interests, and encumbrances.
4. If requested by the ENGINEER, the CONTRACTOR shall provide, with subsequent pay requests, invoices receipted by the supplier showing payment in full has been made.

E. PAYMENT

After deducting the retainage and the amount of all previous partial payments made to the CONTRACTOR from the amount earned, the amount due will be made payable to the CONTRACTOR. Recommendations for payment received by the OWNER less than 9 days Prior to the scheduled day for payment will not be Processed or paid until the following month.

70. CLAIMS FOR EXTRA WORK

In any case where the CONTRACTOR deems additional time or compensation will become due him under this Contract for circumstances other than those defined in Article DELAYS AND EXTENSION OF TIME, the CONTRACTOR shall notify the ENGINEER, in writing, of his intention to make claim for such time or compensation before he begins the work on which he bases the claim, in order that such matters may be settled, if possible, or other appropriate action taken. The notice of claim shall be in duplicate, in writing, and shall state the circumstances and the reasons for the claim, but need not state the amount. If such notification is not given or if the ENGINEER is not afforded proper facilities by the CONTRACTOR for keeping strict account of actual cost, then the CONTRACTOR hereby agrees to waive the claim for such additional time or compensation. Such notice by the CONTRACTOR, and fact that the ENGINEER has kept account of the cost as aforesaid, shall not in any way be construed as proving the validity of the claim.

No extension of time will be granted to the CONTRACTOR for delays resulting from extra work that have no measurable impact on the completion of the total work under this Contract. Claims for additional time or compensation shall be made in itemized detail and submitted, in writing, to the OWNER and ENGINEER within 10 days following completion of that portion of the work for which the CONTRACTOR bases his claim. Failure to make the claim for additional compensation in the manner and within the time specified above shall constitute waiver of that claim. In case the claim is found to be just, it shall be allowed and paid for as provided in Article PAYMENT FOR CHANGE ORDERS.

71. RELEASE OF LIENS OR CLAIMS

The CONTRACTOR shall indemnify and hold harmless the OWNER from all claims for labor and materials furnished under this

Contract. Prior to the final payment, the CONTRACTOR shall furnish to the OWNER, as part of his final payment request, a certification that all of the CONTRACTOR's obligations on the project have been satisfied and that all monetary claims and indebtedness have been paid. The CONTRACTOR shall furnish complete and legal effective releases or waivers, satisfactory to the OWNER, of all liens arising out of or filed in connection with the work.

72. FINAL PAYMENT

Upon completion of all the work under this Contract, the CONTRACTOR shall notify the ENGINEER, in writing, that he has completed his part of the Contract and shall request final payment. Upon receipt of such notice the ENGINEER will inspect and, if acceptable, submit to the OWNER his recommendation as to acceptance of the completed work and as to the final estimate of the amount due the CONTRACTOR. Upon approval of this final estimate by the OWNER and compliance by the CONTRACTOR with Provisions in Article **RELEASE OF LIENS OR CLAIMS,** and other Provisions as may be applicable, the OWNER shall pay to the CONTRACTOR all monies due him under the Provisions of these Contract Documents.

73. NO WAIVER OF RIGHTS

Neither the inspection by the OWNER, through the ENGINEER or any of his employees, nor any order by the OWNER for payment of money, nor any payment for, or acceptance of, the whole or any part of the work by the OWNER or ENGINEER, nor any extension of time, nor any possession taken by the OWNER or its employees, shall operate as a waiver of any Provision of this Contract, or any power herein reserved to the OWNER, or any right to damages herein Provided, nor shall any waiver of any breach in this Contract be held to be a waiver of any other or subsequent breach. Acceptance or final payment shall not be final and conclusive with regards to latent defects, fraud, or such gross mistakes as may amount to fraud, or as regards the OWNER's rights under the warranty.

74. ACCEPTANCE OF FINAL PAYMENT CONSTITUTES RELEASE

The acceptance by the CONTRACTOR of the final payment shall release the OWNER and the ENGINEER, as representatives of the OWNER, from all claims and all liability to the CONTRACTOR for all things done or furnished in connection with the work, and every act of the OWNER and others relating to or arising out of the work except claims Previously made in writing and still unsettled. No payment, however, final or otherwise, shall operate to release the CONTRACTOR or his Sureties from obligations under this Contract and the Performance Bond, Payment Bond, and other bonds and warranties, as herein provided.

SUPPLEMENTARY CONDITIONS

The General Conditions are hereby revised as follows:

ARTICLE 9 "ENGINEER"

Delete Article "ENGINEER" in its entirety and substitute the following:

The person or organization identified as such in the Contract Documents. The Term "ENGINEER" means "ARCHITECT" or his authorized representative.

ARTICLE 32. "ASSIGNMENT OF CONTRACT"

A. Assignment of any part or the whole of this Contract shall be subject to review and approval of the City Commission.

ARTICLE 34 "INSURANCE & LIABILITY"

Delete Articles 34A, 34B, 34C, and 34D and substitute the following:

Contractor shall maintain limits no less than those stated below:

CONTRACTOR is to secure, pay for, and file with the City of Key West, prior to commencing any work under the Contract, all certificates for workers' compensation, public liability, and property damage liability insurance, and such other insurance coverages as may be required by specifications and addenda thereto, in at least the following minimum amounts with specification amounts to prevail if greater than minimum amounts indicated. Notwithstanding any other provision of the Contract, the CONTRACTOR shall provide the minimum limits of liability insurance coverage as follows:

Auto Liability	$1,000,000	Combined Single Limit
General Liability	$2,000,000	Aggregate (Per Project)
	$2,000,000	Products Aggregate
	$1,000,000	Any One Occurrence
	$1,000,000	Personal Injury
	$ 300,000	Fire Damage/Legal
Additional Umbrella Liability	$1,000,000	Occurrence / Aggregate

CONTRACTOR shall furnish an original Certificate of Insurance indicating, and such policy providing coverage to, City of Key West named as an additional insured on a PRIMARY and NON CONTRIBUTORY basis utilizing an ISO standard endorsement at least as broad as CG 2010 (11/85) or its equivalent, (combination of CG 20 10 07 04 and CG 20 37 07 04, providing coverage for completed operations, is acceptable) including a waiver of subrogation clause in favor of City of Key West on all policies. CONTRACTOR will maintain the General Liability and Umbrella Liability insurance coverages summarized above with coverage continuing in full force including the additional insured endorsement until at least 3 years beyond completion and delivery of the work contracted herein.

Notwithstanding any other provision of the Contract, the CONTRACTOR shall maintain complete workers' compensation coverage for each and every employee, principal, officer, representative, or agent of the CONTRACTOR who is performing any labor, services, or material under the Contract. Further, CONTRACTOR shall additionally maintain the following minimum limits of coverage:

Bodily Injury Each Accident	$1,000,000
Bodily Injury by Disease Each Employee	$1,000,000
Bodily Injury by Disease Policy Limit	$1,000,000

CONTRACTOR shall provide the City of Key West with a Certificate of Insurance verifying compliance with the workman's compensation coverage as set forth herein and shall provide as often as required by the City of Key West such certification which shall also show the insurance company, policy number, effective and expiration date, and the limits of workman's compensation coverage under each policy.

CONTRACTOR's insurance policies shall be endorsed to give 30 days' written notice to the City of Key West in the event of cancellation or material change, using form CG 02 24, or its equivalent.

Certificates of Insurance submitted to the City of Key West will not be accepted without copies of the endorsements being requested. This includes additional insured endorsements, cancellation/material change notice endorsements, and waivers of subrogation. PLEASE ADVISE YOUR INSURANCE AGENT ACCORDINGLY.

CONTRACTOR will comply with any and all safety regulations required by any agency or regulatory body including but not limited to OSHA. CONTRACTOR will notify City of Key West immediately by telephone at (305) 809-3963 any accident or injury to anyone that occurs on the jobsite and is related to any of the work being performed by the CONTRACTOR.

Add the following Article:

G. SURETY AND INSURER QUALIFICATIONS

All bonds, insurance contracts, and certificates of insurance shall be either executed by or countersigned by a licensed resident agent of the Surety or insurance company, having his place of business in the State of Florida, and in all ways complying with the insurance laws of the State of Florida. Further, the said Surety or Insurance Company shall be duly licensed and qualified to do business in the State of Florida. If requested, Contractor shall Provide Proof of Florida Licensure for all insurance companies. The City of Key West shall be named as Additional Insured on the insurance certificates.

ARTICLE 35 “INDEMNITY”

Delete Article “INDEMNITY” in its entirety and substitute the following:

INDEMNITY

To the fullest extent permitted by law, the CONTRACTOR expressly agrees to indemnify and hold harmless the City of Key West, their officers, directors, agents, and employees (herein called the “indemnitees”) from liabilities, damages, losses and costs, including, but not limited to, reasonable attorney’s fees and court costs, such legal expenses to include costs incurred in establishing the indemnification and other rights agreed to in this Paragraph, to persons or property, to the extent caused by the negligence, recklessness, or intentional wrongful misconduct of the CONTRACTOR, its Subcontractors or persons employed or utilized by them in the performance of the Contract. Claims by indemnitees for indemnification shall be limited to the amount of CONTRACTOR’s insurance or $1 million per occurrence, whichever is greater. The parties acknowledge that the amount of the indemnity required hereunder bears a reasonable commercial relationship to the Contract and it is part of the project specifications or the bid documents, if any.

The indemnification obligations under the Contract shall not be restricted in any way by any limitation on the amount or type of damages, compensation, or benefits payable by or for the CONTRACTOR under workers’ compensation acts, disability benefits acts, or other employee benefits acts, and shall extend to and include any actions brought by or in the name of any employee of the CONTRACTOR or of any third party to whom CONTRACTOR may subcontract a part or all of the Work. This indemnification shall continue beyond the date of completion of the work.

ARTICLE 39 "CODES, ORDINANCES, PERMITS, AND LICENSES"

Add the following:

A. PERMIT FOR WORK WITHIN LOCAL RIGHTS-OF-WAY

The Contractor shall obtain from the City of Key West the necessary permits for work within the rights-of-way. The Contractor shall abide by all regulations and conditions, including maintenance of traffic.

B. NOISE ORDINANCE

City of Key West has a noise ordinance that allows working hours between 8:00 AM to 7:00 PM, Monday through Friday. No work should be performed during weekends or City Holidays, State Holidays and National Holidays. Any construction operations outside these hours and these days will require a variance from the City of Key **West** Commission.

C. "LICENSES"

1. Within 10 days of Notice of Award, the successful Bidder must represent that he holds all applicable, county, and City of Key West licenses and permits required to do business as a contractor with respect to the work described in the Contract Documents.

2. Further, the successful Bidder must, within 10 days of Notice of Award, furnish documentation showing that, as a minimum, he has complied with the provisions of Chapter 18 of the Code of Ordinances of the City of Key West in order to enter into the Agreement contained in the Contract Documents.

3. Specifically, within 10 days after Notice of Award, the successful Bidder must demonstrate that he holds, as a minimum, the following licenses and certificates:

   a.) City of Key West Tax License Receipt;
   b.) A valid Certificate of Competency issued by the Chief Building Official of Key West, Florida
   c.) A valid occupational license issued by the City of Key West, Florida.

E. WORK DURING HOLIDAYS

There shall be no work during City Holidays, State Holidays and National Holidays. Any construction operations during these days shall be approved by the City of Key West.

ARTICLE 40 “SUPERENTENDENCE”

Add the following sub article:

The CONTRACTOR shall keep at the project site, competent supervisory personnel, able to read, write and speak English to effectively communicate with City staff.

ARTICLE 42 "SAFETY"

Add the following sub article:

OCCUPATIONAL SAFETY AND HEALTH

The Contractor shall observe and comply with all applicable local, state, and federal occupational safety and health regulations during the prosecution of work under this Contract. In addition, full compliance by the Contractor with the U.S. Department of Labor's Occupational Safety and Health Standards, as established in Public Law 91-596, will be required under the terms of this Contract.

ARTICLE 43 "PROTECTION OF WORK AND PROPERTY"

Add the following Article:

HISTORIC PRESERVATION

The Contractor shall comply with Florida's Archives and Historic Act (Florida Statutes, Chapter 267) and the regulations of the local historic preservation board as applicable and protect against the potential loss or destruction of

significant historical or archaeological data, sites, and properties in connection with the project.

ARTICLE 57 “OWNERS RIGHT TO TRANSFER EMPLOYMENT”

Add the following Article:

TERMINATION FOR CONVENIENCE AND RIGHT OF SUSPENSION

A. Owner shall have the right to terminate this Contract without cause by written notice of Termination to the Contractor. In the event of such termination for convenience, the Contractor’s recovery against the Owner shall be limited to that portion of the Contract amount earned through the date of termination, together with any retainage withheld and reasonable termination expenses incurred. Contractor shall not be entitled to any other or further recovery against the Owner, including, but not limited to, damages or any anticipated profit on portions of the Work not performed.

B. The Owner shall have the right to suspend all or any portions of the Work upon giving the Contractor prior written notice of such suspension. If all or any portion of the Work is so suspended, the Contractor shall be entitled to reasonable costs, expenses and time extension associated with the suspension.

ARTICLE 60 "LIQUIDATED DAMAGES"

Delete Article "LIQUIDATED DAMAGES" in its entirety and substitute the following:
LIQUIDATED DAMAGES

Should the Contractor fail to complete the work or any part thereof in the time agreed upon in the Contract Documents or within such extra time as may have been allowed for delays by extensions granted as provided in the Contract, the Contractor shall reimburse the Owner for the additional expense and damage for each calendar day, Sundays and legal holidays included, that project outlined in Contract Documents remains uncompleted after the completion date. Liquidated damages shall be assessed. It is agreed that the amount of such additional expense and damage incurred by reason of failure to complete the work is the per diem rate as stipulated in the Proposal. The said amount is hereby agreed upon as a reasonable estimate of the costs which may be accrued by the Owner after the expiration of the time of completion. It is expressly understood and agreed that this amount is not to be considered in the nature of a penalty but as liquidated damages, which have accrued against the Contractor. The Owner shall have the right to deduct such damages from any amount due or that may become due the Contractor or the amount of such damages shall be due and collectible from the Contractor or Surety.

ARTICLE 68 “PAYMENT”

Sub article C. “COST REIMBURSEMENT WORK”

Delete the third & fourth paragraph in its entirety & substitute the following;

In addition to 1 through 5 above, an added fixed fee of 15 percent (%) for general overhead & profit shall be allowed for the CONTRACTOR (or approved SUBCONTRACTOR) actually executing the Cost Reimbursement work.

An additional fixed fee of 5 % will be allowed the CONTRACTOR for the administrative handling of portions of the work that are executed by an approved SUBCONTRACTOR. No additional fixed fee will be allowed for the administrative handling of work executed by the SUBCONTRACTOR of a SUBCONTRACTOR.

ARTICLE 69 "PARTIAL PAYMENTS"

Delete the first paragraph of Sub Article B. "ESTIMATE" and substitute the following:

No more than once each month the Contractor shall submit to the Engineer a detailed estimate of the amount earned during the preceding month for the separate portions of the work and request payment. As used in this Article the words "amount earned" means the value, on the date of the estimate, for partial payment of the work completed in accordance with the Contract Documents and the value of approved materials delivered to the project site suitably stored and protected prior to incorporation into the work. Payment will be made by the Owner to the Contractor within 40 days' receipt of the written recommendation of payment from the Engineer.

Sub Article C. "DEDUCTION FROM ESTIMATE

Delete third sentence in its entirety and substitute add the following;

1. When the work is 90 per cent complete, the OWNER may reduce the retainage to 5 percent of the dollar value of all work satisfactorily completed to date provided the CONTRACTOR is making satisfactory progress and there is no specific cause for greater retainage.

Delete Sub Article E. "PAYMENT" in its entirety and substitute the following:

After deducting the retainage and the amount of all previous partial payments made to the Contractor from the amount earned the amount due will be made payable to the Contractor. Recommendations for payment received by the Owner less than 40 days prior to the scheduled day for payment will not be processed or paid until the following month.

ARTICLE 72 "FINAL PAYMENT"

Delete Article "FINAL PAYMENT" in its entirety and substitute the following:

FINAL PAYMENT

Upon completion of the work the Contractor shall notify the Engineer, in writing, that he has completed it and shall request final payment. The Contractor shall be

responsible for keeping an accurate and detailed record of his actual construction. Upon completion of construction and before final acceptance and payment the Contractor shall furnish the Engineer as-built drawings of his construction. Upon receipt of a request for final payment and the as-built drawings the Engineer will inspect and, if acceptable, submit to the Owner his recommendation as to acceptance of the completed work and as to the final estimate of the amount due the Contractor. Upon approval of this final estimate by the Owner and compliance by the Contractor with provisions in Article RELEASE OF LIENS OR CLAIMS, and other provisions as may be applicable, the Owner shall pay to the Contractor all monies due him under the provisions of these Contract Documents.

ARTICLE 72 "FINAL PAYMENT"

Add the following;

A. Acceptance and Final Payment

Whenever the Contractor has completely performed the work provided for under the Contract and the Engineer has performed a final inspection and made final acceptance and subject to the terms of the Engineer will prepare a final estimate showing the value of the work as soon as the Engineer makes the necessary measurements and computations. The Engineer will correct all prior estimates and payments in the final estimate and payment. The OWNER will pay the estimate, less any sums that the OWNER may have deducted or retained under the provisions of the Contract, as soon as practicable after final acceptance of the work, provided the Contractor has met the requirements of (1) through (7) below.

1 The Contractor has agreed in writing to accept the balance due or refund the overpayment, as determined by the OWNER, as full settlement of his account under the Contract and of all claims in connection therewith, or the Contractor, accepted the balance due or refunded the overpayment, as determined by the OWNER, with the stipulation that his acceptance of such payment or the making of such refund does not constitute any bar, admission, or estoppel, or have any effect as to those payments in dispute or the subject of a pending claim between the Contractor and the OWNER. To receive payment based on a FINAL PAYMENT CERTIIFCATE, The Contractor further agrees, by submitting a FINAL PAYMENT CERTIFICATE that any pending or future arbitration claim or suit is limited to those particulars, including the itemized amounts, defined in the original FINAL PAYMENT CERTIFICATE , and that he will commence with any such arbitration claim or suit within 15 calendar days from and after the time of final PAYMENT of the work and that his failure to file a formal claim within this period constitutes his full acceptance of the Engineer's final estimate and payment. The overpayment refund check from the Contractor, if required, will be considered a part of any Acceptance Letter executed.

2 The Contractor has properly maintained the project, as specified hereinbefore.

3 The Contractor has furnished a sworn affidavit to the effect that the Contractor has paid all bills and no suits are pending (other than those exceptions listed, if any) in connection with work performed under the Contract and that the Contractor has not

offered or made any gift or gratuity to, or made any financial transaction of any nature with, any employee of the OWNER in the performance of the Contract.

4 The surety on the contract bond consents, by completion of their portion of the affidavit and surety release subsequent to the Contractor's completion of his portion, to final payment to the Contractor and agrees that the making of such payment does not relieve the surety of any of its obligations under the bond.

5 The Contractor has furnished all required mill tests and analysis reports to the Engineer.

6 Final payment will not be released until the City receives Certified As-built drawings in Auto Cad & adobe format as well as:

7. As-Built Drawing Standards:

All supplied data collections, as-builts, drawings and files to be compatible with esri ArcGIS 10.2.2 Software. The current computing environment consists of:

- Microsoft SQL Server - Windows 7/Server 2008 - ESRI GIS Platform

Interfaces and Integrations:

The City of Key West uses a number of software applications critical to its core operation and mission. The proposed mobile asset data collection solution will need to interface or integrate with these existing platforms. - Arc Collector-ArcGIS Online - ArcMap 10.2

If there are any questions or concerns on whether your files meet this request. Please contact Matt Willman, GIS Manager, @ 305-809-3721.

PART 4

GENERAL REQUIREMENTS

SECTION 01001
GENERAL REQUIREMENTS

PART 1 - GENERAL

1.1 PROJECT DESCRIPTION

A. The following information though not all-inclusive, is given to assist Contractors in the evaluation of the work required to meet the project objectives.

B. A brief description of the work is stated in the Invitation to Bid. To determine the full scope of the project or of any particular part of the project, coordinate the applicable information in the several parts of these Contract Documents.

1.2 MOBILIZATION AND DEMOBILIZATION

A. Contractor shall be responsible for mobilization and demobilization of labor, materials and equipment. Payment for mobilization and demobilization will be included in the lump sum price indicated in the BID.

B. DAILY REPORTS
   1) The CONTRACTOR shall submit daily reports of construction activities for each site, including non-work days. The report shall include:
      a) Manpower, number of men by craft
      b) Quality Control
      c) Equipment on the Project
      d) Major deliveries
      e) Activities worked with reference to the Work Order items
      f) New problems
      g) Other pertinent information
   2) A similar report shall be submitted for/by each Subcontractor.
   3) The reports shall be submitted to the ENGINEER each month.

1.3 SCHEDULING

A. Plan the work and carry it out with minimum interference to the operation of the existing facilities. Prior to starting the work, confer with the Engineer and Owner's representative to develop an approved work schedule, which will permit the facilities to function as normally as practical. It may be necessary to do certain parts of the work outside normal working hours in order to avoid undesirable conditions. The Contractor shall do this work at such times and at no additional cost to the Owner.

B. SPECIAL EVENTS: Contractor may be asked to stop work during special events. No work will be allowed for intersections (TBD) on days corresponding to the events and schedule listed below. All material and equipment shall be totally off all streets by 5:00 P.M. the day before these dates:

No work on roof shall be allowed to interfere with polling locations open on election days. Monroe County Precincts (update from 2012)

PRECINCT#	ADDRESS		CITY
Prec. #1	Jaycee Clubhouse, 3825 Flagler Avenue.		Key West
Prec. #2	Key West High School Auditorium, 2100 Flagler Ave		Key West
Prec. #3	Key West High School Auditorium, 2100 Flagler Ave.		Key West
Prec. #4	Martin Luther King Community Pool, 300 Catherine St.		Key West
Prec. #5	Old City Hall, 510 Greene Street.		Key West
Prec. #6	St. Mary's Convent, 724 Truman Avenue.		Key West
Prec. #7	Moose Club, 700 Eisenhower Dr.		Key West
Prec. #8	Glad Tiding Tabernacle Assembly of God1209 United St (Georgia St Entrance).		Key West
Prec. #9	Senior Citizens Plaza Auditorium (Rear Entrance), 1400 Kennedy Dr.		Key West
Prec. #10	Church of Jesus Christ of Latter Day Saints, 3424 Northside Dr.		Key West

1.4 COORDINATION

A. Contractors shall cooperate in the coordination of their separate activities in a manner that will provide the least interference with the Owner's operations and other contractors and utility companies working in the area, and in the interfacing and connection of the separate elements of the overall project work.

B. If any difficulty or dispute should arise in the accomplishment of the above, the problem shall be brought immediately to the attention of the Engineer.

C. CONTRACTOR shall notify all residents and proprietors adjacent to construction site of work to be performed, more specifically the notice shall state the day and time construction will begin, the name and phone number of the Contractor's representative responsible for the completion of the proposed improvements. Notice shall also include the Owner's representative for the project

1.5 WORK TO BE PERFORMED BY OTHERS

A. During the construction period for this project, the Owner (either with his own forces or under a separate contract) may be performing work that may require the cooperation of the Contractors in scheduling and coordination to avoid conflicts.

B. If any difficulty or dispute should arise in the accomplishment of the above, the problem shall be brought immediately to the attention of the Engineer.

C. All Contractors working on this site are subject to this requirement for cooperation, and all shall abide by the Engineer's decision in resolving project coordination problems without additional cost to the Owner.

1.6 SITE INVESTIGATION AND REPRESENTATION

A. The Contractor acknowledges satisfaction as to the nature and location of the work, the general and local conditions, particularly those bearing upon availability of transportation, access to the site, disposal, handling and storage of materials, availability of labor, water, electric power, roads, and uncertainties of weather, or similar physical conditions at the site, the conformation and conditions at the site, the character of equipment and facilities needed preliminary to and during the prosecution of the work, and all other matters which can any way affect the work or the cost thereof under this Contract.

B. The Contractor further acknowledges satisfaction as to character, quality, and quantity of surface and subsurface materials to be encountered from his inspection of the site and from reviewing any available records of exploratory work furnished by the Owner or included in these Documents. Failure by the Contractor to become acquainted with the physical conditions of the site and all available information will not relieve the Contractor from responsibility for properly estimating the difficulty or cost of successfully performing the work.

C. The Contractor warrants that as a result of examination and investigation of all the aforesaid data, the contractor can perform the work in a good and workmanlike manner and to the satisfaction of the Owner.

D. The Owner assumes no responsibility for any representations made by any of its officers or agents during or prior to the execution of this Contract, unless (1) such representations are expressly stated in the Contract, and (2) the Contract expressly provides that the responsibility therefore is assumed by the Owner.

1.7 INFORMATION ON SITE CONDITIONS

A. General: Any information obtained by the Engineer regarding site conditions, subsurface information, water level, existing construction of site facilities as applicable, and similar data will be available for inspection at the office of the Engineer upon request. Such information is offered as supplementary information only. Neither the Engineer nor the Owner assumes any responsibility for the completeness or interpretation of such supplementary information.

1.8 DIFFERING SUBSURFACE CONDITIONS

A. The Engineer shall investigate such conditions promptly and following this investigation, the Contractor shall proceed with the work, unless otherwise instructed by the Engineer. If the Engineer finds that such conditions do so materially differ and cause an increase or decrease in the cost of, or in the time required for performing the work, the Engineer will recommend to the Owner the amount of adjustment in cost and time he considers reasonable. The Owner will make the final decision on all Change Orders to the Contract regarding any adjustment in cost or time for completion.

1.9 UTILITIES

A. During excavation the Contractor shall be responsible for determining, at his cost, the locations of all known utilities in the project area.

B. Contractor shall notify utility location service (e.g. Call Sunshine 1-800-432-4770) a minimum for 48 hours prior to work order mobilization. Assigned notification number shall be maintained at the job site at all times and recorded in the daily reports.

1.10 CONTRACTOR'S RESPONSIBILITY FOR UTILITY PROPERTIES AND SERVICE

A. Where the Contractor's operations could cause damage or inconvenience to telephone, television, gas, water, sewer, or irrigation systems, the operations shall be suspended until all arrangements necessary for the protection of these utilities and services have been made by the Contractor.

B. Notify all utility offices, which are affected by the construction operation at least 48 hours in advance. Under no circumstances expose any utility without first obtaining permission from the appropriate agency. Once permission has been granted, locate, expose, and provide temporary support for all existing underground utilities.

C. The Contractor shall be solely and directly responsible to the Owner and operators of such properties for any damage, injury, expense, loss, inconvenience, delay, suits, actions, or claims of any character brought because of any injuries or damage which may result from the construction operations under this Contract

D. Neither the Owner nor its Officers or agents shall be responsible to the Contractor for damages as a result of the Contractor's failure to protect utilities encountered in the work.

E. In the event of interruption to domestic water, sewer, storm drain, or other utility services as a result of accidental breakage due to construction operations, promptly notify the proper authority. Cooperate with said authority in restoration of service as promptly as possible and bear all costs of repair. In no case shall interruption of any water or utility service be allowed to exist outside working hours unless prior approval is granted.

F. In the event the Contractor encounters water service lines that interfere with trenching, he may, by obtaining prior approval of the property owner, Florida Keys Aqueduct Authority (FKAA), or Fire Department as applicable, and the ENGINEER, cut the service dig through, and restore service with similar and equal materials at the Contractor's expense.

G. The Contractor shall replace, at his own expense, all existing utilities or structures removed or damaged during construction, unless otherwise provided for in these Contract Documents or ordered by the Engineer.

1.11 TEMPORARY WATER

A. The Contractor shall make his own arrangements to obtain suitable water for any need and shall pay all costs.

1.12 TEMPORARY ELECTRIC POWER

A. The Contractor shall make his own arrangements to obtain and pay for electrical power used until final acceptance by the Owner.

1.13 SAFETY REQUIREMENTS FOR TEMPORARY ELECTRIC POWER

A. Temporary electric power installation shall meet the construction Safety requirements of OSHA, State, and other governing agencies.

1.14 SANITARY FACILITIES

A. The Contractor shall provide and maintain sanitary facilities for his employees and his subcontractor's employees that will comply with the regulations of the local and State Departments of Health and as directed by the Owner.

1.15 STORAGE OF MATERIALS

A. Materials shall be so stored as to ensure the preservation of their quality and fitness for the work. When considered necessary, they shall be placed on wooden platforms or other clean hard surfaces and not on the ground. Stored materials shall be located so as to facilitate prompt inspection. Stored materials on city property must safe and secured from the general public and if necessary they must be fitted with lights at night. Private property shall not be used for storage purposes without the written permission of the owner or lessee. Materials shall not be stored where access to any structure, plot, or road is blocked. Location of stored materials approved by the ENGINEER or his designee.

B. Delicate instruments and materials subject to vandalism shall be placed under lock cover and, if necessary, provided with temperature control as recommended by the manufacturer.

1.16 CONSTRUCTION SAFETY PROGRAM

A. The Contractor shall develop and maintain for the duration of this Contract, a safety program that will effectively incorporate and implement all required safety provisions. The Contractor shall appoint an employee who is qualified and authorized to supervise and enforce compliance with the safety program.

B. The duty of the Engineer to conduct construction review of the Contractor's performance is not intended to include a review or approval of the adequacy of the Contractor's safety supervisor, the safety program or any safety measures taken in, on, or near the construction site.

C. The Contractor shall do all work necessary to protect the general public from hazards, including, but not limited to, surface irregularities, or unramped grade changes on pedestrian walkways and docks. Barricades, lights, and proper signs shall be furnished in sufficient amount to safeguard the public and the work.

D. The performance of all work shall be in accordance with the applicable governing safety authorities.

1.17 ACCIDENT REPORTS

A. If death or serious injuries or serious damages are caused; the Contractor must promptly report by telephone or messenger to the Engineer. In addition, the Contractor must promptly report in writing to the Engineer all accidents whatsoever arising out of or in connection with, the performance of the work whether on, or adjacent, to the site, giving full details and statements of witnesses.

B. If a claim is made against the Contractor or any subcontractor on account of any accident, the Contractor shall promptly report the facts in writing to the Engineer, giving full details of the claim.

1.18 FIRE PREVENTION AND PROTECTION

A. The Contractor shall perform all work in a fire-safe manner and shall supply and maintain on the site adequate fire-fighting equipment capable of extinguishing incipient fires. The Contractor shall comply with applicable federal, state, and local fire-prevention regulations. Where these regulations do not apply, applicable parts of the National Fire Prevention Standard for Safeguarding Building Construction Operations (NFPA No. 241) shall be followed.

1.19 HURRICANE PREPAREDNESS PLAN

A. Within 30 days of the date of Notice to Proceed, the CONTRACTOR shall submit to the ENGINEER and City Representative a Hurricane Preparedness Plan. The plan should outline the necessary measures which the CONTRACTOR proposes to perform at no additional cost to the OWNER in case of a hurricane warning.

B. In the event of inclement weather, or whenever Owners Representative shall direct, CONTRACTOR will, and will cause Subcontractors to protect carefully the Work and materials against damage or injury from the weather. If, in the opinion of Owner's Representative, any portion of Work or materials shall have been damaged or injured by reason of failure on the part of CONTRACTOR or any Subcontractors to so protect the Work, such Work and materials shall be removed and replaced at the expense of the CONTRACTOR.

1.20 SITE RESTORATION AND CLEANUP:

A. At all times during the work keep the premises clean and orderly and upon completion of daily work repair all damage caused by equipment and leave the project free of rubbish or excess materials of any kind.

B. Stockpile excavated materials in a manner that will cause the least damage to adjacent lawns, grassed areas, gardens, shrubbery, or fences regardless of whether these are on private property, or State, County, or City rights-of-way. Remove all excavated materials from grassed and planted areas, and leave these surfaces in a condition equivalent to their original condition.

1.21 FINISHING OF SITE, BORROW, AND STORAGE AREAS

A. Upon completion of the project, all areas used by the Contractor shall be properly cleared of all temporary structures, rubbish and waste materials and properly graded to drain and blend in with the abutting property. Areas used for the deposit of waste materials shall be finished to properly drain and blend in with the surrounding terrain.

1.22 AREA CLEANUP DURING CONSTRUCTION

A. Thoroughly clean all spilled dirt, gravel, sand or other foreign materials caused by the construction operations from all streets and roads, grass, pathways, docks or concrete walkways and from adjacent areas at the conclusion of each day's operation. Truck or equipment wash down is not to be performed on City Property.

1.23 PREVENTION

A. Applicable environmental regulations shall be strictly adhered to.

1.24 SUBMITTALS

A. See Submittals section 1.4 in the Summary of Work

1.25 PAYMENT

A. The cost of the work in this section is considered incidental to the contract.

END OF SECTION

SUMMARY OF WORK

PART 1 - SUMMARY OF WORK

1.1 DESCRIPTION

A. Work Included: The furnishing of all materials, equipment and labor for the construction of MLK COMMUNITY CENTER ROOF REPLACEMENT IS72011601 and all necessary appurtenances, record drawings, surveys, and incidental work to provide a complete and serviceable project identified as:

IS72011601 / MLK COMMUNITY CENTER ROOF REPLACEMENT

Bid Scope of Work:

Lump Sum Base Bid to Include:

1. Mobilization and Demobilization
2. Removing &disposing of existing roofing membrane, metal coping, leader heads, and downspouts down to ground level
3. Installation of new metal coping at parapet and new roof
4. Enlarging the existing stainless steel liners and scuppers (4 locations)
5. Installing (2) two new stainless steel lined scuppers
6. See drawing package for complete scope of work

B. Related requirements in other parts of the Contract Documents: Include but not limited to:

PART 3: CONDITIONS OF THE CONTRACT

PART 5: STRUCTURAL EVALUATION REPORT AND SPECIFICATIONS & DRAWINGS

C. Contractor's Duties:

1. In addition to provisions stipulated in other portions of the Contract Documents, the Contractor shall:

   a. Secure permits as necessary for proper execution and completion of the work.

   b. Notify (in writing) all residents and proprietors adjacent to construction site of work to be performed, more specifically the notice shall state the day and time construction will begin, hours of work, the name and phone number of the Contractor’s Superintendent and an end date for the project.

D. The Contractor shall be totally responsible for all required permits and payment of associated fees. Contractor shall ensure that construction complies with all applicable local, state, and federal codes.

E. Provide an experienced, qualified, and competent Superintendent able to read, write and speak English to oversee the work and perform quality assurance inspections. Prior to starting construction, the proposed Superintendent's qualifications shall be submitted in writing to the City for approval. The approved Superintendent shall be expected to remain for the duration of the Project, unless the City or Engineer deem him/her inadequate and requests his/her removal or the Contractor cannot continue his services to the Project for a reason or reasons that shall be communicated in writing to the City.

F. A replacement Superintendent shall be required to follow the same approval process as required for the original. The Superintendent shall provide to the City Inspector Construction Reports for each day of construction, the reports shall be in English, legible, and signed. Contractor shall provide PDF copies monthly. Reports shall include quantity control checks done daily

G. It shall be the Contractor's responsibility to request approval for entrance to the site for work on Saturdays, Sundays, holiday, and weekday hours other than 7:00 AM until 7:00 PM. No construction can commence before 8:00 AM on weekdays.

H. The Contractors is responsible for all costs relating to the removal & disposal of the existing roof membrane including all items associated with the removal, disposal and replacement of the roof. The Contractor must dispose of all materials in an environmentally responsible manner.

I. The Contractor shall provide material safety data sheets (2 copies) for chemicals, paints, coatings and materials used on-site prior to initiation of work.

1.2 CONTRACTOR'S USE OF PREMISES

A. Work shall be scheduled as to not interfere with on-going area activities.

B. Coordinate use of premises and requirements for security under direction of City.

C. This is a smoke free construction zone. **NO SMOKING PERMITED WITHIN CONSTRUCTION ZONE.**

D. Assume full responsibility for the protection and safekeeping of products, under this Contract, stored on the site.

E. Obtain and pay for the use of additional storage or work areas needed for operation.

F. Contractor shall provide drinking water and toilet facilities for construction personnel; The City will not provide.

1.3 MAINTENANCE OF EXISTING UTILITIES OPERATION

A. Provide at least three weeks' notice prior to interruption of utility services for temporary or permanent connections.

B. Keep interruption of utility services, and utility outages during disconnection, moving, and reconnection to a minimum.

C. Keys Energy shall be notified two weeks in advance in writing by the contractor for any KEYS support equipment required by the Contractor during any excavation. (e.g., Power poles next to excavations requiring support, etc.) No additional payment will be paid for this coordination.

1.4 SUBMITTALS:

Roofing System: All roofing assemblies require shop drawing submittals. The submittal shall include all components of the assembly including base sheets (if any), insulation if integral to the assembly such as tapered insulation to achieve roof slopes, cover board, membranes and attachment, including edge conditions. The submittal shall include N.O.A. or F.P.A**.** test data for the entire assembly, as a unit, or for each component used, including anchorage / attachment to its supporting substrate on down to the structural deck.
Documentation that the project specific roofing assembly meets design wind loading is required. This can be accomplished by submittal of N.O.A. test data or by signed and seal certification by a Florida Registered Engineer. Provide manufacture's requirements and installation instructions for review.

Submittals

A. Insulation:
   a. Shop Drawings (layout)
   b. Product Data
   c. Test Reports, N.O.A.'s
B. Coverboard:
   a. Product Data
   b. Test Reports
C. Membrane System:
   a. Shop Drawings
   b. Product Data
   c. Test Reports, N.O.A.'s
   d. Samples
D. Flashing + Trim:
   a. Shop Drawings (profiles)
   b. Product Data
   c. Test Reports, N.O.A.'s
E. Sealants:
   a. Product Data
   b. Test Reports
F. Roof Specialties:
   a. Shop Drawings
   b. Product Data
   c. Test Reports, N.O.A.'s
G. Warranty Information
   a. A copy of the manufacturer's warranty will be required before final acceptance.

H. **ADD/ALT**

1. **Solar Heating System:** Radiant energy (solar) pool water heating system
   Submittals: Shop drawing showing code compliance and product data. Contractor is required to have final system meeting all code requirements. Provide shop drawings by a Florida Registered Engineer, signed and sealed.

2. **Liquid applied waterproofing system:** New SealoFlex or equal, liquid applied, fabric reinforced, 3 coat waterproofing system over existing concrete awning at building entrance.

3. **Lightning Protection System: Lightning protection system attached to parapet wall in compliance with NFPA 780.**
   Submittals: Shop drawing showing code compliance and product data. Contractor is required to have final system meeting all code requirements. Provide shop drawings by a Florida Registered Engineer, signed and sealed.

END OF SECTION

PART 5

STRUCTURAL EVALUATION REPORT & SPECIFICATIONS AND DRAWINGS

ARTIBUS DESIGN
ENGINEERING AND PLANNING

Structural Evaluation Report

MLK Community Pool & Community Center Roof Deck

Property Address:
300 Catherine St,
Key West, FL 33040

AD Job#: 1605-10

Artibus Design
August 2016

SERGE MASHTAKOV
LICENSE
No. 71480
STATE OF FLORIDA
PROFESSIONAL ENGINEER

Serge Mashtakov, PE, FL License No. 71480

AUG 22 2016

Date

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040

(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

May 10, 2016

Attn: Mr. William P. Horn, PA
915 Eaton St,
Key West, FL 33040

Roof Deck Evaluation Report

Structure located at: 300 Catherine St, Key West, FL 33040

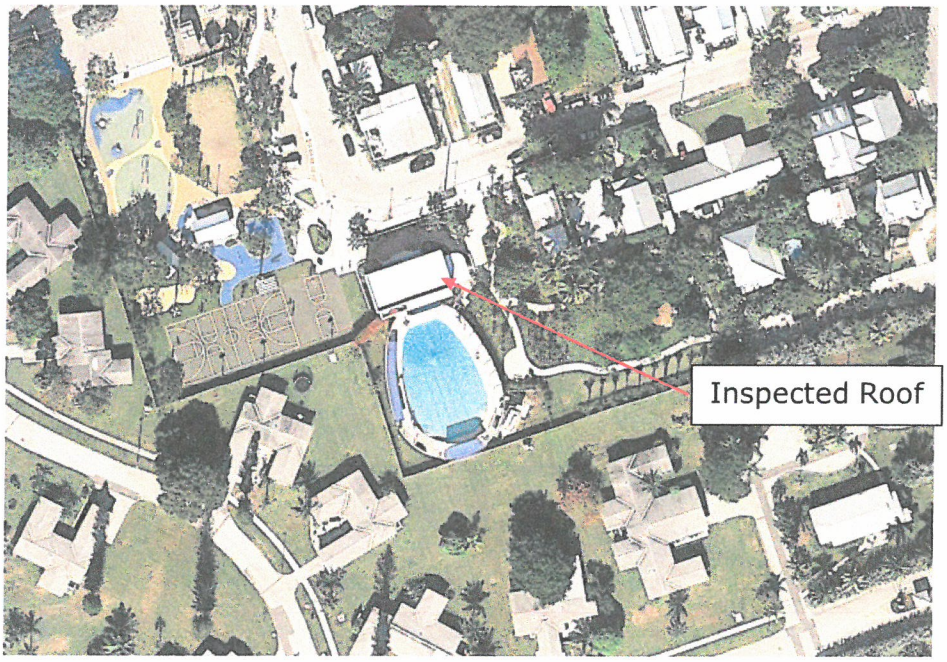

Figure 1. Site Plan Diagram

Date of Construction: 1957 (MCPAFL.ORG)

Type of Construction:
Ground level two story CMU structure with flat roof and parapet. Ground floor - slab on grade, second floor and roof deck - double tee, precast, pre-stressed concrete slabs.

Introduction
The existing roof is experiencing significant leaks and water intrusion into interior. Owner is expressing interest of using roof deck surface for solar water heating needs or solar PV array.

The intent of the evaluation is to provide a professional opinion of the overall structural adequacy and feasibility of additional loads from proposed systems.

This report is based on the information gathered during the site inspection by Serge Mashtakov P.E. On April 06th, 2016.

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040
(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

Figure 2. Front Elevation View

Inspection Procedure

Structure was visually inspected from interior and exterior, roof slab was evaluated in several locations including water intrusion places. Only exposed elements were inspected, subgrade conditions and any covered elements were not inspected.

Background and Findings

The evaluated roof slab consists of a series precast, pre-stressed elements 48" wide and 14" deep and "Double Tee" shape. Approximate clear span of the roof deck slab is 28'-4". It appears that there is no cast-in-place topping on the slab and roofing membrane is directly adhered to the precast member.

According to Precast/Prestressed Concrete Institute (PCI) Journal Article *"The legacy and future of an American icon: The precast, prestressed concrete double tee"* July-August 2015 *"no prestressed concrete double tee was produced in Florida until 1953"*. Which places the slab in the early era of the engineering and use for this particular style of slab. Actual Precast/Prestressed Concrete Institute is a current authority in the industry and it was founded in 1954 in Tampa, Florida.

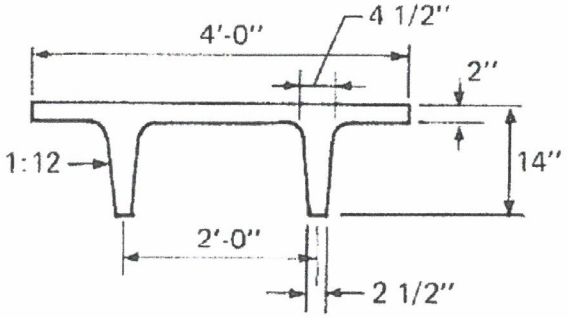

Figure 3. Typical Double Tee Profile

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040
(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

Typical double tee section view shown on Figure 3 reflects a standardized section adopted later and is sourced from PCI Design Handbook 1st Edition dated 1971. According to the previously referenced article first published double-tee load tables where indeed 1st Edition (1971) which is much later date from the current slab.

This explains dimensional variations between the typical profile and available section. The existing slab ribs are slightly wider +/- 3-1/2" on the bottom and +/- 5-1/2" at slab. The available section can be identified as a predecessor of typical section 4DT14. Such sections have been discontinued from the load tables (assume manufacturing) already in the 2nd edition of the PCI Design Handbook published on 1978.

It is evident that the original designers were utilizing latest and leading technologies of the time.

The available load tables for 4DT14 style slabs with a similar span and profile the available safe superimposed live loads vary from 29 psf to 98 psf depending on the number and arrangement of the reinforcing strand. Due to the fact that the slab is pre dating the earliest published load tables the lowest range will be conservative to assume.

Figure 4. Overall View of the Slab

The condition of the roof slab precast elements is good. No concrete spalling was evident along strands nor in the 2" top slab. The system used pre-tensioned strands located in the rib and small diameter wire mesh in the top slab. Significant benefit of the pre-stressed concrete is that initial shrinkage cracks which are typically occur in concrete elements are closed after the strand release due to compression transferred from the tendons. This effect provides prolonged durability and longevity for the system (currently at 40+ year of useful life).

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040

(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

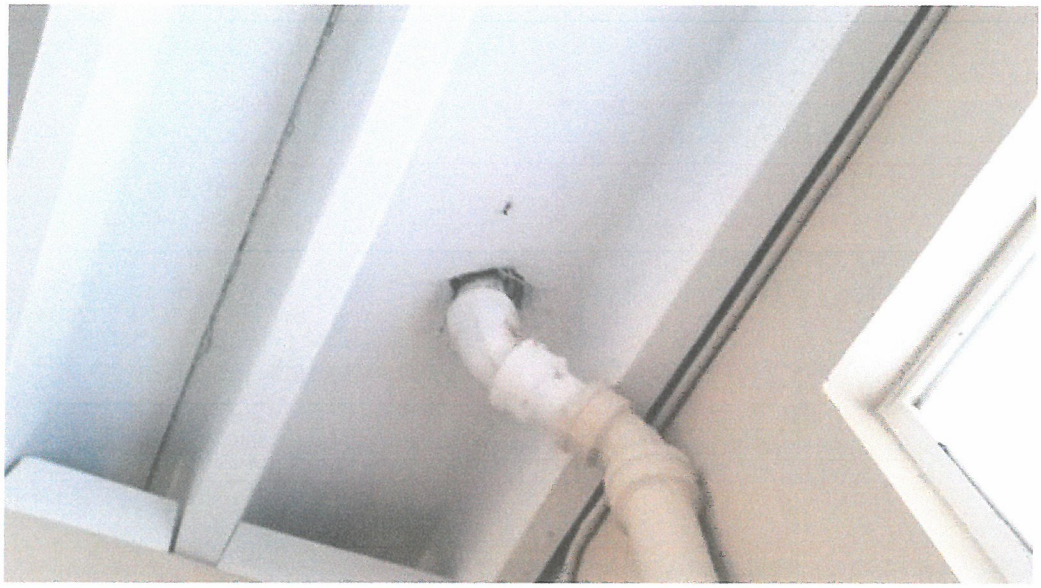

Figure 5. Piping penetration through the slab.

Above shown penetration in the top slab with exposed wire mesh reinforcement shows no signs of adverse impact on the slab system.

Figure 6. Signs of water leaks in the storage area.

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040

(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

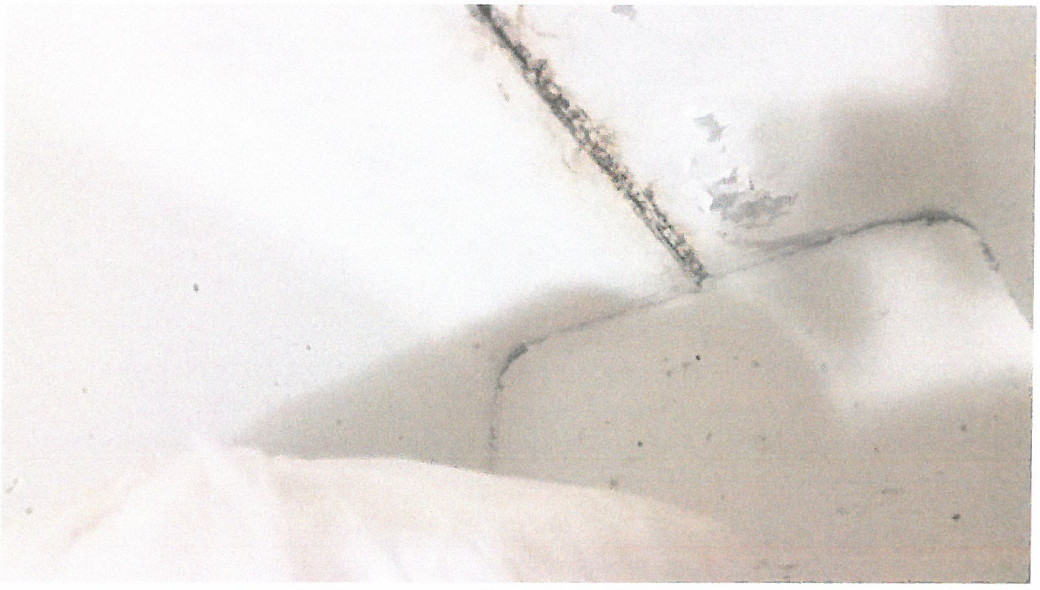

Figure 7. Signs of water leaks in the storage area. (Close-up)

Even in the locations of the prolonged roofing leaks and water intrusion no signs of structural damage to the slab system components were discovered during the inspection.

Figure 8. Roof surface with stains from algae grows in standing water.

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040

(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

Roofing surface is installed directly to the precast slab surface and does not provide any slope towards the scuppers. Scuppers are undersized and prone to plugging with debris. No secondary scuppers (overflows) are available. Roofing membrane is aged and allows rain water into the building interior.

Figure 9. Right Side elevation. Undersized scuppers and damaged downspout on right side.

Cracks were discovered in several locations of the parapet wall, more prominent in the corners.

Figure 10. Cracks in CMU at the left back side.

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040

(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

Figure 11 and 12. Cracks in CMU parapet wall.

The consistent spalling damage across the perimeter of parapet wall indicates water intrusion through gaps in wall coping.

During the site inspection more concrete spalling was discovered in the building elements downstairs, which are not part of this inspection and report. Concrete damage is affecting important bearing structural components (beams and columns) that support floors upstairs and will require repairs in near future.

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040

(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

Figure 13. Concrete spalling along the cast-in-place concrete beams. Grade level interior spaces.

Figure 14. Concrete spalling of columns. Grade level interior spaces.

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040

(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

Conclusions and Recommendations

In my professional opinion the existing slab is in good condition and is capable of caring light foam tapered insulation, light roofing membrane (total up to 10 psf of dead load) and additional live loads from the solar equipment and maintenance personal (total up to 30 psf). Typical PV Solar array panels and mounting hardware loads are in the range 3-4 psf. Solar water heating systems range 4-8 psf filled.

There shall be **no** water storage tanks or large collectors installed on the roof deck. Any collector piping shall be located along parapet walls and preferably attached to walls.

Roofing membrane shall be replaced and installed over tapered insulation which provides sufficient slope for efficient roof runoff. Scuppers shall be replaced with current code compliant size and number and overflow scuppers shall be provided. All downspouts shall be repaired to prevent further water damage to the masonry.

Concrete spalling in the parapet masonry and rake beam shall be repaired per engineered details.

Wall coping shall be replaced with current code compliant system, sloped towards roof interior and with watertight joints.

Sincerely,
Artibus Design LLC
Serge Mashtakov, P.E.
President

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040

(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

DOUBLE TEE

TYPE "A" LOAD TABLE

4DT 14

Table of safe superimposed live load (psf) — Normal Weight Concrete — No Topping — 4'-0" x 14" Double Tee

Strand Pattern		Span, ft 20	22	24	26	28	30	32	34	36	38	40	42	44	46	48	50
27-S		94*	71*	54*	40*	29*											
47-S					90*	79*	64*	52*	41*	32*	25*						
67-S						96*	80*	66*	54*	44*	35*						
47-D1							97*	80*	66*	55*	45*	37*	30*	24*			
67-D1									108*	92*	79*	67*	57*	49*	41*	35*	28
87-D1																31	24
Dead Load	f_t	167	190	228	265	307	356	402	454	509	567	626	692	760	831	905	982
	f_b	−282	−475	−565	−663	−769	−880	−1005	−1135	−1272	−1418	−1571	−1732	−1901	−2077	−2262	−2455
	a	0.035	0.045	0.136	0.188	0.272	0.335	0.431	0.549	0.695	0.894	1.061	1.278	1.529	1.830	2.190	2.587
100 plf Live Load	f_t	83	101	120	141	164	189	214	242	271	302	335	369	405	443	482	523
	f_b	−209	−253	−301	−354	−410	−471	−536	−605	−678	−756	−837	−923	−1013	−1103	−1206	−1309
	a	0.022	0.043	0.061	0.001	0.110	0.148	0.192	0.245	0.305	0.382	0.469	0.570	0.677	0.821	0.973	1.145

*Capacity governed by ultimate strength. Values below heavy line require camber during fabrication. f_c = 6000 psi, f_{pu} = 270,000 psi

Notation

f_t = top fiber stress, psi (after assumed 22% loss)
f_b = bottom fiber stress, psi (after assumed 22% loss)
a = center deflection, in.
0.001 l^2 α = initial center camber, in. (after assumed 10% loss)
l = span (ft)
M_u = ult. moment capacity, in.-kips

Strand Pattern	Eccentricity in. end	Eccentricity in. ctr	Prestress alone end f_t	end f_b	center f_t	center f_b	α	M_u
27-S	6.00	6.00	−26	502	−96	500	0.412	944
47-S	5.00	5.00	−36	1563	−93	1583	0.667	946
67-S	3.33	3.33	31	1752	91	1792	0.887	1027
47-D1	5.00	7.78	−56	1565	−380	2223	0.941	1245
67-D1	3.33	7.56	91	1752	−510	3256	1.268	1732
87-D1	2.00	7.34	375	1792	−630	4230	1.528	2147

Strand Pattern Designation

108 D1
- No. of strand (10)
- S = straight, D = depressed
- No. of depression points
- Diameter of strand in 16ths



Section Properties

A	=	189 in.^{2}
I	=	2864 in.^{4}
y_b	=	10.00 in.
y_t	=	4.00 in.
Z_b	=	286 in.^{3}
Z_t	=	716 in.^{3}
wt	=	188 plf
		47 psf

Normal Weight Concrete
No Topping
4'-0" x 14" Double Tee

4DT 14

PC Design Aids

3706 N. ROOSEVELT BLVD,
SUITE I-208
KEY WEST, FL 33040
(305) 304-3512
INFO@ARTIBUSDESIGN.COM
WWW.ARTIBUSDESIGN.COM

DR. MARTIN LUTHER KING JR. MEMORIAL COMMUNITY CENTER - ROOF RENOVATION

AREA OF WORK

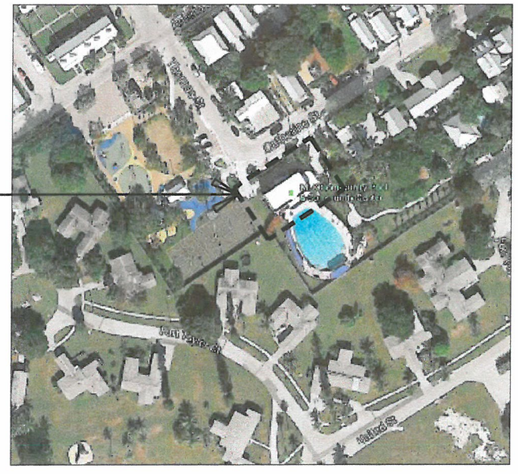

AREA OF WORK

KEY WEST CITY COMMISSIONERS

MAYOR CRAIG CATES
COMMISSIONER JIMMY WEEKLEY, DISTRICT I
COMMISSIONER SAMUEL KAUFMAN, DISTRICT II
COMMISSIONER BILLY WARDLOW, DISTRICT III
COMMISSIONER RICHARD PAYNE, DISTRICT IV
COMMISSIONER MARGARET ROMERO, DISTRICT V
COMMISSIONER CLAYTON LOPEZ, DISTRICT VI
CITY MANAGER JAMES K. SCHOLL

INDEX OF SHEETS

PAGE	DESCRIPTION
A-0	COVER SHEET
A-1	PROPOSED ROOF PLAN
A-2	PROPOSED ELEVATIONS
A-3	SPECIFICATIONS
EX-1	EXISTING ROOF PLAN
EX-2	EXISTING ELEVATIONS
S-1	STRUCTURAL NOTES
S-2	STRUCTURAL PLANS AND DETAILS
P-1	PLUMBING NOTES, PLAN, & DETAILS

SCOPE OF WORK

THE BUILDING SHALL BE OCCUPIED AND OPERATIONAL THROUGHOUT THE COURSE OF THE WORK.

ROOF
SHALL CONSIST OF THE REMOVAL OF EXISTING ROOF MEMBRANE, PARAPET METAL COPING, AND GUTTER SYSTEM. NEW WORK TO INCLUDE INSTALLATION OF SLOPED RIGID INSULATION, NEW SINGLE PLY ROOF SYSTEM OVER EXISTING CONCRETE STRUCTURE, AND NEW PARAPET COPING.

SOLAR ARRAY
SHALL CONSIST OF NEW SOLAR PANELS ON METAL STANDS ATTACHED TO EXISTING CONCRETE ROOF STRUCTURE.

GUTTER
SHALL CONSIST OF THE REMOVAL OF THE EXISTING DOWNSPOUTS AND LEADER HEADS. EXISTING SCUPPERS TO BE EXPANDED TO ACCOMMODATE ROOF WATER. TWO NEW STAINLESS STEEL LINED SCUPPERS.

BID SCOPE OF WORK
LUMP SUM BASE BID TO INCLUDE
1. MOBILIZATION AND DEMOBILIZATION
2. REMOVING EXISTING ROOFING MEMBRANE, METAL COPING, LEADER HEADS, AND DOWNSPOUTS
3. INSTALLING NEW METAL COPING AT PARAPET AND NEW ROOF
4. ENLARGING THE EXISTING STAINLESS STEEL LINERS AND SCUPPERS (4 LOCATIONS)
5. INSTALLING (2)TWO NEW STAINLESS STEEL LINED SCUPPERS
6. SEE DRAWINGS FOR COMPLETE SCOPE OF WORK

ALTERNATE 1
RADIANT ENERGY (SOLAR) POOL WATER HEATING SYSTEM

DESIGN CRITERIA

THE FLORIDA BUILDING CODE 2014 EDITION, AS AMENDED BY GOVERNING LOCAL ORDINANCES AND REQUIREMENTS OF THE STATE OF FLORIDA 'COASTAL ZONE PROTECTION ACT', TOGETHER WITH APPLICABLE REQUIREMENTS OF GOVERNING PUBLIC AGENCIES AND THE FOLLOWING LISTED CODES SHALL APPLY TO THIS PROJECT
NATIONAL ELECTRIC CODE, 2014 EDITION
FLORIDA PLUMBING CODE, 2014 EDITION
WIND LOADING SHALL BE BASED ON ASCE 7-10 150 MPH WIND LOADING.
NOTE ANY REFERENCE TO WIND LOADING FOUND IN THE DRAWINGS OR SPECIFICATIONS WHICH DIFFERS FROM THE ABOVE SHALL BE SUPERCEDED BY THIS STATEMENT.

SITE DATA

SITE AREA: 7,476.5 S.F.
LAND USE: HHDR
FLOOD ZONE: AE +7.0'

SETBACKS:
FRONT SETBACK: REQUIRED = 10'-0" PROPOSED = EXISTING TO REMAIN
SIDE SETBACK: REQUIRED = 5'-0" PROPOSED = EXISTING TO REMAIN
REAR SETBACK: REQUIRED = 20'-0" PROPOSED = EXISTING TO REMAIN

BUILDING COVERAGE AREA: REQUIRED: 50% MAX PROPOSED: EXISTING TO REMAIN
IMPERVIOUS AREA: REQUIRED: 60% MAX. PROPOSED: EXISTING TO REMAIN
LANDSCAPE AREA: PROPOSED: EXISTING TO REMAIN
OPEN SPACE AREA: PROPOSED: EXISTING TO REMAIN

WILLIAM P. HORN
ARCHITECT, P.A.

915 EATON ST.
KEY WEST,
FLORIDA
33040

TEL (305) 296-8302
FAX (305) 296-1033

LICENSE NO.
AA 0003040

MLK ROOF
304 CATHERINE ST.
KEY WEST, FL

SEAL

8-23-16

THESE DRAWINGS MAY NOT BE REPRODUCED WITHOUT WRITTEN AUTHORIZATION BY WILLIAM P. HORN

DATE
06-29-2016 50% SET
07-29-2016 HARC
08-11-2016 100% SET
08-17-2016 BID SET

REVISIONS

DRAWN BY
JW

PROJECT NUMBER
1601

A-0

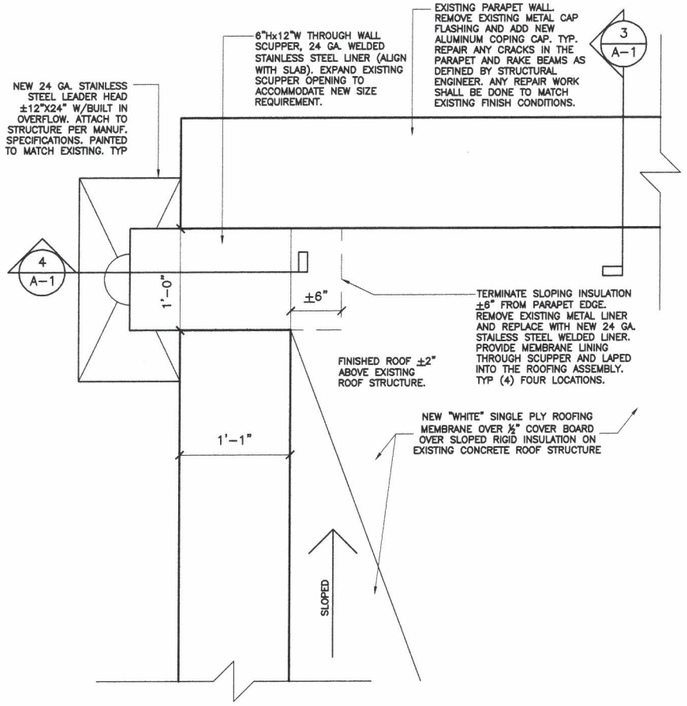

ENLARGED PLAN

2 A-1 SCALE: 1 1/2"=1'-0"

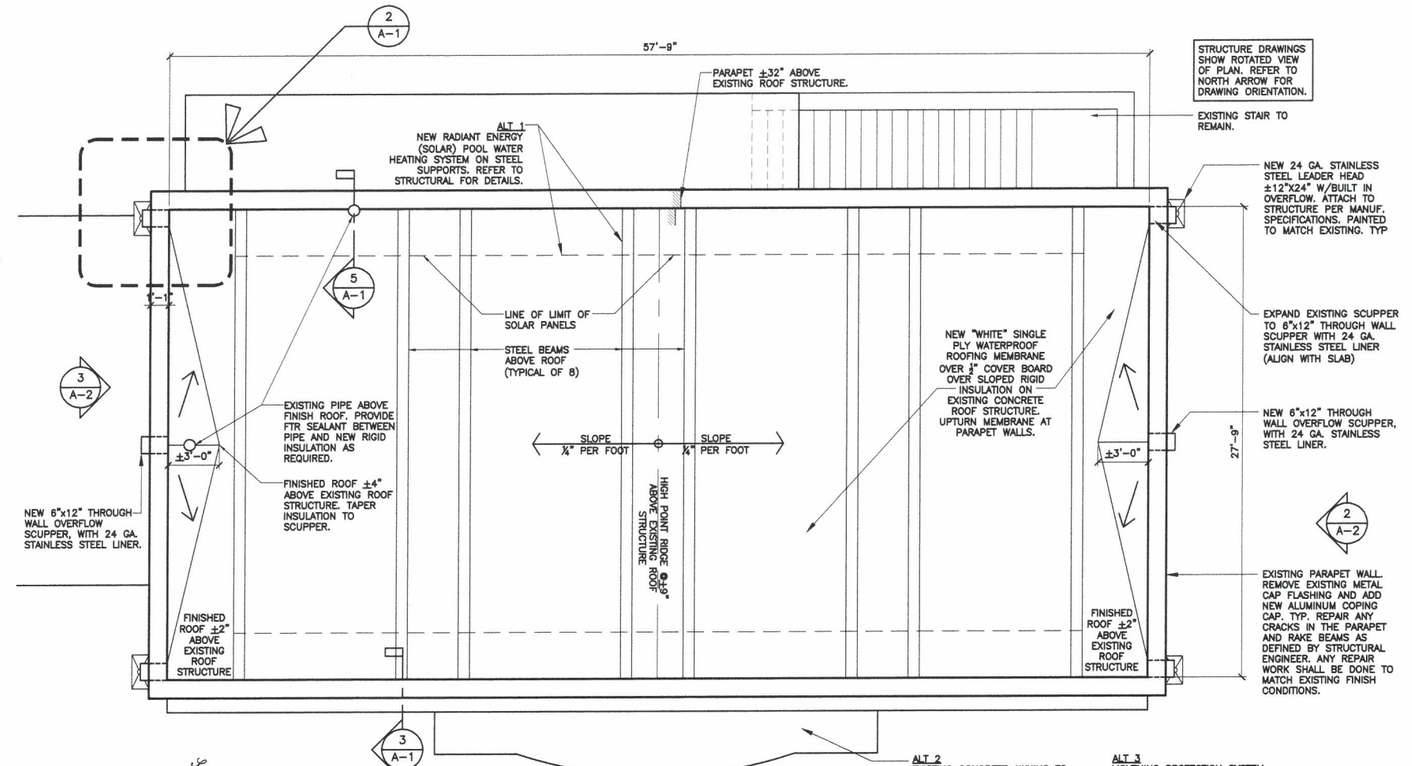

PROPOSED ROOF PLAN

SCALE: 1/4"=1'-0"

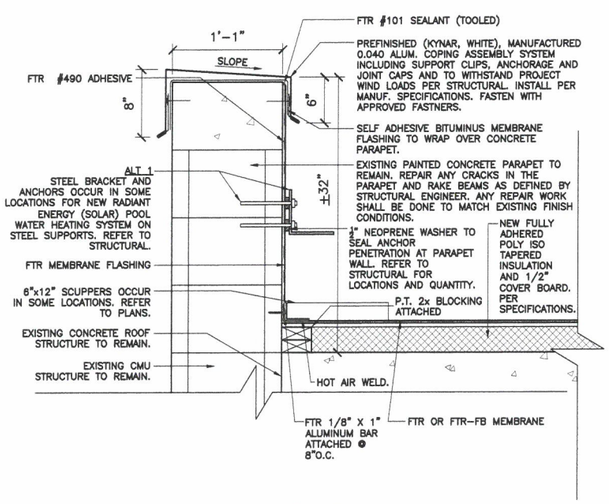

PARAPET SECTION DETAIL

3 A-1 SCALE: 1 1/2"=1'-0"

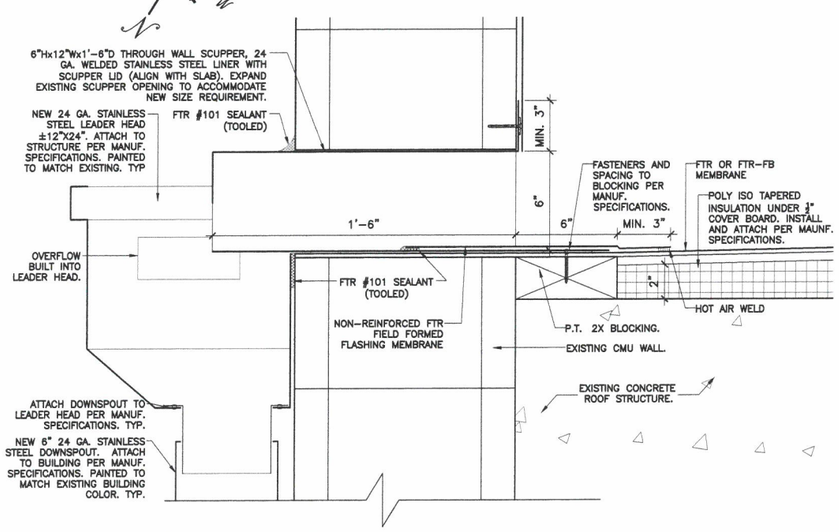

SCUPPER DETAIL

4 A-1 SCALE: 3"=1'-0"

SINGLE PLY FULLY ADHERED MEMBRANE ROOFING ASSEMBLY – BASIS OF DESIGN OR EQUAL

- 60 MIL FIBERTITE BRITE WITH KYNAR (WHITE) FULLY ADHERED ROOFING ASSEMBLY WITH FTR-490 WATER BASED ADHESIVE AT 0.83 GAL/SQ. OVER ½" DENS DECK PRIME COVER BOARD FULLY ADHERED TO TAPERED POLYIOSCYANURATE INSULATION FULLY ADHERED TO CONCRETE DECK.
- ASSEMBLY SHALL BE FULLY ADHERED PER THE MANUFACTURES RECOMMENDATIONS AND SHALL INCORPORATE ASSEMBLY PREFINISHED COMPATIBLE FLASHING PRODUCTS.
- REFERENCE NOA FOR ROOF ASSEMBLY: 15-0421.08
- PROVIDE A FULL SHOP DRAWING SUBMITTAL INCLUDING N.O.A. COMPLIANCE WITH PROJECT WIND LOADS AND ALL ACCESSORIES AND DETAILS REQUIRED FOR A COMPLETE WATERTIGHT INSTALLATION.
- REFER TO STRUCTURAL FOR DESIGN PRESSURES.

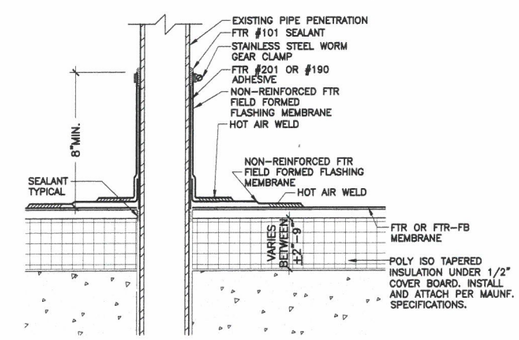

PENETRATION FLASHING

5 A-1 © EXISTING ROOF PENETRATIONS SCALE: 3"=1'-0"

DR. MARTIN LUTHER KING JR. MEMORIAL COMMUNITY CENTER - ROOF RENOVATION

304 CATHERINE STREET
KEY WEST, FLORIDA

WILLIAM P. HORN ARCHITECT, P.A.
915 EATON ST.
KEY WEST,
FLORIDA
33040
TEL (305) 296-8302
FAX (305) 296-1033
LICENSE NO.
AA 0003040

MLK ROOF
304 CATHERINE ST.
KEY WEST, FL

SEAL

8-23-16

THESE DRAWINGS MAY NOT BE REPRODUCED WITHOUT WRITTEN AUTHORIZATION BY WILLIAM P. HORN

DATE
06-29-2016 50% SET
07-29-2016 HARC
08-11-2016 100% SET
08-17-2016 BID SET

REVISIONS

DRAWN BY
JW

PROJECT NUMBER
1601

A-1

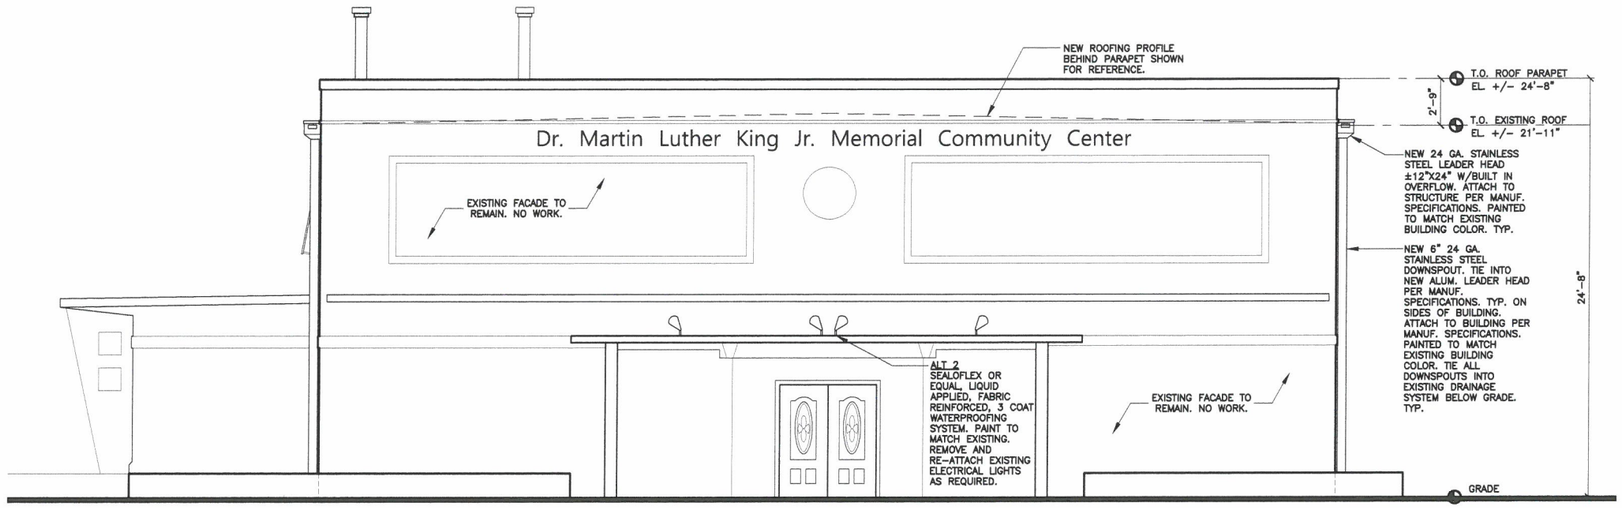

1 / A-2 PROPOSED FRONT ELEVATION

SCALE: 1/4"=1'-0"

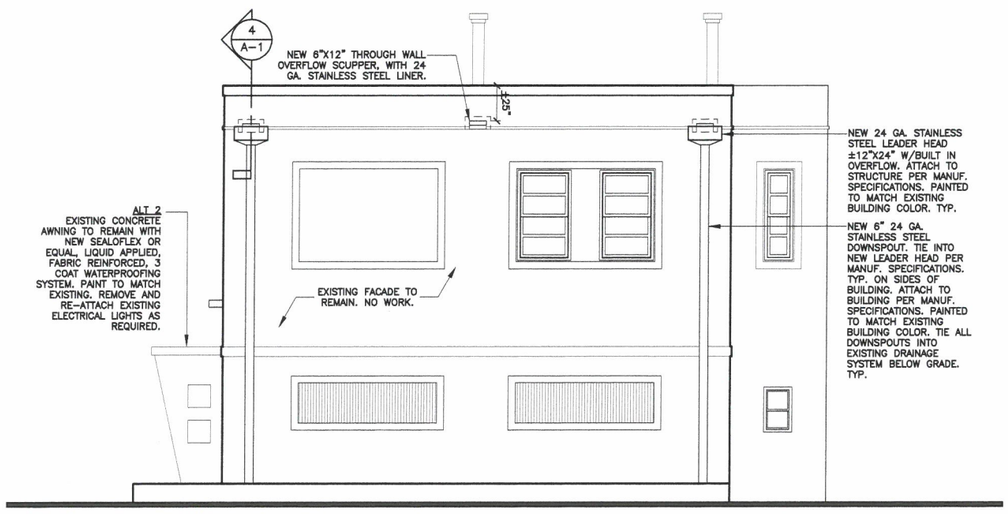

2 / A-2 PROPOSED WEST ELEVATION

SCALE: 1/4"=1'-0"

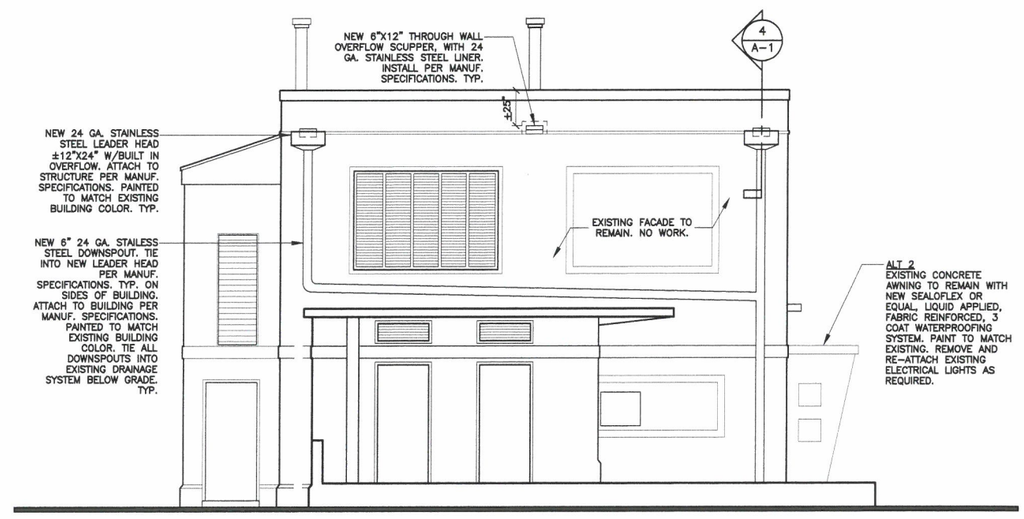

3 / A-2 PROPOSED EAST ELEVATION

SCALE: 1/4"=1'-0"

WILLIAM P. HORN
ARCHITECT, P.A.

915 EATON ST.
KEY WEST,
FLORIDA
33040

TEL (305) 296-6302
FAX (305) 296-1033

LICENSE NO.
AA 0003040

MLK ROOF
304 CATHERINE ST.
KEY WEST, FL

SEAL

8-23-16

THESE DRAWINGS MAY NOT BE REPRODUCED WITHOUT WRITTEN AUTHORIZATION BY WILLIAM P. HORN

DATE
06-29-2016 50% SET
07-29-2016 HARC
08-11-2016 100% SET
08-17-2016 BID SET

REVISIONS

DRAWN BY
JW

PROJECT NUMBER
1601

A-2

DR. MARTIN LUTHER KING JR. MEMORIAL COMMUNITY CENTER - ROOF RENOVATION

304 CATHERINE STREET
KEY WEST, FLORIDA

01800 - GENERAL REQUIREMENTS

Project Description The Contractor shall furnish all labor and materials required and necessary for re-roofing the building such that the result is a complete habitable, weatherproof, safe and secure finish building, suitable for human occupancy in accordance with Specifications, Drawing and Project Documents.

The General Conditions of the Contract, AIA Document A201, latest edition, are hereby made a part of these Construction Documents and shall apply to this Project.

The Florida Building Code 2014 Edition, as amended by Governing Local Ordinances and requirements of the State of Florida "Coastal Zone Protection Act", together with applicable requirements of governing public agencies and the following listed codes shall apply to this project.

Florida Existing Building Code, 2014 Edition
National Electric Code 2014 Edition.
Florida Plumbing Code, 2014 Edition
Florida Mechanical Code, 2014 Edition.
Florida Fuel Gas Code, 2014 Edition.

FEMA- Coordinate all building items required to be above flood elevation for project and other FEMA regulations that apply to the project.

Contractor shall visit the site to become familiar with existing conditions and requirements of construction prior to bidding.

Contractor shall complete new work in conformance with these drawings. Notify Architect if conflicts appear or are uncovered during the progress of the work prior to any field modifications or construction. Deviations from permitted drawings without Architects prior written approval shall be at the Contractors responsibility. Contractor is to verify all dimensions of project prior to proceeding with construction. Notify architect of any conflicts or problems so solutions can be achieved prior to construction. In event of conflict between drawings and specifications the most stringent requirements shall apply. Verification shall include, but is not limited to, coordination of site work, existing conditions, buildings and utilities.

Live Loads used in design:

Refer to Structural Specifications

General Notes:

A. The building will remain occupied and fully functional throughout the course of construction. Coordinate site access, staging areas and construction hours with owner. Provide temporary safety barriers and overhead walkway covers at building access points.

B. Engineer's approval must be secured for structural revisions, if any. Coordinate with Architect.

C. Contractor to verify all dimensions before proceeding with any work.

D. Provide temporary bracing and precautions necessary to withstand all construction and/or wind loads. Provide temporary refuse chute or other precautions necessary to protect the building from dirt or damage during construction.

E. Submit shop and erection drawings for all items required by the drawing or elsewhere in the specifications for written approval. The manufacture or fabrication of any items prior to written approval of shop drawings will be entirely at the risk of the contractor.All references to standards to be of the latest issue applicable.

F. This project is in a coastal salt water environment. Contractor shall consider this in selections of materials used in the exterior and non-air conditioned areas. All materials shall be salt resistant.

G. Manufactured assemblies; such as roofing, soffits, panels, coping assemblies, flashing assemblies and other external assemblies incorporated into the project shall require detailed shop drawing submittals. Miami Dade N.O.A'S providing tested assembly installation details and windload compliance are required. Manufacturers recommendations and requirements (including warranty requirements) shall be incorporated along with the latest industry standards and best practices.

H. Waterproofing, vapor barriers, waterstop, air seals,, etc. shall be as indicated in the Specifications and as per manufacturer and industry standards.

I. Contractor to provide all required fire blocking as required by Code.

J. Contractor to take all precautions to prevent mold from growing in or on the building. Do not use materials that have mold on them for construction, seal work in progress each night to keep water out.

K. All penetrations of fire rated construction shall be treated with dampers, seals or collars rated for the specific application and UL listed.

L. When working within occupied or partially occupied buildings it is the contractors responsibility to provide safe access and to maintain in operation all features of existing life safety systems including alarms, detectors, lighting and exit ways throughout the course of construction.

DIVISION 2 - SITE AND CIVIL WORK

02250 - Demolition shall include the removal of all items as indicated on the drawings, as well as incidental items necessary for new work to progress. All work shall be done in a workman like manner with minimal disturbance to existing to remain; All unwanted material to be removed from the site and properly disposed of. Unless noted otherwise, patch all areas to remain to match existing in areas damaged by demolition.

DIVISION 3 - CONCRETE REPAIRS (SEE STRUCTURAL) - Coordinate with Architect if hidden conditions are encountered in the course of the work.

DIVISION 4 - MASONRY (SEE STRUCTURAL)
DIVISION 5 - METALS (See flashing and sheet metal)
DIVISION 6 - WOOD AND PLASTICS

06100 - Rough Carpentry all framing lumber shall be dry southern pine, 19% MC, No. 2 or better, (Fb = 975 PSI Minimum). Member sizes noted on drawings are nominal. Provide 1"x4" cross bridging not over 8 feet o.c. for all wood joist and 2 x solid blocking between joist at all supports.

06130 Pressure Treated: All wood indicated shall be pressured-treated with chemicals to protect from decay and insects. Dry after treatment. All metal connectors to be by Simpson Strong-Tie Company or equal approved in writing by the engineer and to be stainless steel finish, unless otherwise noted. All connectors to be installed with all Manufacturers specified fasteners before loading. All fasteners used in pressure treated shall be stainless steel.

DIVISION 7 - THERMAL AND MOISTURE PROTECTION

07190 - Liquid applied water proof membrane (IF NOTED FOR USE ON THE DRAWINGS) - Provide Sealoflex waterbased, waterproofing system. Concrete or plywood decks. All surfaces clean and free of grease, dirt, oils or particles. Concrete shall be primed with Dampseal 101, Sealoment Plus or Sealbont Primer; per manufacturers recommendations for the project. Waterproofing System shall consist of a base coat with embed fabric while wet a saturation coat and when dry, 2 coats of Sealoflex Finish Coat (white).

At joints or cracks in substrate, lap 6" with base coat, fabric and saturation coat and allow to dry prior to applying the system to the entire area.

07210 - Insulation - Provide a tapered insulation installation as shown on drawings and as follows:

A. Polyisocyanurate board insulation: provide rigid, cellular thermal insulation with glass-fiber-reinforced polyisocyanurate closed-cell foam core. Complying with ASTM C1289 and complying with FS HH-1-1972/1, class 2; aged R- Values of 8 and 7.2 at 40 and 75 Deg. F. (4.4. and 23.9 Deg. C), respectively; and as follows:

1. Surface burning characteristics: maximum flame spread and smoke developed values of 25 and 50; respectively.
2. Thickness 1" for specification criteria (see drawings for required thickness at each location). Comply with manufacture's recommendations and specification for the current installation. Seal all joints as required.

B. All insulation shall be formalidehyde free.

07315 - Roofing Shop Drawings : All roofing assemblies require shop drawing submittals. The submittal shall include all components of the assembly including base sheets (if any), insulation if integral to the assembly such as tapered insulation to achieve roof slopes, cover board, membranes and attachment, including edge conditions. The submittal shall include N.O.A. test data for the entire assembly, as a unit, or for each component used, including anchorage/ attachment to its supporting substrate on down to the structural deck.

Documentation that the project specific roofing assembly meets design wind loading is required. This can be accomplished by submittal of N.O.A. test data or by signed and sealed certification by a Florida Registered Engineer. Provide manufacture's requirements and installation instructions for review.

07550 - Membrane Roofing - Provide membrane roofing utilizing a fully adhered 60 mil. single-ply system; Basis of Design as noted sheet A-1. Contractor to provide a complete roofing system, following all of the manufacturers specifications and details, and provide a roofing membrane manufacturer's 20 year warranty on the roofing system. All flashing material to be coordinated with other roofing systems and or existing conditions. Provide manufacturer's requirements, installation instructions and valid N.O.A. of system showing that the system meets the pressure requirements shown on S-1. Single ply assemblies by other manufacturers with similar characteristics and equal performance and warranty are acceptable. It is the contractors responsibility to document equality of products proposed.

Note: Assembly is installed over tapered insulation and shall provide a minimum of 1/4" slope per foot. 07620 - Flashing and sheet metal:

A. This section to include; metal flashing and base flashing, stops, built-in metal scuppers and miscellaneous sheet metal accessories.
B. Material shall be pre-finished 24 ga. min. stainless steel, commercial quality, except as noted otherwise. Coordinate finish with roofing assembly recommendations and requirements.
C. Shapes shall match existing or detailed profiles of flashing and stops.
D. Shop-fabricate work to the extent possible. Comply with details shown and applicable requirements of SMACNA "Architectural sheet metal manual" and material manufacturer recommendations.

07920 - Sealants

A. All sealants used in conjunction with roofing shall be compatible with and as recommended by the roofing assembly manufacturer.
B. Siliconized Acrylic Caulk - 25 years, paintable, non-staining, mildew resistant. For interior and exterior use, wood and masonry, as a filler for cracks voids and holes in preparation for paint or other finish. - See existing wood preparation.
C Polyseamseal all purpose adhesive caulk, paintable, non-staining, mildew resistant. For interior and exterior use as a filler and joint seal at tile, tub and counters.
D. Silicone Rubber Sealant - FSTT-S-001543, class A, one part non-sag low modules silicone rubber sealant. For interior and exterior use in working joints where some movement is anticipated, wood, masonry, metal and glass. Provide backer rod depth control in all joints in excess of 1/4"
E. All interior architectural caulks and sealants to have a VOC limit of 250 g/L.

DIVISION 8-15 NOT USED
DIVISION 16 - ELECTRICAL

1604 - LIGHTNING PROTECTION

1. Work shall be done in accordance with NFPA 780-standard for installation of lightning protection system.
2. Connect conduits using mechanical connections or exothermic welding process; protect adjacent construction elements and finishes from damage.
3. Ensure compatibility of all adhesives with roof and parapet wall assemblies.
4. At the end of the work perform a field inspection to insure all connections are made and that the system is complete providing protection to the entire structure and is properly grounded.

WILLIAM P. HORN
ARCHITECT , P.A.

915 EATON ST.
KEY WEST,
FLORIDA
33040

TEL (305) 296-8302
FAX (305) 296-1033

LICENSE NO.
AA 0003040

MLK ROOF
304 CATHERINE ST.
KEY WEST, FL.

SEAL

B-23-16

THESE DRAWINGS MAY NOT BE REPRODUCED WITHOUT WRITTEN AUTHORIZATION BY WILLIAM P. HORN

DATE
06-29-2016 50% SET
07-29-2016 HARC
08-11-2016 100% SET
08-17-2016 BID SET

REVISIONS

DRAWN BY
JW

PROJECT NUMBER
1601

A-3

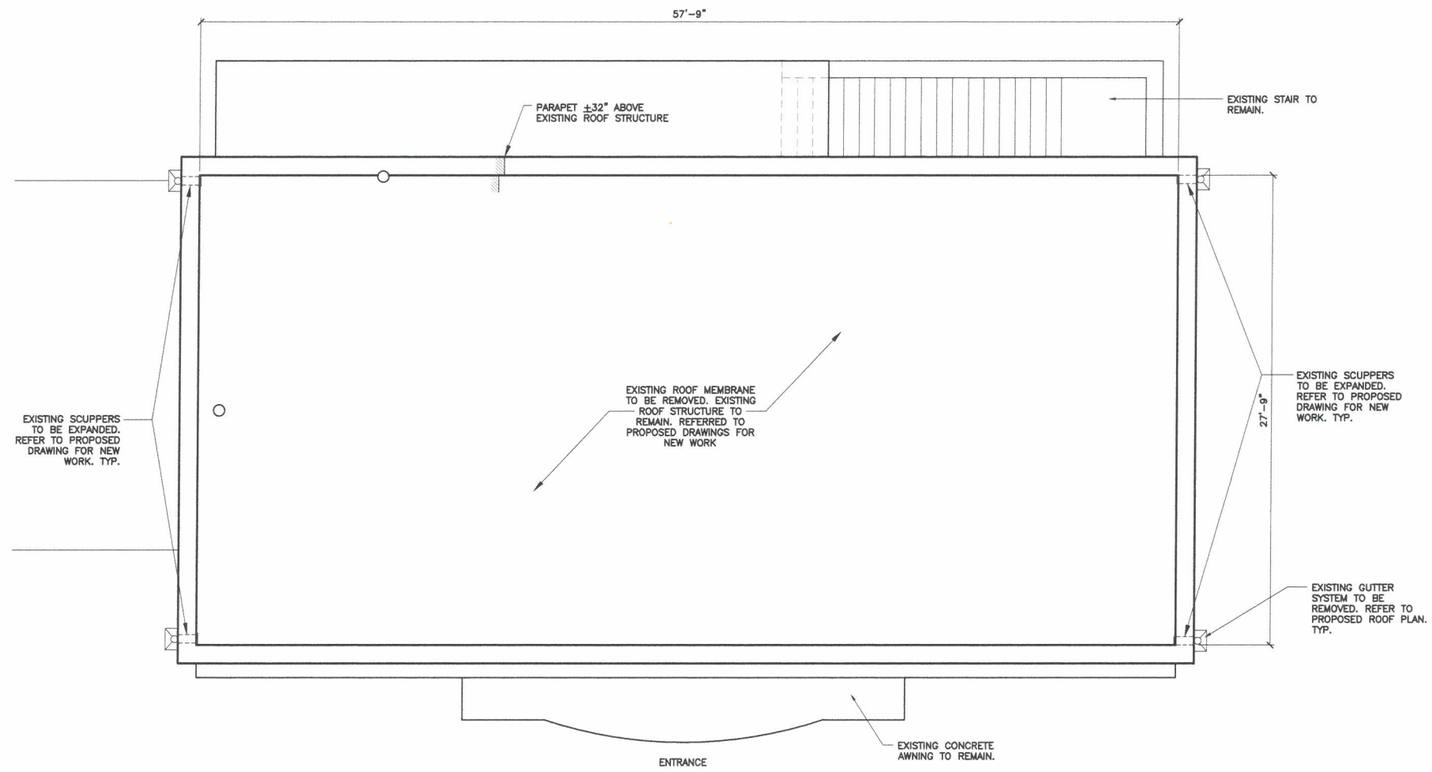



EXISTING ROOF PLAN

SCALE: 1/4"=1'-0"

WILLIAM P. HORN
ARCHITECT, P.A.

915 EATON ST.
KEY WEST,
FLORIDA
33040

TEL (305) 296-8302
FAX (305) 296-1033

LICENSE NO.
AA 0003040

MLK ROOF
304 CATHERINE STREET
KEY WEST, FL

SEAL

8-23-16

THESE DRAWINGS MAY NOT BE REPRODUCED WITHOUT WRITTEN AUTHORIZATION BY WILLIAM P. HORN

DATE
06-29-2016 50% SET
07-29-2016 HARC
08-11-2016 100% SET
08-17-2016 BID SET

REVISIONS

DRAWN BY
JW

PROJECT NUMBER
1601

Ex-1

MLK ROOF
304 CATHERINE STREET
KEY WEST, FLORIDA

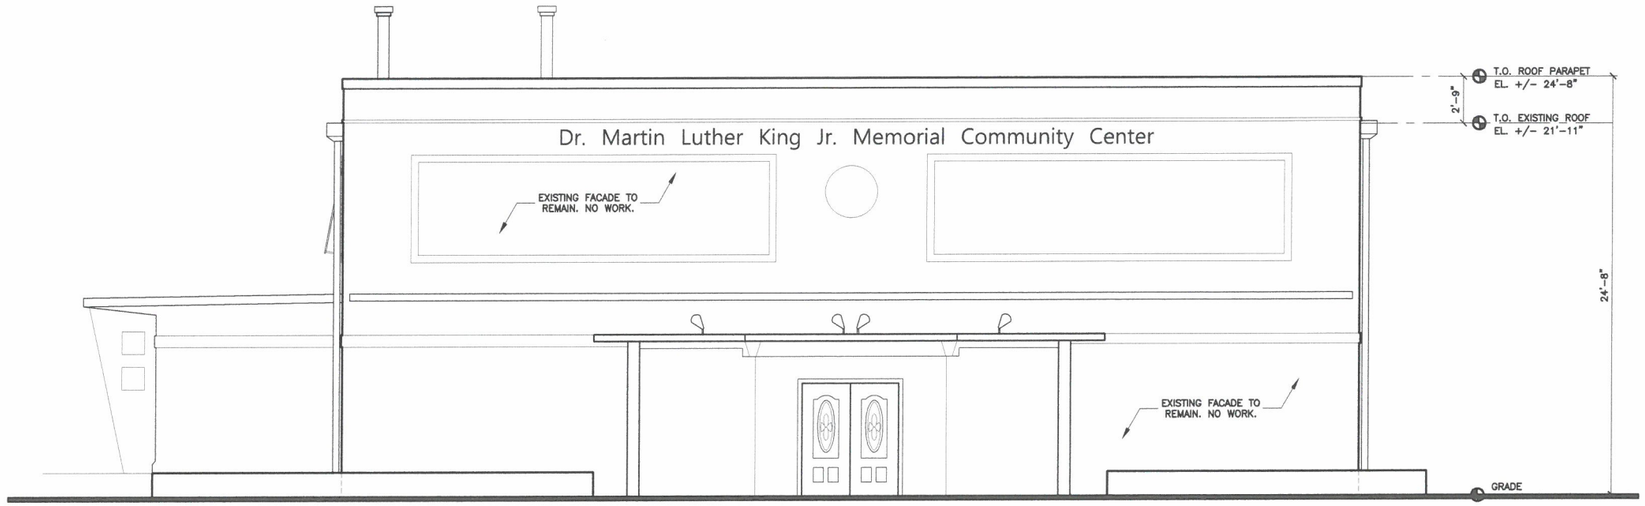

1 Ex-2 EXISTING FRONT ELEVATION

SCALE: 1/4"=1'-0"

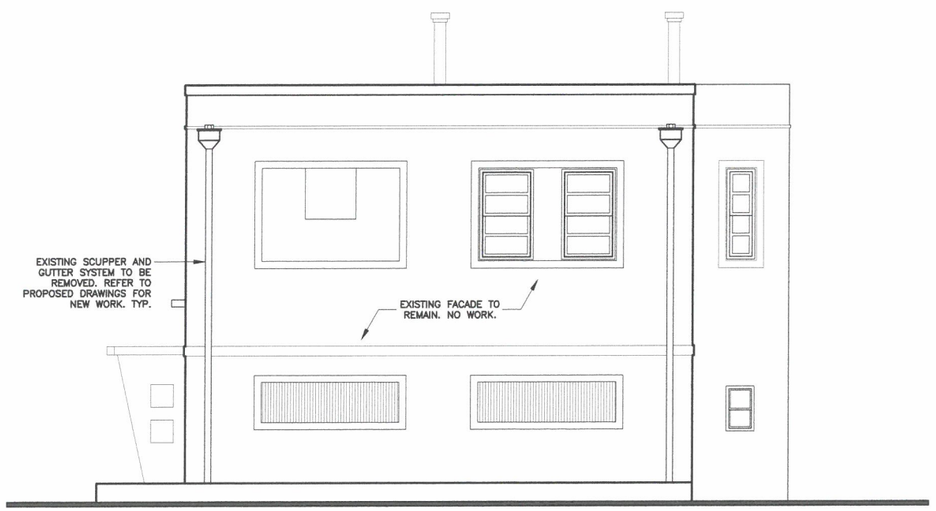

2 Ex-2 EXISTING WEST ELEVATION

SCALE: 1/4"=1'-0"

3 Ex-2 EXISTING EAST ELEVATION

SCALE: 1/4"=1'-0"

WILLIAM P. HORN
ARCHITECT, P.A.

915 EATON ST.
KEY WEST,
FLORIDA
33040

TEL (305) 296-8302
FAX (305) 296-1033

LICENSE NO
AA 0003040

MLK ROOF
304 CATHERINE STREET
KEY WEST, FL

SEAL

8-23-16

THESE DRAWINGS MAY NOT BE REPRODUCED WITHOUT WRITTEN AUTHORIZATION BY WILLIAM P. HORN

DATE
06-29-2016 50% SET
07-29-2016 HARC
08-11-2016 100% SET
08-17-2016 BID SET

REVISIONS

DRAWN BY
JW

PROJECT NUMBER
1601

Ex-2

MLK ROOF

304 CATHERINE STREET
KEY WEST, FLORIDA

General Requirements:

1. Prior starting any work the Contractor shall review these plans and site conditions and notify the Engineer if any discrepancies are discovered.
2. The Engineer is not responsible for the supervision of the Contractor nor his employees during the construction. It is Contractor's responsibility to provide means and establish methods of the construction to meet requirements of all applicable codes, industry standards and requirements of these plans.
3. Quality of the work shall meet or exceed industry standard practices.
4. Any deviations from these plans shall be reviewed and approved by the Engineer.

Design Data:

1. Applicable Building Code: FBC Existing Building 5th Edition (2014)
2. Applicable Design Loads: per ASCI/SEI 7–10
   Floor Live Load: N/A
   Roof Live Load: 20 psf (300 lb conc.)
   Basic Wind Speed: 180 MPH
   Exposure: D
   Structural Category: II

All pressures shown are based on ASD Design,
with a Load Factor of 0.6

Concrete

1. Applicable Code ACI 318 latest edition and ACI 301.
2. All concrete elements shall have a min. compressive strength of 4000 psi unless otherwise is shown on the plans. Water Cement ratio shall not exceed W/C=0.40.
3. All cast–in–place concrete shall be cured and protected from overdrying per ACI 305R–10 "Hot Weather Concreting".
4. All exposed edges shall have 1/2" chamfers.
5. No cold joints are allowed unless otherwise approved by the Engineer.
6. TESTING: All Field and Laboratory Testing shall be performed by the independent specialized company.
The contractor is responsible for all scheduling, coordination and cost of testing company.
Three (3) samples shall be taken and tested each time.
Minimum Sampling Frequency:
a) Each day of concreting for every concrete mix;
b) Every 50 cubic yards;
c) Every 2000 sq.ft. of slab area.

All testing shall be per latest ACI and ASTM requirements.
Laboratory shall supply three (3) original signed&sealed report results to the Engineer.

7. Cast–in–place and precast members erection tolerances shall be as specified in the table 8.2.2 or in section 8.3 of "PCI design handbook/sixth edition".

Reinforcement

1. All rebar shall be deformed carbon–steel ASTM A615/A615M–13 Grade 60 unless otherwise specified on the plans.
* ADD ALTERNATE REINFORCEMENT OPTION: ASTM A1035 Grade 100 (MMFX2) as corrosion resistant alternative for all reinforcement.
2. All requirements for placement, cover, tolerances, etc. Shall be per ACI 318–11.
3. All hooks and bends shall be factory made unless field bends are approved by the Engineer.
4. Only PLASTIC CHAIRS and CENTRALIZERS shall be used for rebar support.

Concrete repairs:

1. Remove all loose and unsound concrete.
2. Expose all corroded rebar from all sides (1.5" around).
3. Clean all exposed rebar by mechanical means to near–white condition.
4. Pressure wash all concrete and reinforcement with potable water.
5. Prime existing reinforcement w/ "sika armatec 110 epocem" or approved equal. follow manufacturer instructions for surface preparation, application and curing.
6. All rebar with loss of section over 10% shall be duplicated with new rebar of equal size.
7. Minimum concrete cover shall be 2.0" unless otherwise is approved by the engineer.
8. Install sacrificial anodes "sika galvashield xp" (or approved equal) as shown on the diagrams.

9. For small patch repairs (depth up to 4", area up to 10 ft2) use "sikarepair 22" repair mortar. strictly follow manufacturer instructions for surface preparation, application and curing.

9A. For large repairs (full depth slab, beam or column repair/replacement) use 4000 psi concrete mix with w/c ratio 0.4 max. with high range plastesizer and rust inhibiting admixtures.

! Moist curing for minimum of 4 days is required. follow hot weather concreting guidelines.

11. The contractor is responsible for any shoring/reshoring and temporary supports of all structural elements during the repair and through the concrete curing period.

Structural Lumber

1. All wood members shall meet or exceed requirements specified in "ANSI/AF&PA National Design Specification (NDS) for Wood Construction" and all referenced standards.
2. All wood members shall be Souther Pine No2 or Greater kiln dried as specified in the Standards, unless otherwise specified.
3. All wood members exposed to exterior, in direct contact with concrete or steel shall be Pressure–Treated (PT) UC3B grade per AWPA Standards.
4. All field cuts in pt lumber shall treated on site.
5. Nailing shall be in accordance with FBC 2014. Nails and other fasteners for PT wood shall be Stainless Steel or ACQ Approved treated.
6. Sheathing shall be 19/32" CDX Plywood Sheathing Grade, unless otherwise is specified on the plans. Use 10d ring–shank nails with spacing of 4" o.c. on all edges and 6" o.c. in the field.

Hardware

1. Hardware shall be 316 Stainless Steel or better or HDG galvanized for non exposed Simpson products, unless otherwise specified.
2. All connectors shall have stainless steel screws and fasteners or ACQ Approved treated (for not exposed locations).

Reinforced Masonry (CMU)

1. All Masonry shall be reinforced concrete masonry unit in accordance with the latest eddition of ACI 530/ASCE 5/TMS 402.
2. Install all blocks in running bond.
3. Minimum masonry block (ASTM C90) strength shall (F'm) be 2000 psi.
4. Type "S" mortar (ASTM C270) shall be used using 3/8" full bedding reinforced w/ 9 gage galvanized ladder wire every 2nd row.
5. Filled cells shall be reinforced with #5 rebar @ 24" o.c. (unless otherwise is specified on the plans).
6. Grout shall be pea rock pump mix (ASTM C476) with a minimum compressive strength of 4000 psi (28 day) (ASTM C1019). Targeted slump shall be 8"–11".
7. Each grouted cell shall have cleanout openings at the bottom. There shall be no loose mortar or other debris in the bottom of the cell. Use blast pressure washing for surface preparation.

STRUCTURAL STEEL

1. Structural steel components shall be as described in "Specifications for Structural Steel Buildings" AISC 2005 or later eddition.
2. HSS shapes (structural tubing) shall be ASTM A500 (Fy=46 ksi).
3. Steel plates, flanges and miscelenious elements shall be ASTM A36 (Fy=36 ksi) unless noted otherwise on the plans.
4. W–shapes, C–shapes and other formed steel shall be ASTM A992 (Fy=50 ksi).
5. All welding shall be in conformance with the latest specifications AWS D1.1/D1.1M:2010, Structural Welding Code – Steel.
6. Bolts: Hot Dip Galvanized. A325N, A563DH hex nuts, F436 washers.
7. Anchor bolts: Hot Dip Galvanized. A307 grade A, A563DH hex nuts, F844 washers.

STRUCTURAL STEEL COATING:

1. All surfaces shall be abrasive blast cleaned to near–white metal (per SSPC–SP10)

Exposed Steel:

2. All elements shall be galvanized after manufacturing (all cutting, drilling and welding). Galvanization shall be in accordance with ASTM A123 with coating grade of 75 or better.

ALUMINUM COMPONENTS

1. Type 6061–T6 aluminum.
2. MIG welded all joints w/ continuous 1/8" weld. Use 5356 filler wire alloy.
3. All aluminum in contact with concrete, pt wood, dissimilar metals and other corrosive materials shall coated with coal–tar epoxy or protected by other Engineer approved method.

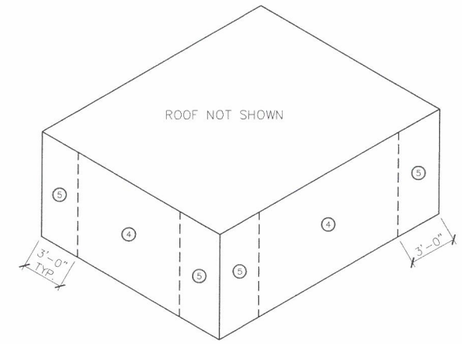

WALLS WIND PRESSURES DIAGRAM

SCALE: NTS

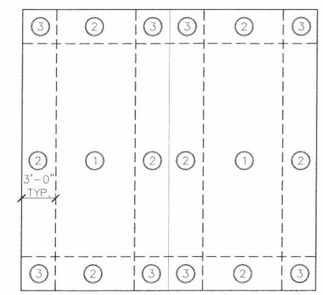

ROOF WIND
PRESSURES DIAGRAM

SCALE: NTS

Enclosed – Building					
Wind Pressure on Components and Cladding (Ch 30 Part 1)					
Description	Width, ft	Span, ft	Area, ft2	Max P, PSF	Min P, PSF
Zone 1	1	1	1	+22.4	–55.0
Zone 2	1	1	1	+22.4	–92.2
Zone 3	1	1	1	+22.4	–138.8
Zone 4	1	1	1	N/A	N/A
Zone 5	1	1	1	N/A	N/A
Solar Heater	4.0	10.5	42	+19.5	–52.1

All pressures shown are based on ASD Design,
with a Load Factor of 0.6

WILLIAM P. HORN
ARCHITECT, P.A.

915 EATON ST.
KEY WEST
FLORIDA
33040

TEL (305) 296-8302
FAX (305) 296-1033

LICENSE NO.
AA 0003040

Artibus Design
3706 N. Roosevelt Blvd
Suite I-208
Key West, FL 33040
(305) 204-2512
www.ArtibusDesign.com
CA # 26835

MLK ROOF
304 CATHERINE ST.
KEY WEST, FL

THIS DRAWING IS NOT VALID WITHOUT THE SIGNATURE AND ORIGINAL SEAL

SIGNATURE

DATE

SERGIO MASHTAKOV
PROFESSIONAL ENGINEER
STATE OF FLORIDA
LICENSE NO 71489

STATE OF FLORIDA

AUG 22 2016

THESE DRAWINGS MAY NOT BE REPRODUCED WITHOUT WRITTEN AUTHORIZATION BY WILLIAM P. HORN

DATE
06-29-2016 50% SET
07-29-2016 HARC
08-11-2016 100% SET
08-17-2016 BID SET

REVISIONS

DRAWN BY
SAM

PROJECT NUMBER
1601

S-1

DR. MARTIN LUTHER KING JR. MEMORIAL COMMUNITY CENTER - ROOF RENOVATION

304 CATHERINE STREET
KEY WEST, FLORIDA

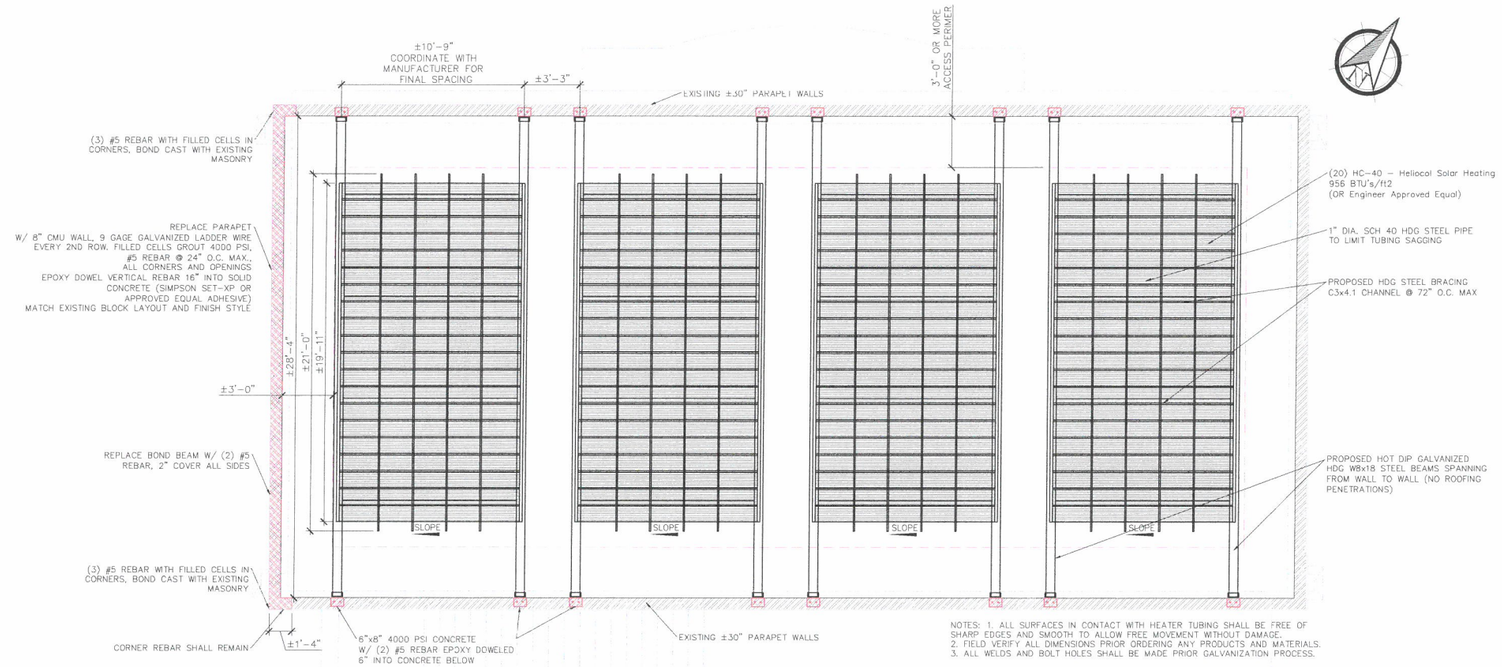

NOTES: 1. ALL SURFACES IN CONTACT WITH HEATER TUBING SHALL BE FREE OF SHARP EDGES AND SMOOTH TO ALLOW FREE MOVEMENT WITHOUT DAMAGE.
2. FIELD VERIFY ALL DIMENSIONS PRIOR ORDERING ANY PRODUCTS AND MATERIALS.
3. ALL WELDS AND BOLT HOLES SHALL BE MADE PRIOR GALVANIZATION PROCESS.

ROOF PLAN VIEW SOLAR WATER HEATER LAYOUT

SCALE: 1/4" = 1'-0"



TYPICAL BRACING CONNECTION DETAIL

SCALE: NTS

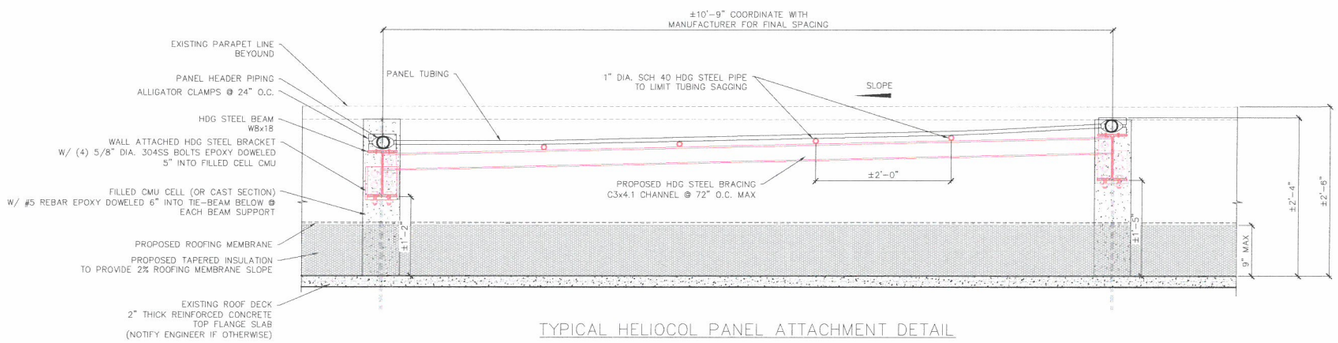

TYPICAL HELIOCOL PANEL ATTACHMENT DETAIL

SCALE: 1" = 1'-0"



TYPICAL SUPPORT PIPE TO BRACE CONNECTION

SCALE: NTS

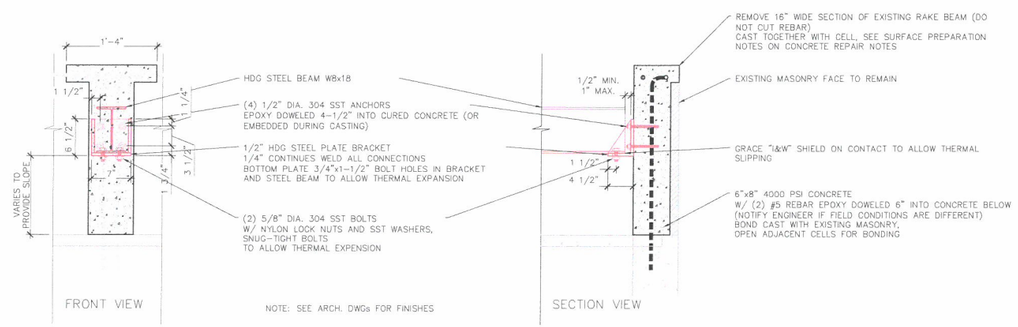

TYPICAL STEEL BEAM SUPPORT DETAIL

SCALE: 1" = 1'-0"

WILLIAM P. HORN
ARCHITECT, P.A.

915 EATON ST.
KEY WEST
FLORIDA
33040

TEL (305) 296-8302
FAX (305) 296-1033

LICENSE NO
AA 0003040

Artibus Design
3706 N. Roosevelt Blvd
Suite F-208
Key West, FL 33040
(305) 304-3013
www.ArtibusDesign.com
CA # 26535

MLK ROOF
304 CATHERINE ST.
KEY WEST, FL

THIS DRAWING IS NOT VALID WITHOUT THE RAISED EMBOSSED SEAL

SIGNATURE

DATE

SERGIO SESTO, P.E.
PROFESSIONAL ENGINEER
STATE OF FLORIDA
LICENSE NO 71460

STATE OF FLORIDA
SERGIO SESTO
71460
PROFESSIONAL ENGINEER

AUG 22 2016

THESE DRAWINGS MAY NOT BE REPRODUCED WITHOUT WRITTEN AUTHORIZATION BY WILLIAM P. HORN

DATE
06-29-2016 50% SET
07-29-2016 HARC
08-11-2016 100% SET
08-17-2016 BID SET

REVISIONS

DRAWN BY
SAM

PROJECT NUMBER
1601

S-2

DR. MARTIN LUTHER KING JR. MEMORIAL COMMUNITY CENTER - ROOF RENOVATION

304 CATHERINE STREET
KEY WEST, FLORIDA

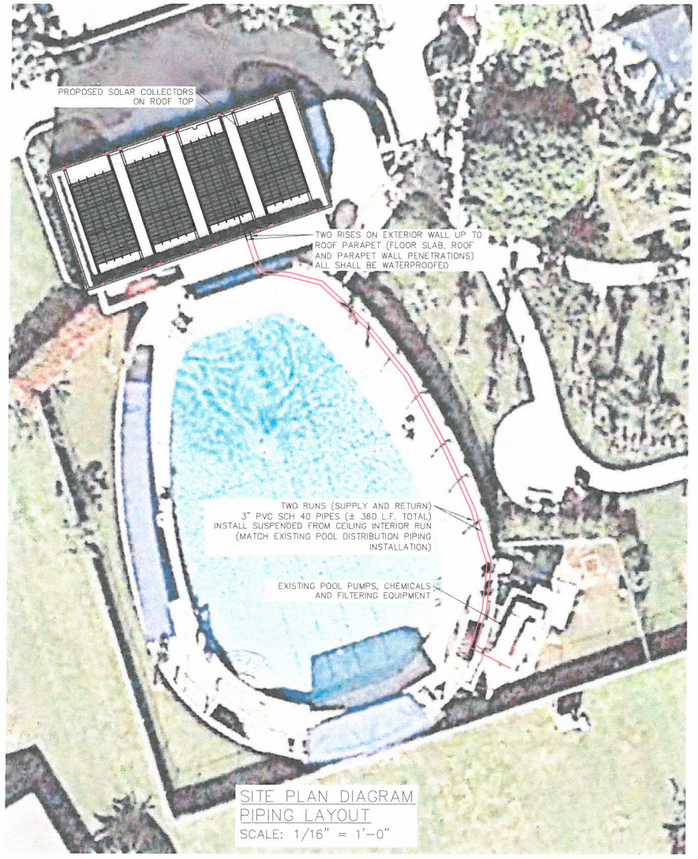

SITE PLAN DIAGRAM
PIPING LAYOUT
SCALE: 1/16" = 1'-0"

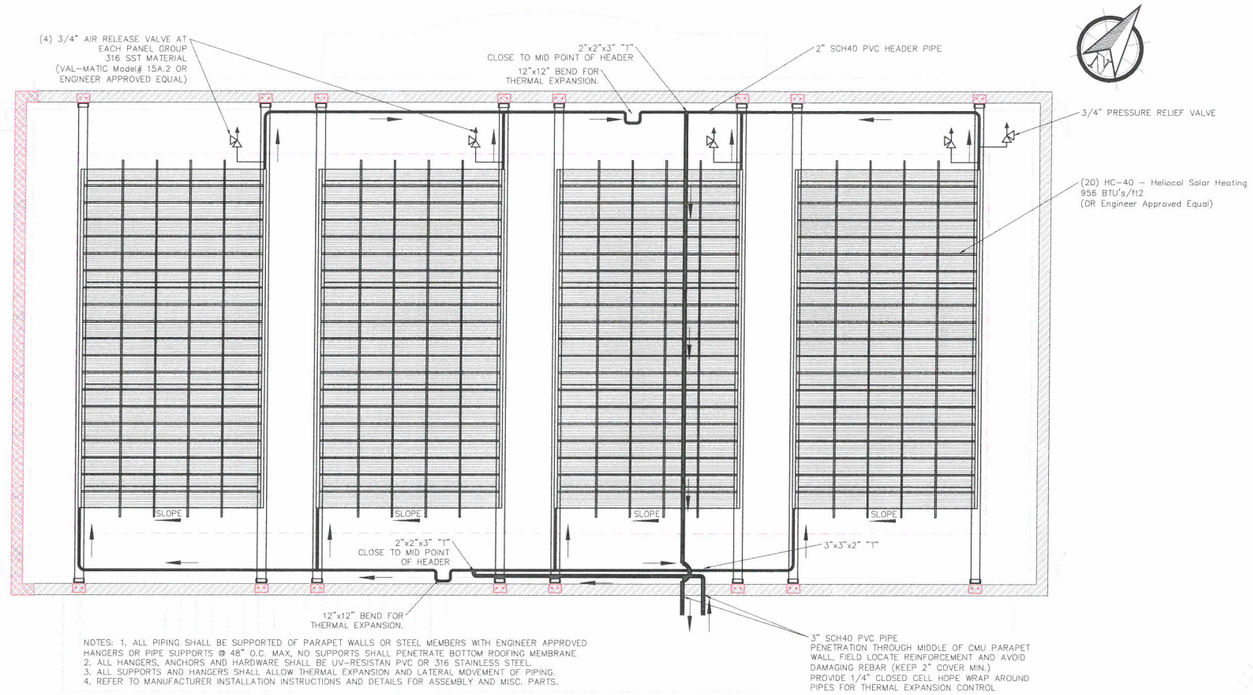

NOTES: 1. ALL PIPING SHALL BE SUPPORTED OF PARAPET WALLS OR STEEL MEMBERS WITH ENGINEER APPROVED HANGERS OR PIPE SUPPORTS @ 48" O.C. MAX, NO SUPPORTS SHALL PENETRATE BOTTOM ROOFING MEMBRANE.
2. ALL HANGERS, ANCHORS AND HARDWARE SHALL BE UV-RESISTAN PVC OR 316 STAINLESS STEEL.
3. ALL SUPPORTS AND HANGERS SHALL ALLOW THERMAL EXPANSION AND LATERAL MOVEMENT OF PIPING.
4. REFER TO MANUFACTURER INSTALLATION INSTRUCTIONS AND DETAILS FOR ASSEMBLY AND MISC. PARTS.

ROOF PLAN VIEW – PIPING LAYOUT
SCALE: 1/4" = 1'-0"

SOLAR PIPING NOTES:
1. ALL WORK AND MATERIALS SHALL BE IN COMPLIANCE WITH FBC 5TH EDITION (2014) PLUMBING AND LOCAL STANDARDS.
2. ALL PIPING SHALL BE SCH 40 PVC.
3. CONTRACTORS SCOPE OF WORK INCLUDES ALL MATERIALS, VALVES, FITTINGS, VENTS ETC. REQUIRED FOR A COMPLETE AND OPERATIONAL SYSTEM. SYSTEM STARTUP, TESTING AND BALANCING SHALL BE INCLUDED IN THE SCOPE.
4. ALL FIXTURES SHALL BE APPROVED BY OWNER PRIOR PURCHASING AND INSTALLATION.
5. WATER HEATER SHALL BE INSTALLED WITH ALL NECESSARY VACUUM BREAKERS AND PRESSURE RELIEVE VALVES AS RECOMMENDED BY THE MANUFACTURER.
6. INSTALLATION DETAILS AND HARDWARE SHALL BE COORDINATED WITH THE FINAL APPROVED SHOP DRAWINGS OF THE COLLECTOR PANEL.
7. INSTALLATION OF THE SYSTEM SHALL BE BY THE QUALIFIED LICENSED SOLAR CONTRACTOR EXPERIENCED IN INSTALLATION OF SIMILAR SYSTEMS.
8. INSTALLED SYSTEM SHALL BE TESTED TO 50 PSI FOR 2 HOURS AFTER 15 MIN. STABILIZATION WITH NO ALLOWABLE LOSS OF PRESSURE AND LEAKS.

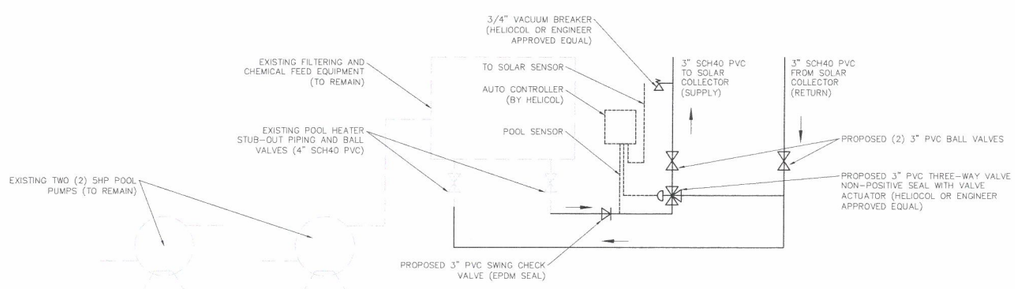

NOTE: ALL PIPING IS SHOWN DIAGRAMMATICALLY. THE CONTRACTOR IS RESPONSIBLE FOR ON SITE VERIFICATION OF ALL EXISTING CONDITIONS BEFORE BID.

PIPING RISER DIAGRAM
SCALE: NTS



NOTES: 1. HANGER SPACING SHALL NOT EXCEED 6FT AND SHALL BE INSTALLED ON ALL CHANGES OF DIRECTIONS.

TYPICAL PIPE HANGER DETAIL
SCALE: NTS

WILLIAM P. HORN
ARCHITECT, P.A.

915 EATON ST.
KEY WEST,
FLORIDA
33040

TEL (305) 296-8302
FAX (305) 296-1033

LICENSE NO.
AA 0003040

Artibus Design
3706 N. Roosevelt Blvd
Suite F-288
Key West, FL 33040
(305) 304-3512
www.ArtibusDesign.com
CA # 30835

MLK ROOF
304 CATHERINE ST.
KEY WEST, FL

THIS DRAWING IS NOT VALID WITHOUT THE SIGNATURE AND ORIGINAL SEAL

SIGNATURE
DATE
SERGE MOSHTAKOFF
PROFESSIONAL ENGINEER
STATE OF FLORIDA
LICENSE NO 71180

AUG 2 2 2016

THESE DRAWINGS MAY NOT BE REPRODUCED WITHOUT WRITTEN AUTHORIZATION BY WILLIAM P. HORN

DATE
06-29-2016 50% SET
07-29-2016 HARC
08-11-2016 100% SET
08-17-2016 BID SET

REVISIONS

DRAWN BY
SAM

PROJECT NUMBER
1601

P-1

DR. MARTIN LUTHER KING JR. MEMORIAL COMMUNITY CENTER - ROOF RENOVATION

304 CATHERINE STREET
KEY WEST, FLORIDA
